































































| ID | % Comp |  | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|----|--------|---|---|---|------------------|--------------------|--------------------|--------------|
| 1 | 65% | |  | Mesquite-Brazito Wastewater System Imp - Project 2 | 303 days? | Wed 3/16/22 | Thu 9/14/23 | |
| 2 | 10... |  |  | NOA | 0 days | Wed 3/16/22 | Wed 3/16/22 | |
| 3 | 10... |  |  | NTP (tentative) | 0 days | Mon 5/2/22 | Mon 5/2/22 | 2FS+47 edays |
| 4 | 95% | |  | Approvals | 42 days? | Wed 3/16/22 | Mon 5/30/22 | |
| 5 | 10... |  |  | SWPPP (DAC Approval) | 45 edays | Wed 3/16/22 | Sat 4/30/22 | 2 |
| 6 | 75% | |  | TCP (DAC Approval) | 45 edays | Wed 3/16/22 | Sat 4/30/22 | 2 |
| 7 | 10... |  |  | Roadway Survey (DAC Approval) | 45 edays | Wed 3/16/22 | Sat 4/30/22 | 2 |
| 8 | 10... |  |  | Building and Site Permits (CID Approval) | 30 edays | Sat 4/30/22 | Mon 5/30/22 | 5 |
| 9 | 10... |  |  | Dewatering Permits (NM OSE /EBID Approval) | 1 day? | Wed 3/16/22 | Wed 3/16/22 | |
| 10 | 10... |  |  | Pipe | 22 edays | Wed 3/16/22 | Thu 4/7/22 | 2 |
| 11 | 10... |  |  | Pumps | 22 edays | Wed 3/16/22 | Thu 4/7/22 | 2 |
| 12 | 10... |  |  | Manholes | 30 edays | Wed 3/16/22 | Fri 4/15/22 | 2 |
| 13 | 98% | |  | Deliveries | 67 days | Thu 4/7/22 | Fri 8/5/22 | |
| 14 | 10... |  |  | Pipe | 25 edays | Thu 4/7/22 | Mon 5/2/22 | 10 |
| 15 | 75% | |  | Manholes | 14 edays | Fri 4/15/22 | Fri 4/29/22 | 12 |
| 16 | 10... |  |  | Pumps | 120 edays | Thu 4/7/22 | Fri 8/5/22 | 11 |
| 17 | 25% | |  | Base Bid - Lift Station 16 | 281 days | Mon 4/25/22 | Thu 9/14/23 | |
| 18 | 10... |  |  | Mobilization | 12 days | Mon 4/25/22 | Mon 5/16/22 | |
| 19 | 10... |  |  | Yard & Temporary Facilities | 12 days | Mon 4/25/22 | Mon 5/16/22 | 27SF |
| 20 | 10... |  |  | Project Sign | 1 day | Wed 4/27/22 | Thu 4/28/22 | 21SF |
| 21 | 10... |  |  | Construction Staking | 8 days | Thu 4/28/22 | Thu 5/12/22 | 22SF |
| 22 | 10... |  |  | Proctor Native Material | 1 day | Thu 5/12/22 | Mon 5/16/22 | 24SF |
| 23 | 10... |  |  | Pre-Construction Video | 1 day | Thu 5/12/22 | Mon 5/16/22 | 27SF |

Project: msproj11
Date: Thu 1/12/23

| | | | | | |
|--------------------|---|-----------------------|---|-----------------|---|
| Task |  | Inactive Task |  | Start-only |  |
| Split |  | Inactive Milestone |  | Finish-only |  |
| Milestone |  | Inactive Summary |  | Deadline |  |
| Summary |  | Manual Task |  | Critical |  |
| Project Summary |  | Duration-only |  | Critical Split |  |
| External Tasks |  | Manual Summary Rollup |  | Progress |  |
| External Milestone |  | Manual Summary |  | Manual Progress |  |

| ID | % Comp | | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|----|--------------|--|-----------|--|-----------------|--------------------|---------------------|--------------|
| 24 | 10... | | | SW3P BMP's In-Place | 0 days | Mon 5/16/22 | Mon 5/16/22 | 27SF |
| 25 | 10... | | | Traffic Control In-Place | 0 days | Mon 5/16/22 | Mon 5/16/22 | 27SF |
| 26 | 29% | | | Lift Station 16 | 105 days | Mon 5/16/22 | Thu 11/17/22 | |
| 27 | 10... | | | Install Precast Wet Well | 4 days | Mon 5/16/22 | Thu 5/19/22 | 15 |
| 28 | 10... | | | Valve Vault | 8 days | Mon 5/23/22 | Mon 6/6/22 | 27 |
| 29 | 10... | | | Piping | 12 days | Tue 6/7/22 | Mon 6/27/22 | 28 |
| 30 | 0% | | | Pumps | 4 days | Mon 11/7/22 | Mon 11/14/22 | 29SF+160 eda |
| 31 | 0% | | | IBOX Odor Control Unit | 4 days | Mon 11/14/22 | Thu 11/17/22 | 30 |
| 32 | 10... | | | Building Underground | 8 days | Tue 6/28/22 | Tue 7/12/22 | 31 |
| 33 | 10... | | | Building Foundation | 8 days | Wed 7/13/22 | Tue 7/26/22 | 32 |
| 34 | 10% | | | CMU Walls | 8 days | Wed 7/27/22 | Tue 8/9/22 | 33 |
| 35 | 0% | | | Roof System | 4 days | Wed 8/10/22 | Tue 8/16/22 | 34 |
| 36 | 0% | | | Doors | 4 days | Wed 8/17/22 | Tue 8/23/22 | 35 |
| 37 | 0% | | | HVAC | 4 days | Wed 8/24/22 | Tue 8/30/22 | 36 |
| 38 | 0% | | | Mag/Hydroxide Odor Control System | 4 days | Wed 8/31/22 | Wed 9/7/22 | 37 |
| 39 | 0% | | | Electrical Service (EPEC) | 0 days | Thu 9/8/22 | Thu 9/8/22 | 40SF |
| 40 | 0% | | | Electrical | 24 days | Thu 9/8/22 | Wed 10/19/22 | 38 |
| 41 | 0% | | | Painting | 4 days | Thu 10/20/22 | Wed 10/26/22 | 40 |
| 42 | 0% | | | Water service | 4 days | Wed 8/17/22 | Tue 8/23/22 | 35 |
| 43 | 0% | | | Site Fencing | 32 days | Wed 8/24/22 | Wed 10/19/22 | 42 |
| 44 | 0% | | | Site Gravel | 4 days | Thu 10/20/22 | Wed 10/26/22 | 43 |
| 45 | 49% | | | Collection System | 138 days | Mon 5/23/22 | Mon 2/6/23 | |
| 46 | 10... | | | East Organ Alignment LS 16 - Sta 48+00 (1,000') | 16 days | Mon 5/23/22 | Mon 6/20/22 | |
| 47 | 10... | | | Mill Existing Asphalt | 2 days | Mon 5/23/22 | Tue 5/24/22 | 27 |

Project: msproj11
Date: Thu 1/12/23

| | | | | | |
|--------------------|--|-----------------------|--|-----------------|--|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Critical | |
| Project Summary | | Duration-only | | Critical Split | |
| External Tasks | | Manual Summary Rollup | | Progress | |
| External Milestone | | Manual Summary | | Manual Progress | |

| ID | % Comp | | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|----|--------|--|-----------|---|------------------|---------------------|---------------------|--------------|
| 48 | 10... | | | Install 10" SAS and Manholes | 10 days | Wed 5/25/22 | Mon 6/13/22 | 47 |
| 49 | 10... | | | 20" Bore Mesquite Drain Sta 48+62-49+97 | 4 days | Tue 6/14/22 | Mon 6/20/22 | 48 |
| 50 | 10... | | | BBQ/Picnic CT Alignment LS 16 - MH 049 (1405') | 8 days | Tue 6/14/22 | Mon 6/27/22 | |
| 51 | 10... | | | Mill Existing Asphalt | 2 days | Tue 6/14/22 | Wed 6/15/22 | 48 |
| 52 | 10... | | | Install 8" SAS and Manholes | 8 days | Tue 6/14/22 | Mon 6/27/22 | 48 |
| 53 | 65% | | | East Organ Alignment Sta 48+00 - 64+00 (1,600') | 59 days | Mon 6/27/22 | Mon 10/10/22 | |
| 54 | 10... | | | Mill Existing Asphalt | 2 days | Mon 6/27/22 | Tue 6/28/22 | 51 |
| 55 | 10... | | | Install 10" SAS and Manholes | 16 days | Mon 7/25/22 | Thu 8/18/22 | |
| 56 | 0% | | | Replace Asphalt Road | 12 days | Mon 8/22/22 | Mon 9/12/22 | 55 |
| 57 | 10... | | | 20" Bore Apache Lateral Sta 64+10-64+80 | 4 days | Tue 10/4/22 | Mon 10/10/22 | 55 |
| 58 | 10... | | | Valles/Relic Alignment LS 16 - MH 046 (1692') | 27 days | Mon 8/22/22 | Thu 10/6/22 | |
| 59 | 10... | | | Mill Existing Asphalt | 2 days | Mon 8/22/22 | Tue 8/23/22 | 55 |
| 60 | 10... | | | Install 8" SAS and Manholes | 8 days | Mon 9/26/22 | Thu 10/6/22 | 55 |
| 61 | 10... | | | Replace Asphalt Road | 4 days | Tue 9/13/22 | Mon 9/19/22 | 56 |
| 62 | 10... | | | Primos CT/Relic CT Alignment LS 16 - MH 048 (1,296') | 10 days | Mon 10/10/22 | Tue 10/25/22 | |
| 63 | 10... | | | Install 8" SAS and Manholes | 6 days | Mon 10/10/22 | Tue 10/18/22 | 60 |
| 64 | 10... | | | Replace Gravel Road | 4 days | Wed 10/19/22 | Tue 10/25/22 | 63 |
| 65 | 10... | | | El Milagro rd. Alignment LS 16 - MH 040 (1242') | 12 days | Mon 8/22/22 | Mon 9/12/22 | |
| 66 | 10... | | | Install 8" SAS and Manholes | 8 days | Mon 8/22/22 | Thu 9/1/22 | 55 |
| 67 | 10... | | | Replace Gravel Road | 4 days | Tue 9/6/22 | Mon 9/12/22 | 66 |
| 68 | 10... | | | East Organ Alignment Sta 39+67 - 13+00 (2,700') | 40.2 days | Tue 9/6/22 | Tue 11/15/22 | |
| 69 | 10... | | | Mill Existing Asphalt | 4 days | Tue 9/20/22 | Mon 9/26/22 | 61 |
| 70 | 10... | | | Install 10" SAS and Manholes | 16 days | Tue 9/6/22 | Tue 11/8/22 | 63 |
| 71 | 10... | | | 20" Bore Las Cruces Lateral Sta 11+94-12+74 | 4 days | Tue 11/8/22 | Tue 11/15/22 | 70 |

Project: msproj11
Date: Thu 1/12/23

| | | | | | |
|--------------------|--|-----------------------|--|-----------------|--|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Critical | |
| Project Summary | | Duration-only | | Critical Split | |
| External Tasks | | Manual Summary Rollup | | Progress | |
| External Milestone | | Manual Summary | | Manual Progress | |

| ID | % Comp | | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|----|--------|--|-----------|--|------------------|---------------------|---------------------|---------------|
| 72 | 16% | | | East Organ Sta 13+00/Calle Picasso Alignment (570') | 19 days | Wed 11/16/22 | Tue 1/3/23 | |
| 73 | 10... | | | Install 10" SAS and Manholes | 3 days | Wed 11/16/22 | Tue 11/29/22 | 70 |
| 74 | 0% | | | Replace Asphalt Road | 16 days | Tue 11/29/22 | Tue 1/3/23 | 73 |
| 75 | 51% | | | Bar X Alignment LS 16 - MH 029 (1397') | 44.2 days | Tue 10/18/22 | Tue 1/17/23 | |
| 76 | 10... | | | Mill Existing Asphalt | 2 days | Tue 10/18/22 | Thu 10/20/22 | 77SF |
| 77 | 90% | | | Install 8" SAS and Manholes | 8 days | Mon 12/19/22 | Thu 1/5/23 | 73SS+30 edays |
| 78 | 0% | | | Replace Asphalt Road | 8 days | Tue 1/3/23 | Tue 1/17/23 | 74 |
| 79 | 0% | | | Raging Bull Place Alignment LS 16 - MH 033 (1,150') | 7.2 days | Mon 1/9/23 | Thu 1/19/23 | |
| 80 | 0% | | | Install 8" SAS and Manholes | 4 days | Mon 1/9/23 | Thu 1/12/23 | 77 |
| 81 | 0% | | | Replace Gravel Road | 2 days | Tue 1/17/23 | Thu 1/19/23 | 78 |
| 82 | 0% | | | Guererro Alignment LS 16 - MH 025 (303') | 4.2 days | Mon 1/16/23 | Mon 1/23/23 | |
| 83 | 0% | | | Install 8" SAS and Manholes | 2 days | Mon 1/16/23 | Tue 1/17/23 | 80 |
| 84 | 0% | | | Replace Gravel Road | 1 day | Thu 1/19/23 | Mon 1/23/23 | 81 |
| 85 | 0% | | | 4" C900 Force Main (3500') | 8 days | Wed 7/27/22 | Tue 8/9/22 | 33 |
| 86 | 0% | | | Private Services | 48 days | Thu 10/20/22 | Wed 1/25/23 | 40 |
| 87 | 0% | | | Septic Tank Abandonment | 24 days | Tue 12/20/22 | Mon 2/6/23 | 86SS+30 days |
| 88 | 1% | | | ALT 4 - Lift Station 11 | 183 days | Tue 10/18/22 | Thu 9/14/23 | |
| 89 | 0% | | | Mobilization | 8 days | Mon 10/31/22 | Mon 11/14/22 | 186 |
| 90 | 0% | | | Construction Staking | 8 days | Tue 11/1/22 | Mon 11/14/22 | 91SF |
| 91 | 0% | | | Proctor Native Material | 1 day | Tue 11/1/22 | Tue 11/1/22 | 92SF |
| 92 | 0% | | | Pre-Construction Video | 1 day | Tue 11/1/22 | Tue 11/1/22 | 93SF |
| 93 | 0% | | | SW3P BMP's In-Place | 0 days | Mon 10/31/22 | Mon 10/31/22 | 94SF |
| 94 | 0% | | | Traffic Control In-Place | 0 days | Mon 10/31/22 | Mon 10/31/22 | 96SF |

Project: msproj11
Date: Thu 1/12/23

| | | | | | |
|--------------------|--|-----------------------|--|-----------------|--|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Critical | |
| Project Summary | | Duration-only | | Critical Split | |
| External Tasks | | Manual Summary Rollup | | Progress | |
| External Milestone | | Manual Summary | | Manual Progress | |

| ID | % Comp | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|-----|--------|-----------|---|-----------------|---------------------|--------------------|--------------|
| 95 | 3% | | Lift Station 11 | 183 days | Tue 10/18/22 | Thu 9/14/23 | |
| 96 | 50% | | Dewatering System In Place | 8 days | Tue 10/18/22 | Mon 1/23/23 | 97SF |
| 97 | 0% | | Install Precast Wet Well | 4 days | Mon 1/23/23 | Thu 1/26/23 | 83SS+5 edays |
| 98 | 0% | | Valve and Meter Vault | 8 days | Mon 1/30/23 | Thu 2/9/23 | 97 |
| 99 | 0% | | Piping | 12 days | Mon 2/13/23 | Thu 3/2/23 | 98 |
| 100 | 0% | | Pumps | 4 days | Mon 3/6/23 | Thu 3/9/23 | 99 |
| 101 | 0% | | Building Underground | 8 days | Mon 3/13/23 | Thu 3/23/23 | 100 |
| 102 | 0% | | Building Foundation | 8 days | Mon 3/27/23 | Thu 4/6/23 | 101 |
| 103 | 0% | | CMU Walls | 8 days | Mon 4/10/23 | Thu 4/20/23 | 102 |
| 104 | 0% | | Roof System | 4 days | Mon 4/24/23 | Thu 4/27/23 | 103 |
| 105 | 0% | | Doors | 4 days | Mon 5/1/23 | Thu 5/4/23 | 104 |
| 106 | 0% | | HVAC | 4 days | Mon 5/8/23 | Thu 5/11/23 | 105 |
| 107 | 0% | | Mag/Hydroxide Odor Control System | 4 days | Mon 5/15/23 | Thu 5/18/23 | 106 |
| 108 | 0% | | Electrical Service (EPEC) | 0 days | Thu 5/18/23 | Thu 5/18/23 | 107 |
| 109 | 0% | | Electrical | 24 days | Mon 5/22/23 | Thu 6/29/23 | 108 |
| 110 | 0% | | Painting | 4 days | Mon 7/3/23 | Thu 7/6/23 | 109 |
| 111 | 0% | | Water service | 4 days | Mon 7/10/23 | Thu 7/13/23 | 110 |
| 112 | 0% | | Site Chainlink Fence | 32 days | Mon 7/17/23 | Thu 9/7/23 | 111 |
| 113 | 0% | | Site Gravel | 4 days | Mon 9/11/23 | Thu 9/14/23 | 112 |
| 114 | 0% | | Collection System | 63 days | Wed 1/18/23 | Mon 5/8/23 | |
| 115 | 0% | | Minter Rd Alignment LS 11 - MH 07 (2,380') | 34 days | Wed 1/18/23 | Thu 3/16/23 | |
| 116 | 0% | | Mill Existing Asphalt | 6 days | Wed 1/18/23 | Mon 1/30/23 | 117SF |
| 117 | 0% | | Install 8" SAS and Manholes | 16 days | Mon 1/30/23 | Thu 2/23/23 | 97 |
| 118 | 0% | | Replace Asphalt Road | 12 days | Mon 2/27/23 | Thu 3/16/23 | 117 |

Project: msproj11
Date: Thu 1/12/23

| | | | | | |
|--------------------|--|-----------------------|--|-----------------|--|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Critical | |
| Project Summary | | Duration-only | | Critical Split | |
| External Tasks | | Manual Summary Rollup | | Progress | |
| External Milestone | | Manual Summary | | Manual Progress | |

| ID | % Comp | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|-----|--------|-----------|---|----------------|--------------------|--------------------|--------------|
| 119 | 0% | | Contreras Alignment LS 11 - MH 035 (1,018') | 8 days | Mon 2/27/23 | Thu 3/9/23 | |
| 120 | 0% | | Install 8" SAS and Manholes | 6 days | Mon 2/27/23 | Tue 3/7/23 | 117 |
| 121 | 0% | | Replace Gravel Road | 2 days | Wed 3/8/23 | Thu 3/9/23 | 120 |
| 122 | 0% | | Peppermint PL Alignment LS 11 - MH 41 (596') | 5 days | Wed 3/8/23 | Wed 3/15/23 | |
| 123 | 0% | | Install 8" SAS and Manholes | 4 days | Wed 3/8/23 | Tue 3/14/23 | 120 |
| 124 | 0% | | Replace Gravel Road | 1 day | Wed 3/15/23 | Wed 3/15/23 | 123 |
| 125 | 0% | | Tarin/Segovia Lane Alignment LS 11 - MH 045 (1,473') | 11 days | Wed 3/15/23 | Mon 4/3/23 | |
| 126 | 0% | | Install 8" SAS and Manholes | 8 days | Wed 3/15/23 | Tue 3/28/23 | 123 |
| 127 | 0% | | Replace Gravel Road | 3 days | Wed 3/29/23 | Mon 4/3/23 | 126 |
| 128 | 0% | | Sanchez/Jarmon Rd Alignment LS 11 - MH 1 (1,975') | 16 days | Wed 3/29/23 | Tue 4/25/23 | |
| 129 | 0% | | Install 8" SAS and Manholes | 12 days | Wed 3/29/23 | Tue 4/18/23 | 126 |
| 130 | 0% | | Replace Gravel Road | 4 days | Wed 4/19/23 | Tue 4/25/23 | 129 |
| 131 | 0% | | Hatheway Ln Alignment LS 11 - MH 013 (500') | 4 days | Wed 4/19/23 | Tue 4/25/23 | |
| 132 | 0% | | Install 8" SAS and Manholes | 3 days | Wed 4/19/23 | Mon 4/24/23 | 129 |
| 133 | 0% | | Replace Gravel Road | 1 day | Tue 4/25/23 | Tue 4/25/23 | 132 |
| 134 | 0% | | Brenna Rd Alignment LS 11 - MH 15 (369') | 3 days | Tue 4/25/23 | Thu 4/27/23 | |
| 135 | 0% | | Install 8" SAS and Manholes | 2 days | Tue 4/25/23 | Wed 4/26/23 | 132 |
| 136 | 0% | | Replace Gravel Road | 1 day | Thu 4/27/23 | Thu 4/27/23 | 135 |
| 137 | 0% | | Wanabe Rd Alignment LS 11 - MH 019 (740') | 4 days | Thu 4/27/23 | Wed 5/3/23 | |
| 138 | 0% | | Install 8" SAS and Manholes | 3 days | Thu 4/27/23 | Tue 5/2/23 | 135 |
| 139 | 0% | | Replace Gravel Road | 1 day | Wed 5/3/23 | Wed 5/3/23 | 138 |
| 140 | 0% | | Munoz Alignment LS 11 - MH 9 (356') | 3 days | Wed 5/3/23 | Mon 5/8/23 | |
| 141 | 0% | | Install 8" SAS and Manholes | 2 days | Wed 5/3/23 | Thu 5/4/23 | 138 |
| 142 | 0% | | Replace Gravel Road | 1 day | Mon 5/8/23 | Mon 5/8/23 | 141 |

Project: msproj11
Date: Thu 1/12/23

| | | | | | |
|--------------------|--|-----------------------|--|-----------------|--|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Critical | |
| Project Summary | | Duration-only | | Critical Split | |
| External Tasks | | Manual Summary Rollup | | Progress | |
| External Milestone | | Manual Summary | | Manual Progress | |






















| ID | % Comp | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|-----|--------|-----------|--|-----------------|--------------------|---------------------|---------------|
| 143 | 0% | | Lift Station No. 4 Forcemain Alignment (5,100') | 28 days | Mon 5/8/23 | Thu 6/22/23 | |
| 144 | 0% | | 12" Bore HWY 192 44+33-44+93 | 4 days | Mon 5/8/23 | Thu 5/11/23 | 141 |
| 145 | 0% | | 12" Bore Del Rio Drain 43+20-43+90 | 4 days | Mon 5/15/23 | Thu 5/18/23 | 144 |
| 146 | 0% | | Install 4" SAS Ductile Iron (3,400') | 10 days | Mon 5/22/23 | Tue 6/6/23 | 145 |
| 147 | 0% | | Install 4" SAS C900 (1,700') | 5 days | Wed 6/7/23 | Wed 6/14/23 | 146 |
| 148 | 0% | | Air Release Valve Vault | 1 day | Thu 6/15/23 | Thu 6/15/23 | 147 |
| 149 | 0% | | Install 6" SAS Ductile Iron Forcemain (620') | 3 days | Mon 6/19/23 | Wed 6/21/23 | 148 |
| 150 | 0% | | Install 6" SAS C900 (120') | 1 day | Thu 6/22/23 | Thu 6/22/23 | 149 |
| 151 | 0% | | Private Services | 48 days | Mon 6/26/23 | Thu 9/14/23 | 150 |
| 152 | 0% | | Septic Tank Abandonment | 24 days | Mon 8/7/23 | Thu 9/14/23 | 151SS+24 days |
| 153 | 22% | | ALT 3 - Lift Station 12 | 267 days | Wed 5/18/22 | Thu 9/14/23 | |
| 154 | 80% | | Mobilization | 10 days | Wed 5/18/22 | Tue 6/7/22 | |
| 155 | 75% | | Construction Staking | 8 days | Wed 5/18/22 | Thu 6/2/22 | 156SF |
| 156 | 10... | | Proctor Native Material | 1 day | Thu 6/2/22 | Mon 6/6/22 | 157SF |
| 157 | 10... | | Pre-Construction Video | 1 day | Mon 6/6/22 | Tue 6/7/22 | 158SF |
| 158 | 10... | | SW3P BMP's In-Place | 0 days | Tue 6/7/22 | Tue 6/7/22 | 159SF |
| 159 | 10... | | Traffic Control In-Place | 0 days | Tue 6/7/22 | Tue 6/7/22 | 161SF |
| 160 | 22% | | Lift Station 12 | 106 days | Tue 6/7/22 | Mon 12/19/22 | |
| 161 | 10... | | Install Precast Wet Well | 4 days | Tue 6/7/22 | Mon 6/13/22 | 28 |
| 162 | 10... | | Valve and Meter Vault | 8 days | Tue 6/14/22 | Mon 6/27/22 | 161 |
| 163 | 75% | | Piping | 12 days | Tue 6/28/22 | Tue 7/19/22 | 162 |
| 164 | 0% | | Pumps | 4 days | Mon 8/8/22 | Thu 8/11/22 | 163,16 |
| 165 | 0% | | Electrical Service (EPEC) | 0 days | Thu 8/11/22 | Thu 8/11/22 | 164 |


Project: msproj11
Date: Thu 1/12/23

| | | | | | |
|--------------------|--|-----------------------|--|-----------------|--|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Critical | |
| Project Summary | | Duration-only | | Critical Split | |
| External Tasks | | Manual Summary Rollup | | Progress | |
| External Milestone | | Manual Summary | | Manual Progress | |

| ID | % Comp | | Task Mode | Task Name | Duration | Start | Finish | Predecessors |
|-----|--------|---|-----------|--|-----------------|--------------------|--------------------|---------------|
| 166 | 0% | | → | Electrical | 24 days | Mon 8/15/22 | Mon 9/26/22 | 165 |
| 167 | 0% | | → | Painting | 4 days | Tue 9/27/22 | Mon 10/3/22 | 166 |
| 168 | 0% | | → | Water service | 4 days | Tue 10/4/22 | Mon 10/10/22 | 167 |
| 169 | 0% | | → | Site Chainlink Fencing | 32 days | Tue 10/11/22 | Mon 12/12/22 | 168 |
| 170 | 0% | | → | Site Gravel | 4 days | Tue 12/13/22 | Mon 12/19/22 | 169 |
| 171 | 14% | | → | Collection System | 178 days | Mon 7/25/22 | Wed 6/14/23 | |
| 172 | 10... | ✓ | → | Carnation CT Alignment LS 12 - MH 055 (1006') | 10 days | Mon 7/25/22 | Tue 8/9/22 | |
| 173 | 10... | ✓ | → | Install 8" SAS and Manholes | 8 days | Mon 7/25/22 | Thu 8/4/22 | 183 |
| 174 | 10... | ✓ | → | Replace Gravel Road | 2 days | Mon 8/8/22 | Tue 8/9/22 | 173 |
| 175 | 0% | | → | HWY 478 Alignment LS 12 - MH 051 (1,600') | 23 days | Tue 5/2/23 | Thu 6/8/23 | |
| 176 | 0% | | → | Mill Existing Asphalt | 3 days | Tue 5/2/23 | Mon 5/8/23 | 177SF |
| 177 | 0% | | → | Install 10" SAS and Manholes | 12 days | Mon 5/8/23 | Thu 5/25/23 | 141 |
| 178 | 0% | | → | Replace Asphalt Road | 8 days | Mon 5/29/23 | Thu 6/8/23 | 177 |
| 179 | 0% | | → | Memory Lane Alignment LS 12 - MH 61 (900') | 6 days | Mon 5/29/23 | Tue 6/6/23 | |
| 180 | 0% | | → | Install 8" SAS and Manholes | 5 days | Mon 5/29/23 | Mon 6/5/23 | 177 |
| 181 | 0% | | → | Replace Gravel Road | 1 day | Tue 6/6/23 | Tue 6/6/23 | 180 |
| 182 | 0% | | → | Indian Lane Alignment LS 12 - MH 058 (850') | 6 days | Tue 6/6/23 | Wed 6/14/23 | |
| 183 | 0% | | → | Install 8" SAS and Manholes | 5 days | Tue 6/6/23 | Tue 6/13/23 | 180 |
| 184 | 0% | | → | Replace Gravel Road | 1 day | Wed 6/14/23 | Wed 6/14/23 | 183 |
| 185 | 0% | | → | Private Services | 16 days | Tue 9/27/22 | Mon 10/24/22 | 166 |
| 186 | 0% | | → | Septic Tank Abandonment | 8 days | Tue 10/18/22 | Mon 10/31/22 | 185SS+12 days |
| 187 | 0% | ! | → | Substantial Completion (450 Calendar Days) | 0 days | Thu 9/14/23 | Thu 9/14/23 | 152 |


Project: msproj11
Date: Thu 1/12/23

| | | | | | |
|--------------------|---|-----------------------|---|-----------------|---|
| Task |  | Inactive Task |  | Start-only |  |
| Split |  | Inactive Milestone |  | Finish-only |  |
| Milestone |  | Inactive Summary |  | Deadline |  |
| Summary |  | Manual Task |  | Critical |  |
| Project Summary |  | Duration-only |  | Critical Split |  |
| External Tasks |  | Manual Summary Rollup |  | Progress |  |
| External Milestone |  | Manual Summary |  | Manual Progress |  |

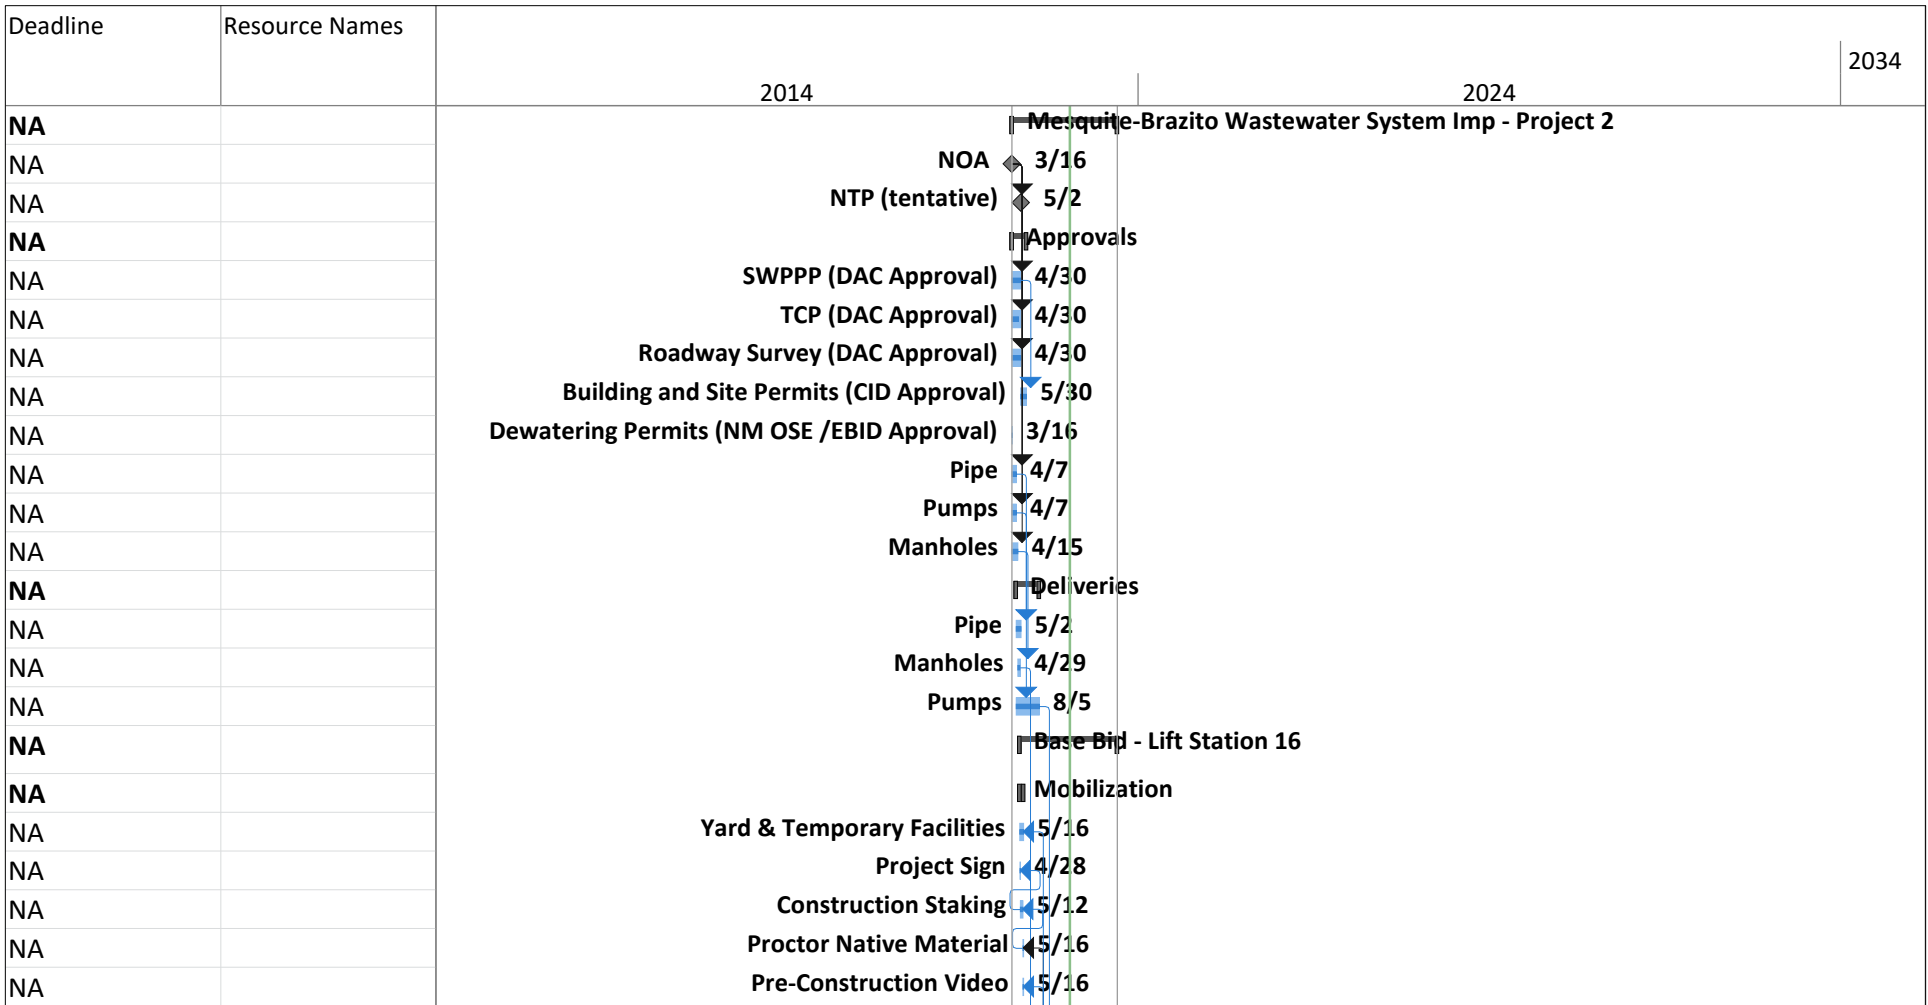

Project: msproj11
Date: Thu 1/12/23


| | | | | | |
|--------------------|--|-----------------------|--|-----------------|--|
| Task | | Inactive Task | | Start-only | |
| Split | | Inactive Milestone | | Finish-only | |
| Milestone | | Inactive Summary | | Deadline | |
| Summary | | Manual Task | | Critical | |
| Project Summary | | Duration-only | | Critical Split | |
| External Tasks | | Manual Summary Rollup | | Progress | |
| External Milestone | | Manual Summary | | Manual Progress | |

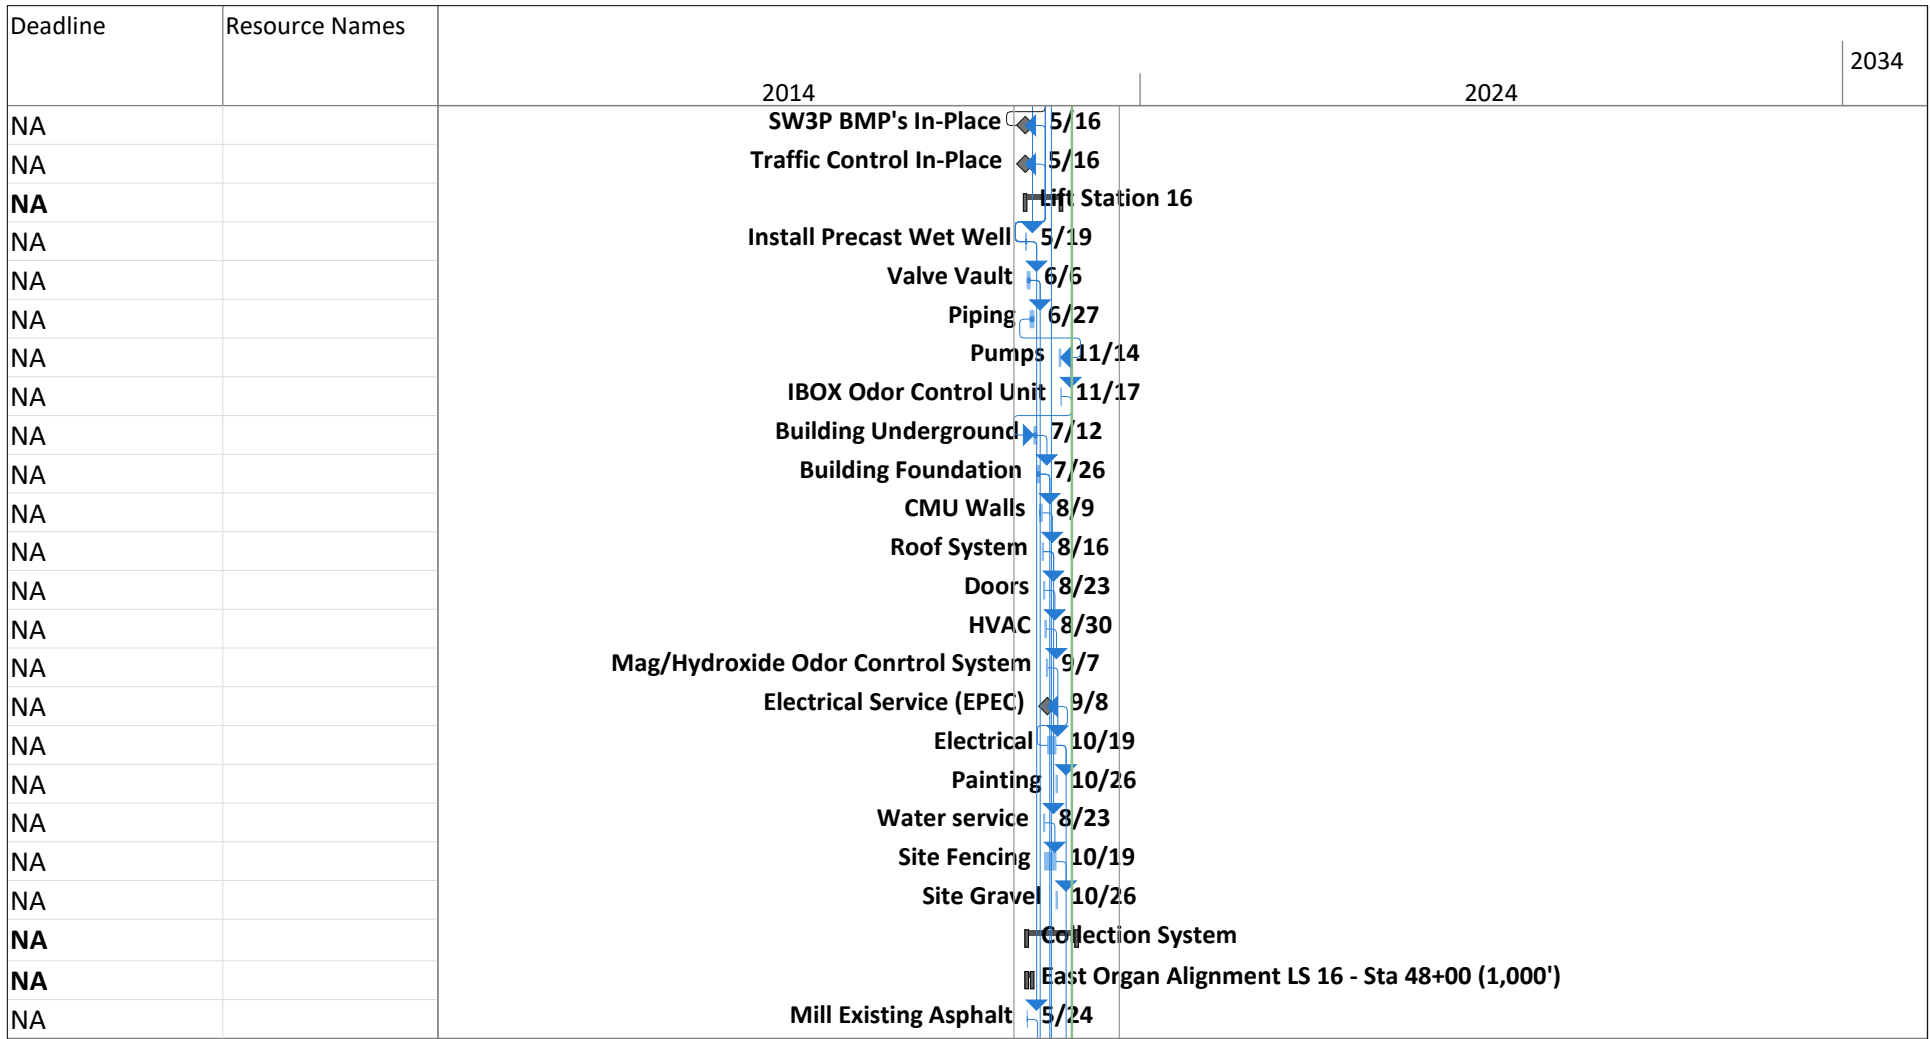


| | | | | | | |
|--|--------------------|--|-----------------------|--|-----------------|--|
| Project: msproj11 Date: Thu 1/12/23 | Task | | Inactive Task | | Start-only | |
| | Split | | Inactive Milestone | | Finish-only | |
| | Milestone | | Inactive Summary | | Deadline | |
| | Summary | | Manual Task | | Critical | |
| | Project Summary | | Duration-only | | Critical Split | |
| | External Tasks | | Manual Summary Rollup | | Progress | |
| | External Milestone | | Manual Summary | | Manual Progress | |

| Deadline | Resource Names | 2014 | 2024 | 2034 |
|----------|----------------|---|-------|--|
| NA | | Install 10" SAS and Manholes | 6/13 | |
| NA | | 20" Bore Mesquite Drain Sta 48+62-49+97 | 6/20 | |
| NA | | | | BBQ/Picnic CT Alignment LS 16 - MH 049 (1405') |
| NA | | Mill Existing Asphalt | 6/15 | |
| NA | | Install 8" SAS and Manholes | 6/27 | |
| NA | | | | East Organ Alignment Sta 48+00 - 64+00 (1,600') |
| NA | | Mill Existing Asphalt | 6/28 | |
| NA | | Install 10" SAS and Manholes | 8/18 | |
| NA | | Replace Asphalt Road | 9/12 | |
| NA | | 20" Bore Apache Lateral Sta 64+10-64+80 | 10/10 | |
| NA | | | | Valles/Relic Alignment LS 16 - MH 046 (1692') |
| NA | | Mill Existing Asphalt | 8/23 | |
| NA | | Install 8" SAS and Manholes | 10/6 | |
| NA | | Replace Asphalt Road | 9/19 | |
| NA | | | | Primos CT/Relic CT Alignment LS 16 - MH 048 (1,296') |
| NA | | Install 8" SAS and Manholes | 10/18 | |
| NA | | Replace Gravel Road | 10/25 | |
| NA | | | | El Milagro rd. Alignment LS 16 - MH 040 (1242') |
| NA | | Install 8" SAS and Manholes | 9/1 | |
| NA | | Replace Gravel Road | 9/12 | |
| NA | | | | East Organ Alignment Sta 39+67 - 13+00 (2,700') |
| NA | | Mill Existing Asphalt | 9/26 | |
| NA | | Install 10" SAS and Manholes | 11/8 | |
| NA | | 20" Bore Las Cruces Lateral Sta 11+94-12+74 | 11/15 | |

| | | | | | | |
|--|--------------------|--|-----------------------|--|-----------------|--|
| Project: msproj11 Date: Thu 1/12/23 | Task | | Inactive Task | | Start-only | |
| | Split | | Inactive Milestone | | Finish-only | |
| | Milestone | | Inactive Summary | | Deadline | |
| | Summary | | Manual Task | | Critical | |
| | Project Summary | | Duration-only | | Critical Split | |
| | External Tasks | | Manual Summary Rollup | | Progress | |
| | External Milestone | | Manual Summary | | Manual Progress | |

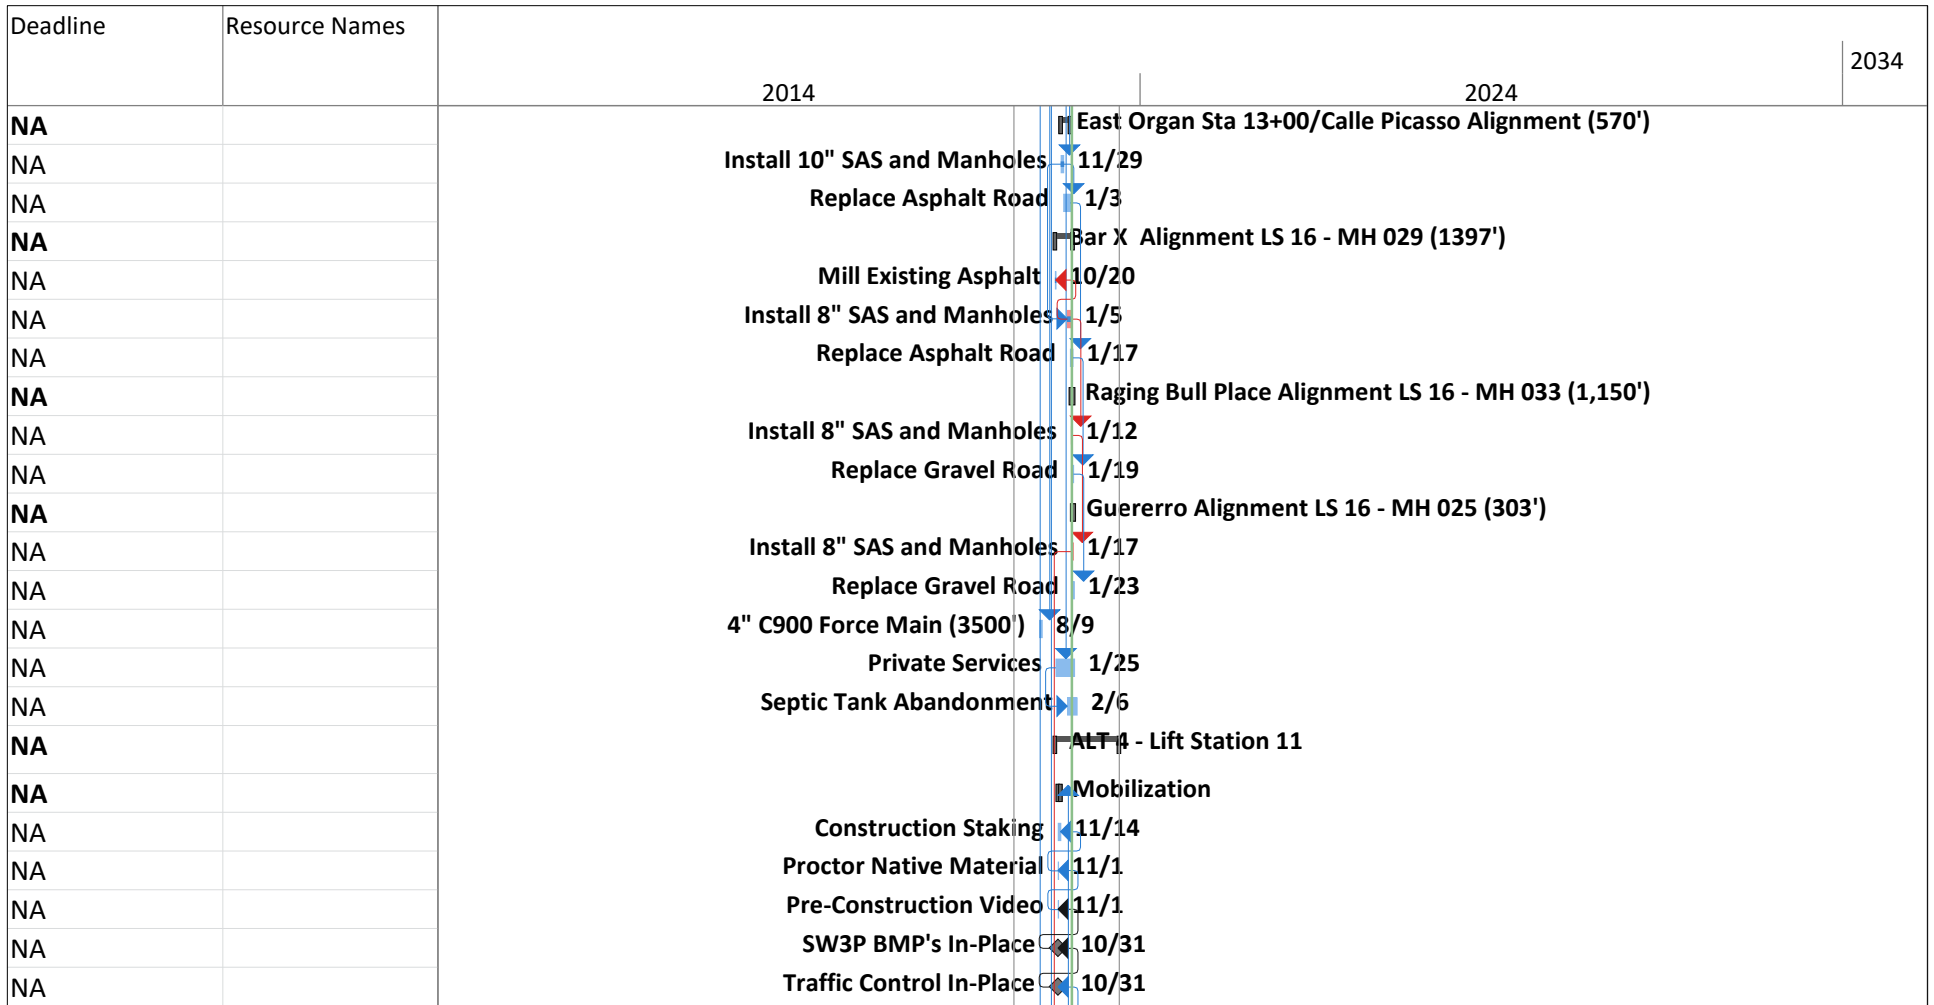


| | | | | | | |
|--|--------------------|--|-----------------------|--|-----------------|--|
| Project: msproj11 Date: Thu 1/12/23 | Task | | Inactive Task | | Start-only | |
| | Split | | Inactive Milestone | | Finish-only | |
| | Milestone | | Inactive Summary | | Deadline | |
| | Summary | | Manual Task | | Critical | |
| | Project Summary | | Duration-only | | Critical Split | |
| | External Tasks | | Manual Summary Rollup | | Progress | |
| | External Milestone | | Manual Summary | | Manual Progress | |

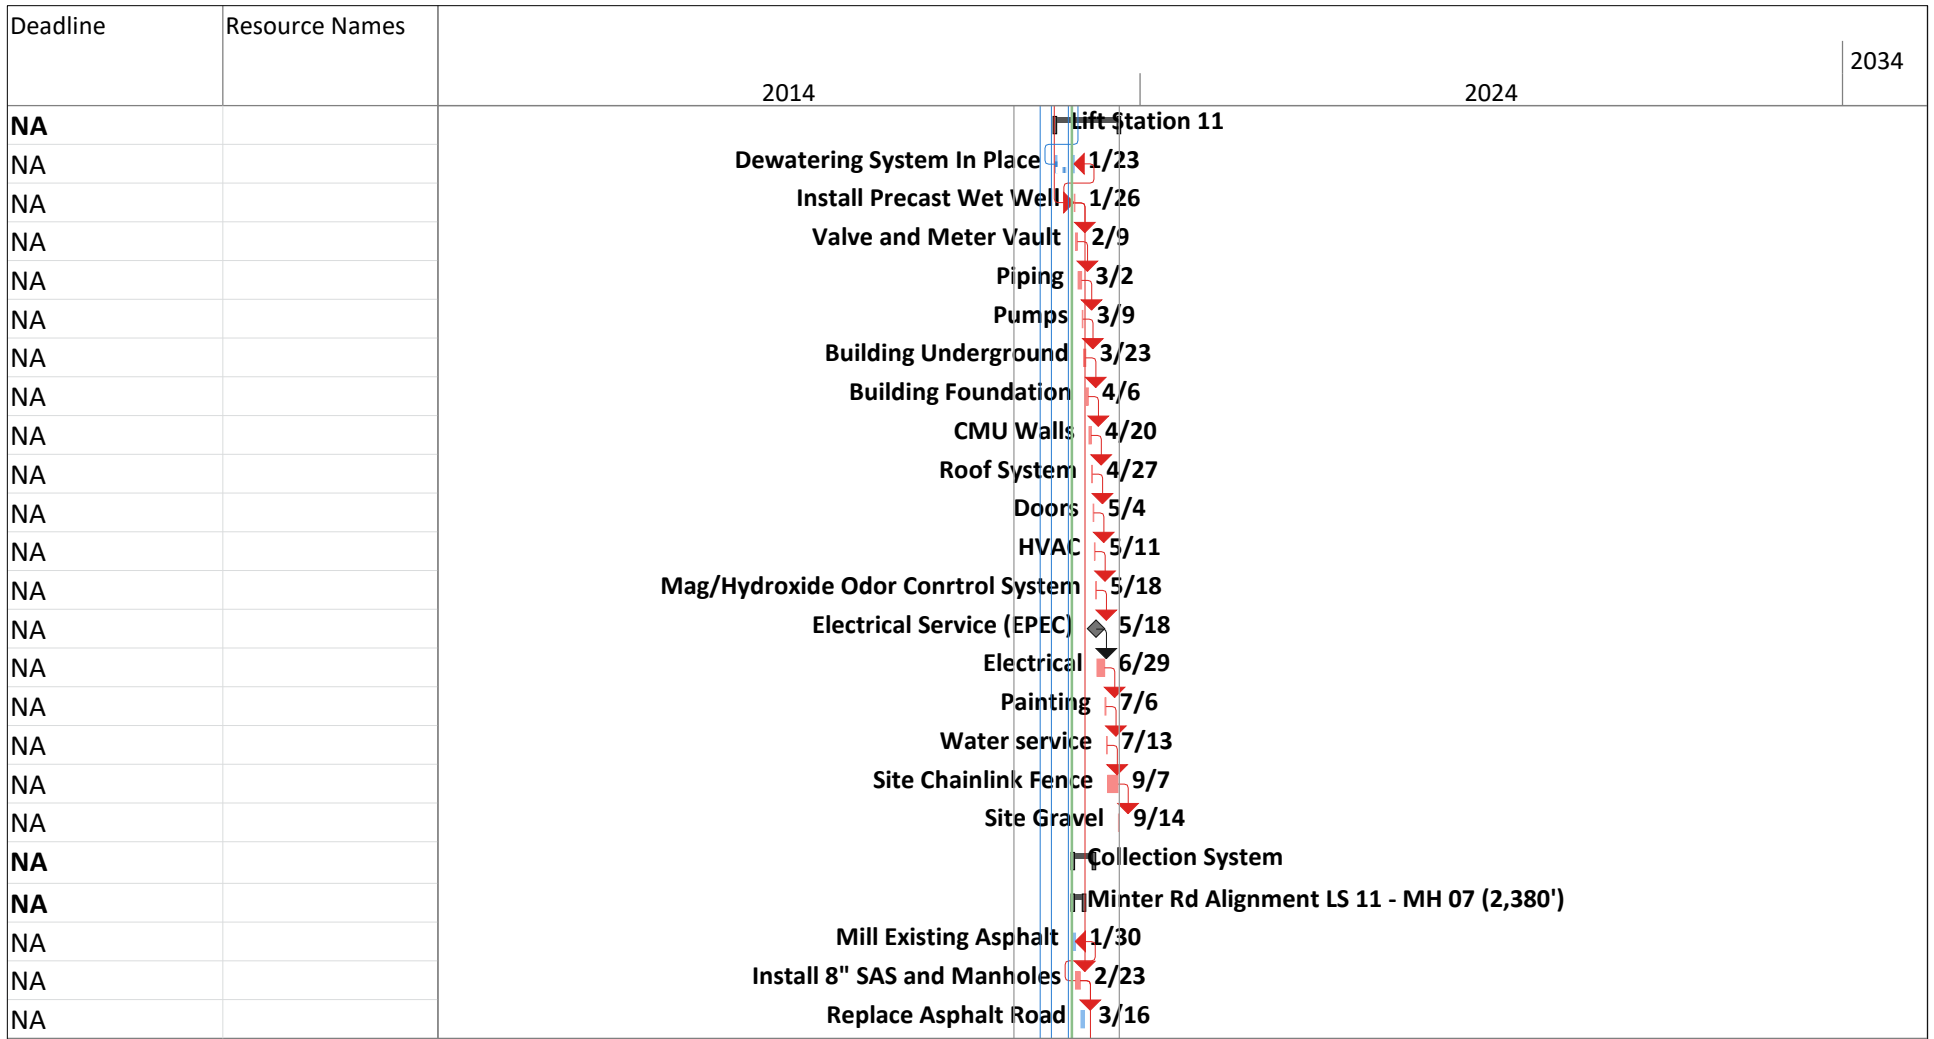


| | | | | | | |
|--|--------------------|--|-----------------------|--|-----------------|--|
| Project: msproj11 Date: Thu 1/12/23 | Task | | Inactive Task | | Start-only | |
| | Split | | Inactive Milestone | | Finish-only | |
| | Milestone | | Inactive Summary | | Deadline | |
| | Summary | | Manual Task | | Critical | |
| | Project Summary | | Duration-only | | Critical Split | |
| | External Tasks | | Manual Summary Rollup | | Progress | |
| | External Milestone | | Manual Summary | | Manual Progress | |

| Deadline | Resource Names | | | 2034 | | |
|--|--------------------|-----------------------------|--|------|-----------------|--|
| | | 2014 | 2024 | | | |
| NA | | | Contreras Alignment LS 11 - MH 035 (1,018') | | | |
| NA | | Install 8" SAS and Manholes | 3/7 | | | |
| NA | | Replace Gravel Road | 3/9 | | | |
| NA | | | Peppermint PL Alignment LS 11 - MH 41 (596') | | | |
| NA | | Install 8" SAS and Manholes | 3/14 | | | |
| NA | | Replace Gravel Road | 3/15 | | | |
| NA | | | Tarin/Segovia Lane Alignment LS 11 - MH 045 (1,473') | | | |
| NA | | Install 8" SAS and Manholes | 3/28 | | | |
| NA | | Replace Gravel Road | 4/3 | | | |
| NA | | | Sanchez/Jarmon Rd Alignment LS 11 - MH 1 (1,975') | | | |
| NA | | Install 8" SAS and Manholes | 4/18 | | | |
| NA | | Replace Gravel Road | 4/25 | | | |
| NA | | | Hatheway Ln Alignment LS 11 - MH 013 (500') | | | |
| NA | | Install 8" SAS and Manholes | 4/24 | | | |
| NA | | Replace Gravel Road | 4/25 | | | |
| NA | | | Brenna Rd Alignment LS 11 - MH 15 (369') | | | |
| NA | | Install 8" SAS and Manholes | 4/26 | | | |
| NA | | Replace Gravel Road | 4/27 | | | |
| NA | | | Wanabe Rd Alignment LS 11 - MH 019 (740') | | | |
| NA | | Install 8" SAS and Manholes | 5/2 | | | |
| NA | | Replace Gravel Road | 5/3 | | | |
| NA | | | Munoz Alignment LS 11 - MH 9 (356') | | | |
| NA | | Install 8" SAS and Manholes | 5/4 | | | |
| NA | | Replace Gravel Road | 5/8 | | | |
| Project: msproj11 Date: Thu 1/12/23 | Task | | Inactive Task | | Start-only | |
| | Split | | Inactive Milestone | | Finish-only | |
| | Milestone | | Inactive Summary | | Deadline | |
| | Summary | | Manual Task | | Critical | |
| | Project Summary | | Duration-only | | Critical Split | |
| | External Tasks | | Manual Summary Rollup | | Progress | |
| | External Milestone | | Manual Summary | | Manual Progress | |
| Page 14 | | | | | | |

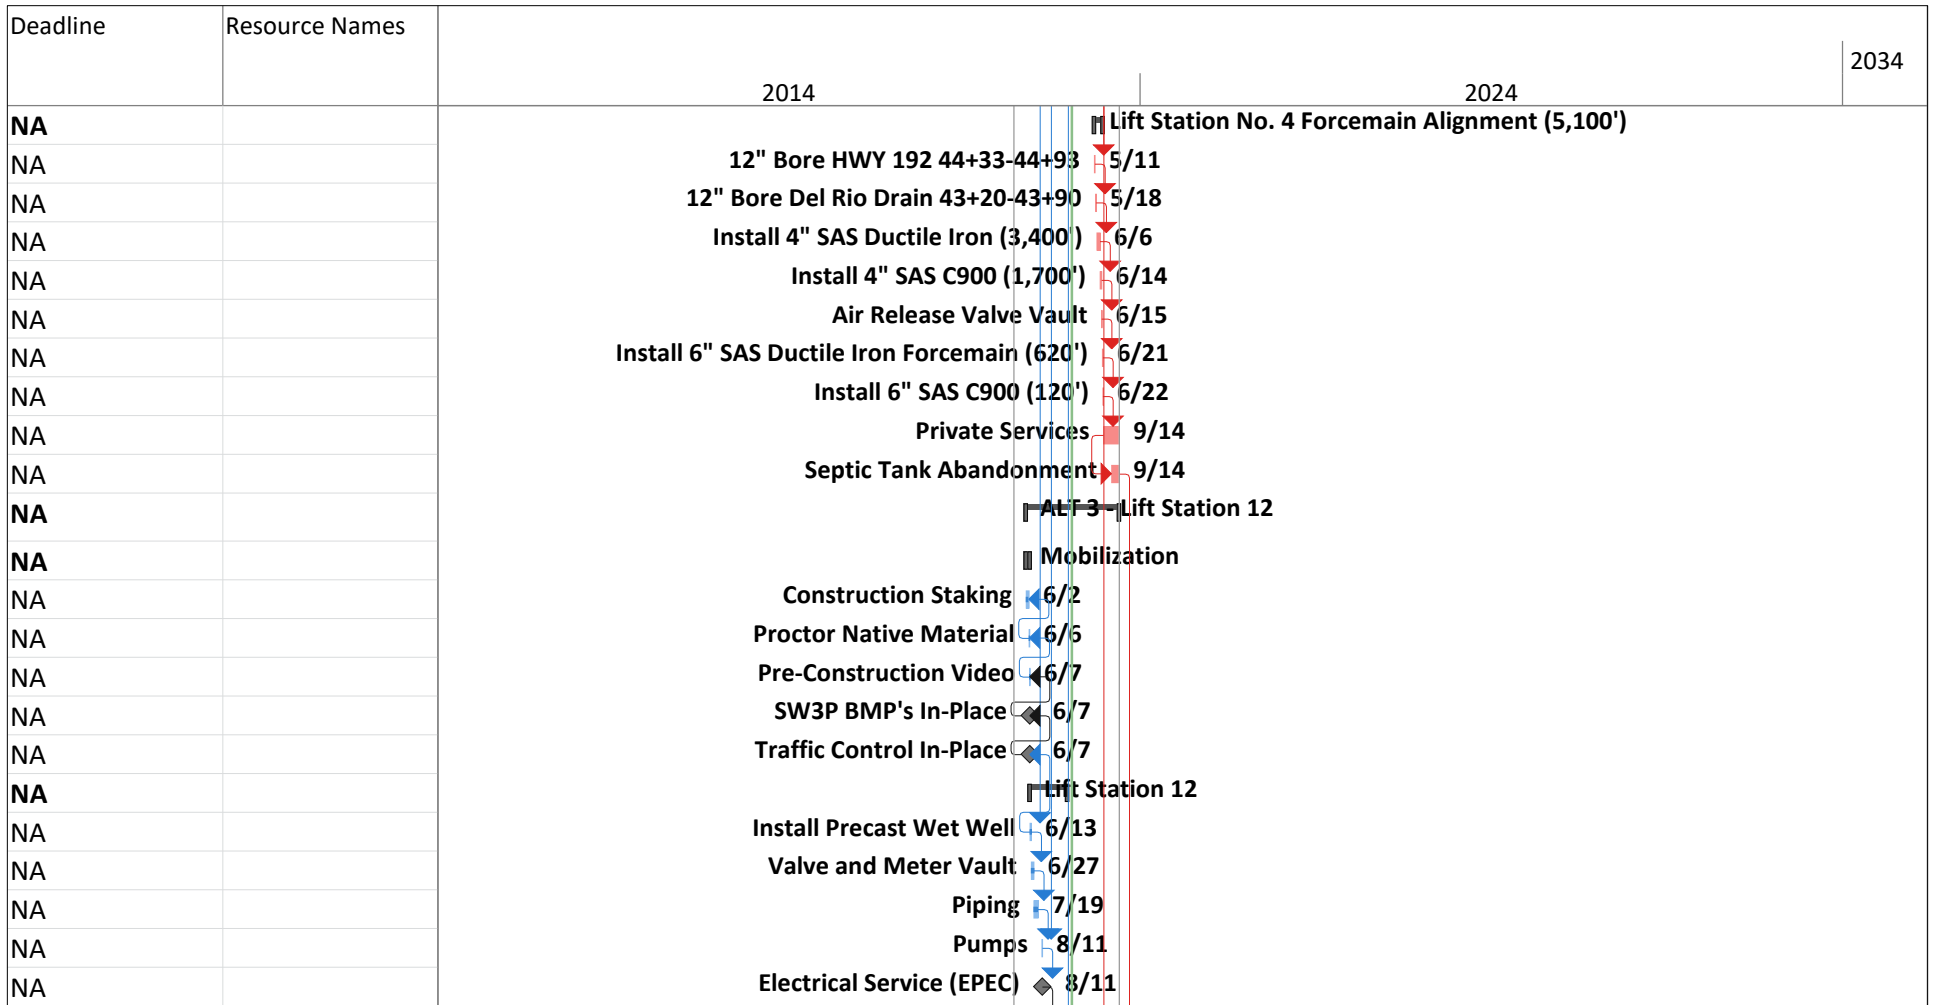

| | | | | | | |
|--|--------------------|--|-----------------------|--|-----------------|--|
| Project: msproj11 Date: Thu 1/12/23 | Task | | Inactive Task | | Start-only | |
| | Split | | Inactive Milestone | | Finish-only | |
| | Milestone | | Inactive Summary | | Deadline | |
| | Summary | | Manual Task | | Critical | |
| | Project Summary | | Duration-only | | Critical Split | |
| | External Tasks | | Manual Summary Rollup | | Progress | |
| | External Milestone | | Manual Summary | | Manual Progress | |

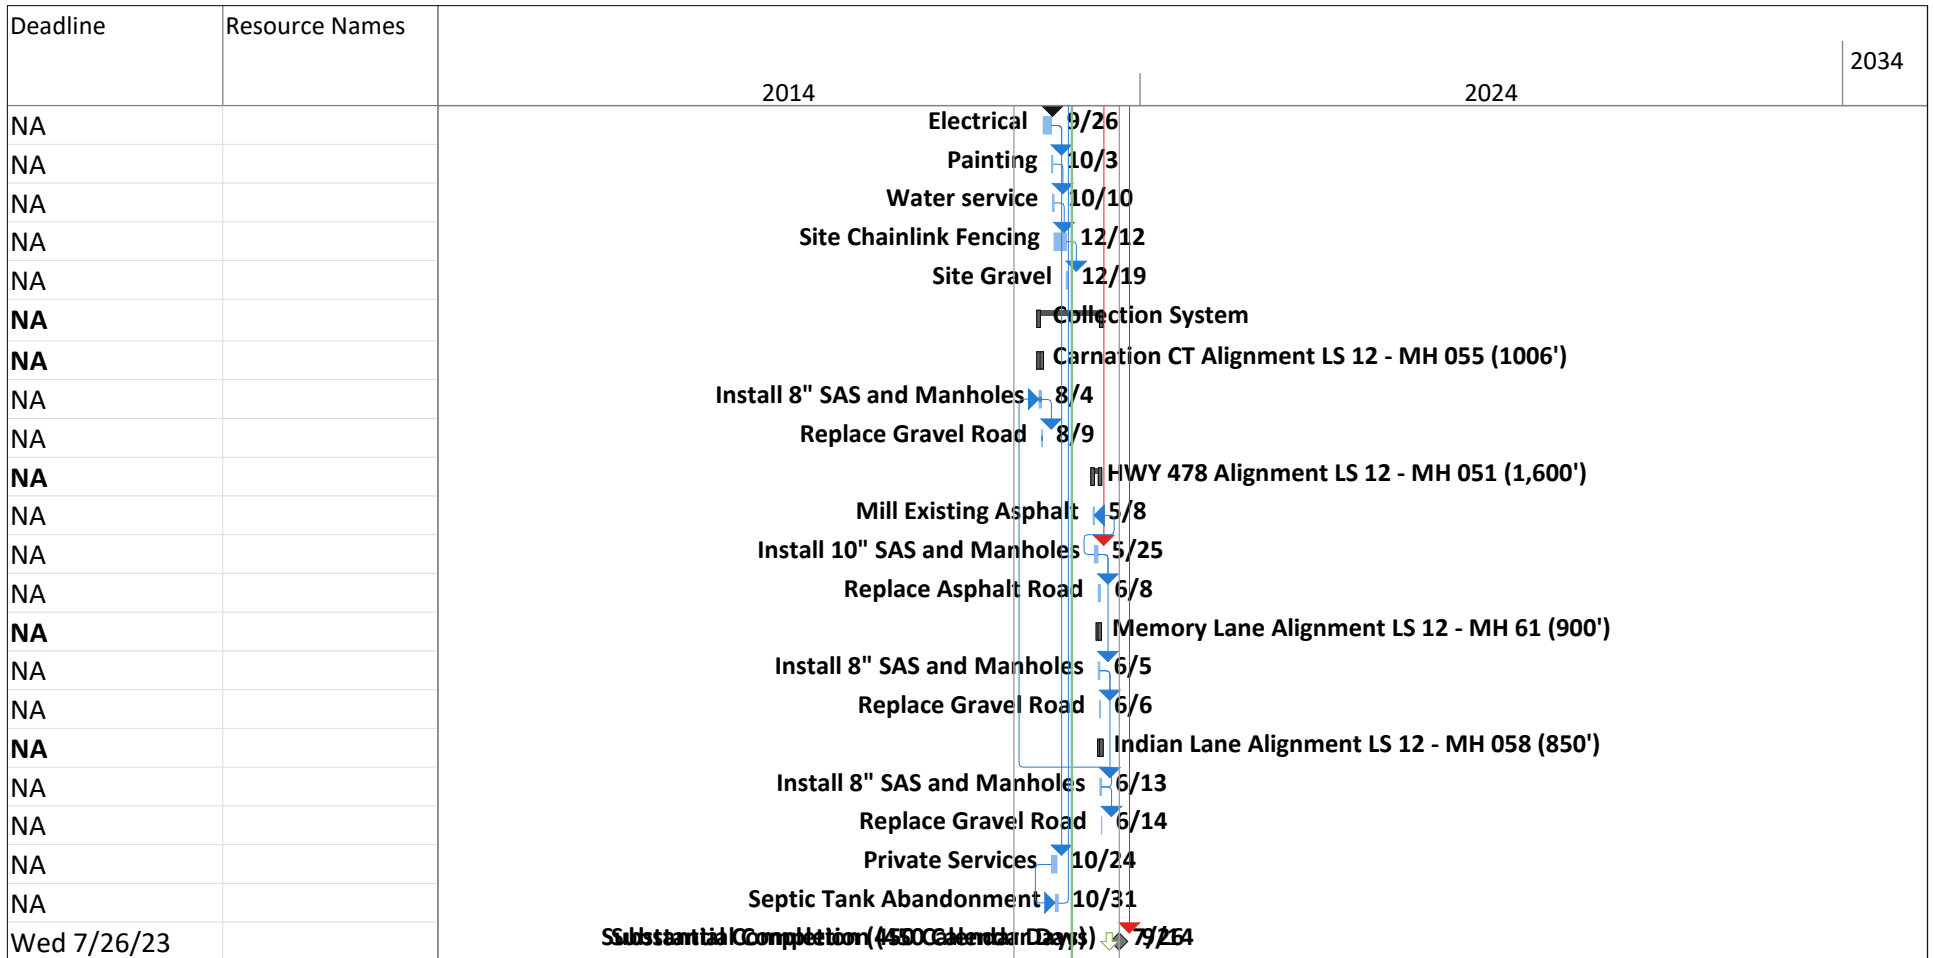

| | | | | | | |
|--|--------------------|--|-----------------------|--|-----------------|--|
| Project: msproj11 Date: Thu 1/12/23 | Task | | Inactive Task | | Start-only | |
| | Split | | Inactive Milestone | | Finish-only | |
| | Milestone | | Inactive Summary | | Deadline | |
| | Summary | | Manual Task | | Critical | |
| | Project Summary | | Duration-only | | Critical Split | |
| | External Tasks | | Manual Summary Rollup | | Progress | |
| | External Milestone | | Manual Summary | | Manual Progress | |
