












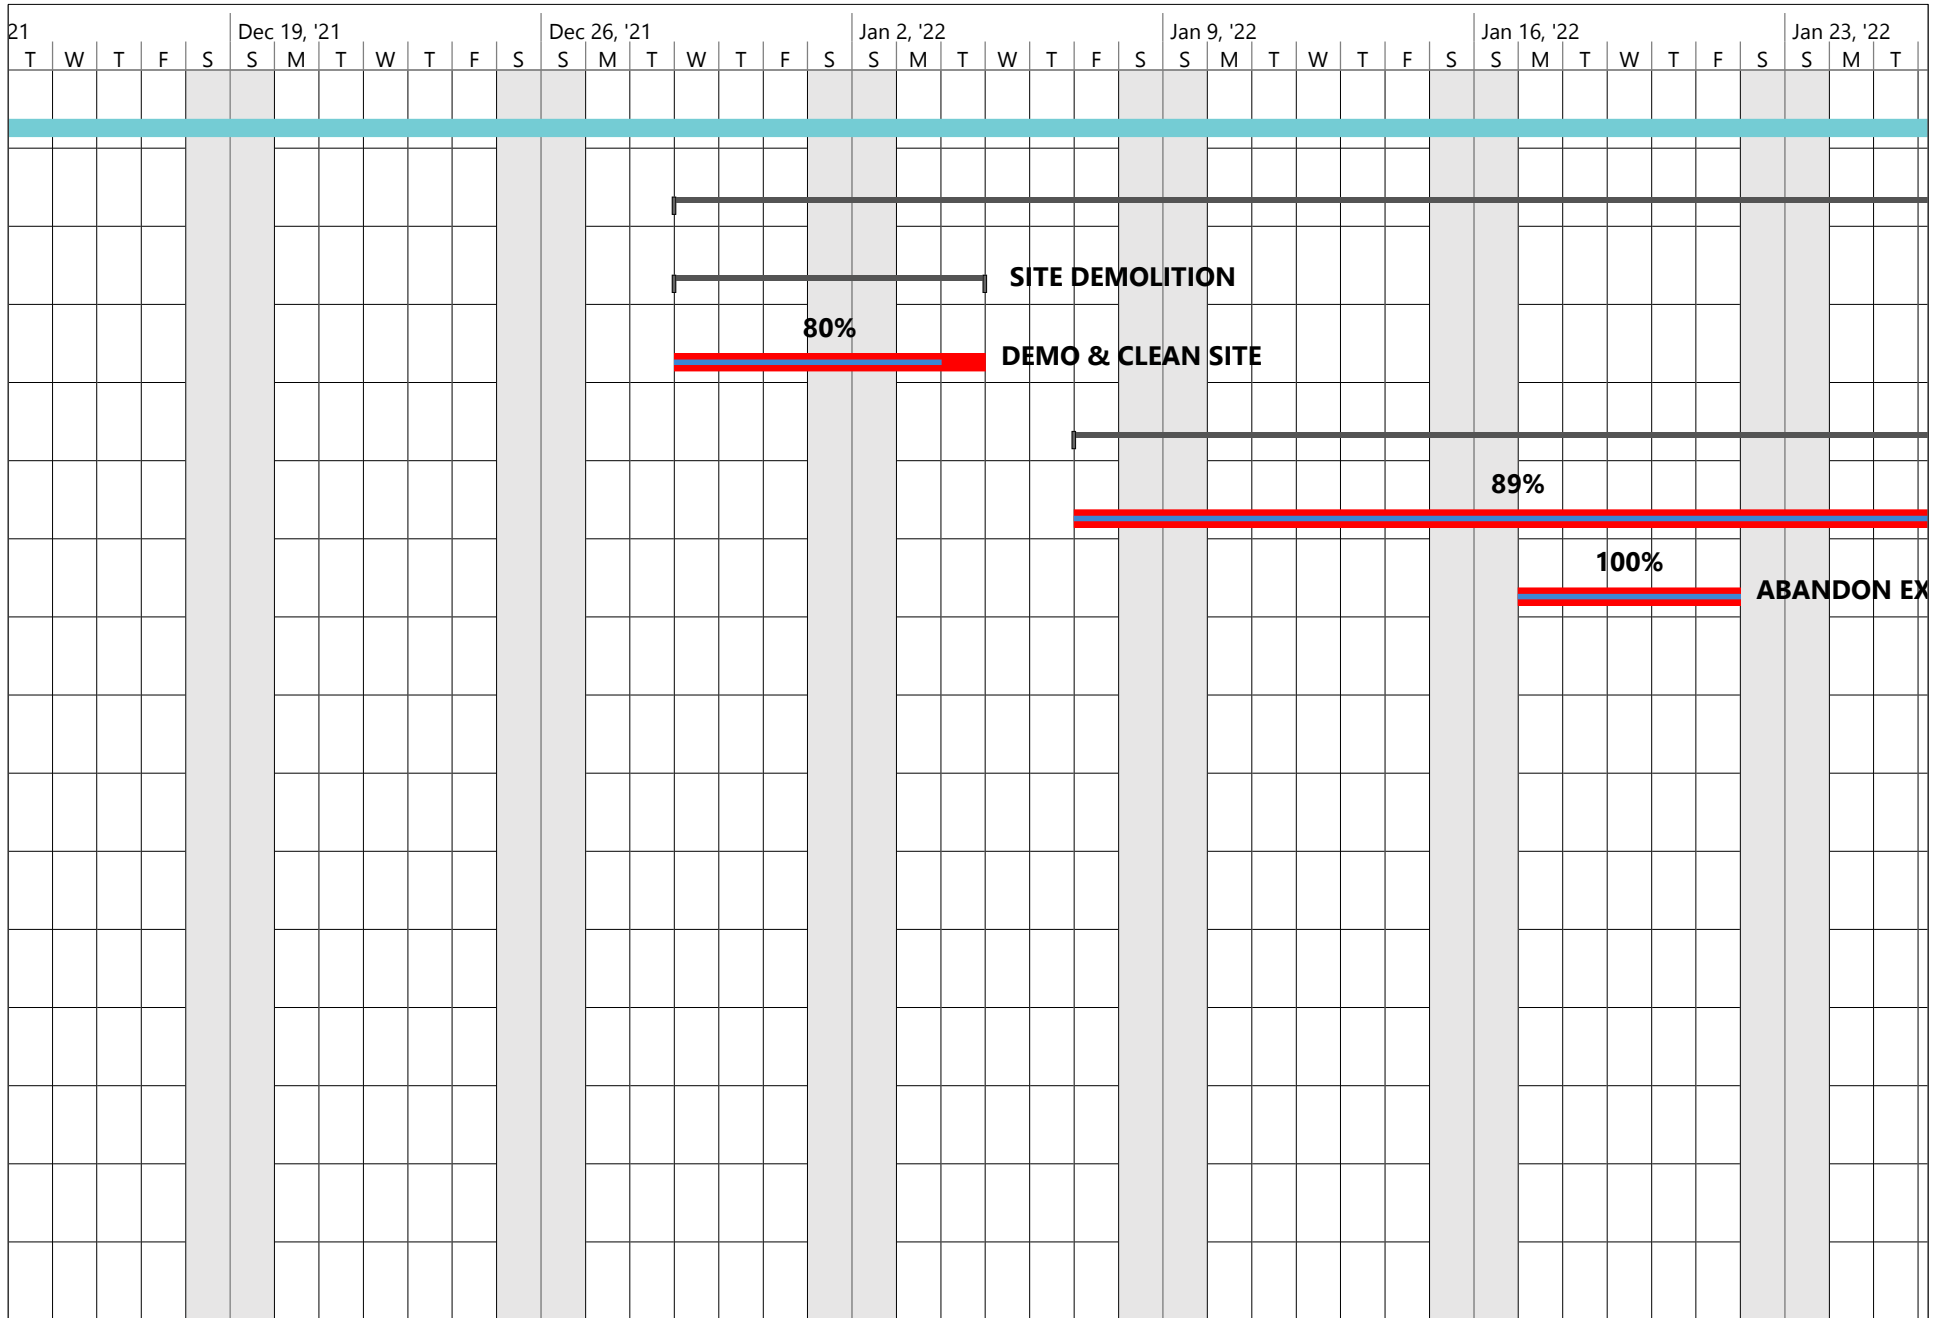



ID	Task Name	Duration	Start	Finish	Predecessors	Dec 5, '21							Dec 12, '2		
						S	M	T	W	T	F	S	S	M	
1	 PROJECT TIME	240 days	Mon 12/6/21	Tue 8/2/22											
2	 CONSTRUCTION TIME WITH MODIFIED TIME	193 days	Wed 12/29/21	Fri 9/23/22											
3	 SITE DEMOLITION	5 days	Wed 12/29/21	Tue 1/4/22											
4	 DEMO & CLEAN SITE	5 days	Wed 12/29/21	Tue 1/4/22											
5	 NEW WELL	45 days	Fri 1/7/22	Thu 3/10/22											
6	 DRILL NEW WELL	45 days	Fri 1/7/22	Thu 3/10/22											
7	 ABANDON EXISTING WELL	5 days	Mon 1/17/22	Fri 1/21/22											
8	 NEW BUILDING	125 days	Mon 4/4/22	Fri 9/23/22											
9	 OVER-EX FOUNDATION/DIG FOOTINGS	11 days	Mon 4/4/22	Mon 4/18/22											
10	 FOOTING REINFORCEMENT	5 days	Mon 4/25/22	Fri 4/29/22											
11	 POUR FOOTINGS	1 day	Wed 5/4/22	Wed 5/4/22											
12	 PLUMBING ROUGH IN	5 days	Mon 5/9/22	Fri 5/13/22											
13	 ELECTRICAL ROUGH IN	15 days	Mon 5/16/22	Fri 6/3/22											
14	 SLAB REINFORCEMENT	12 days	Mon 4/18/22	Tue 5/3/22											
15	 POUR SLAB	1.5 days	Wed 6/8/22	Thu 6/9/22											
16	 MASONRY	12 days	Mon 6/13/22	Tue 6/28/22											

ID	Task Name	Duration	Start	Finish	Predecessors	Dec 5, '21							Dec 12, '2		
						S	M	T	W	T	F	S	S	M	
17	 ROOF	13 days	Wed 6/29/22	Fri 7/15/22	16										
18	 WALL COATINGS	3 days	Mon 7/18/22	Wed 7/20/22	17										
19	 ELECTRICAL	30 days	Thu 7/21/22	Wed 8/31/22	18										
20	 PLUMBING	7 days	Wed 7/6/22	Thu 7/14/22											
21	 HVAC	7 days	Wed 7/6/22	Thu 7/14/22											
22	 FLOOR & FINAL COATINGS	5 days	Mon 9/5/22	Fri 9/9/22											
23	 INSTALL ARSENIC EQUIPMENT	5 days	Mon 9/19/22	Fri 9/23/22											
24	 NEW SLUDGE BEDS	57 days	Mon 4/11/22	Tue 6/28/22											
25	 OVER-EX FOUNDATION/DIG FOOTINGS	10 days	Mon 4/11/22	Fri 4/22/22											
26	 SITE PIPING	20 days	Mon 4/25/22	Tue 6/28/22											
27	 FORM BED FLOOR	16 days	Tue 5/3/22	Mon 6/6/22											
28	 FORM BED WALLS	3 days	Wed 6/8/22	Fri 6/10/22											
29	 BED REINFORCEMENT	3 days	Wed 6/1/22	Fri 6/3/22											
30	 POUR BED FLOOR	3 days	Wed 6/1/22	Fri 6/3/22											
31	 POUR BED WALLS	1 day	Tue 6/14/22	Tue 6/14/22											
32	 SITE WORK	30 days	Thu 7/21/22	Wed 8/31/22											

ID		Task Name	Duration	Start	Finish	Predecessors	Dec 5, '21							Dec 12, '2	
							S	M	T	W	T	F	S	S	M
33		SHAPE AND GRADE SITE & PONDS	5 days	Mon 8/15/22	Fri 8/19/22										
34		CONCRETE WORK IN PONDS	5 days	Thu 7/21/22	Wed 7/27/22										
35		RIP RAP IN PONDS	10 days	Thu 7/28/22	Wed 8/10/22	34									
36		CONCRETE WORK AROUND BUILDING	5 days	Thu 8/11/22	Wed 8/17/22	35									
37		LANDSCAPING	10 days	Thu 8/18/22	Wed 8/31/22	36									




21					Dec 19, '21					Dec 26, '21					Jan 2, '22					Jan 9, '22					Jan 16, '22					Jan 23, '22					
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

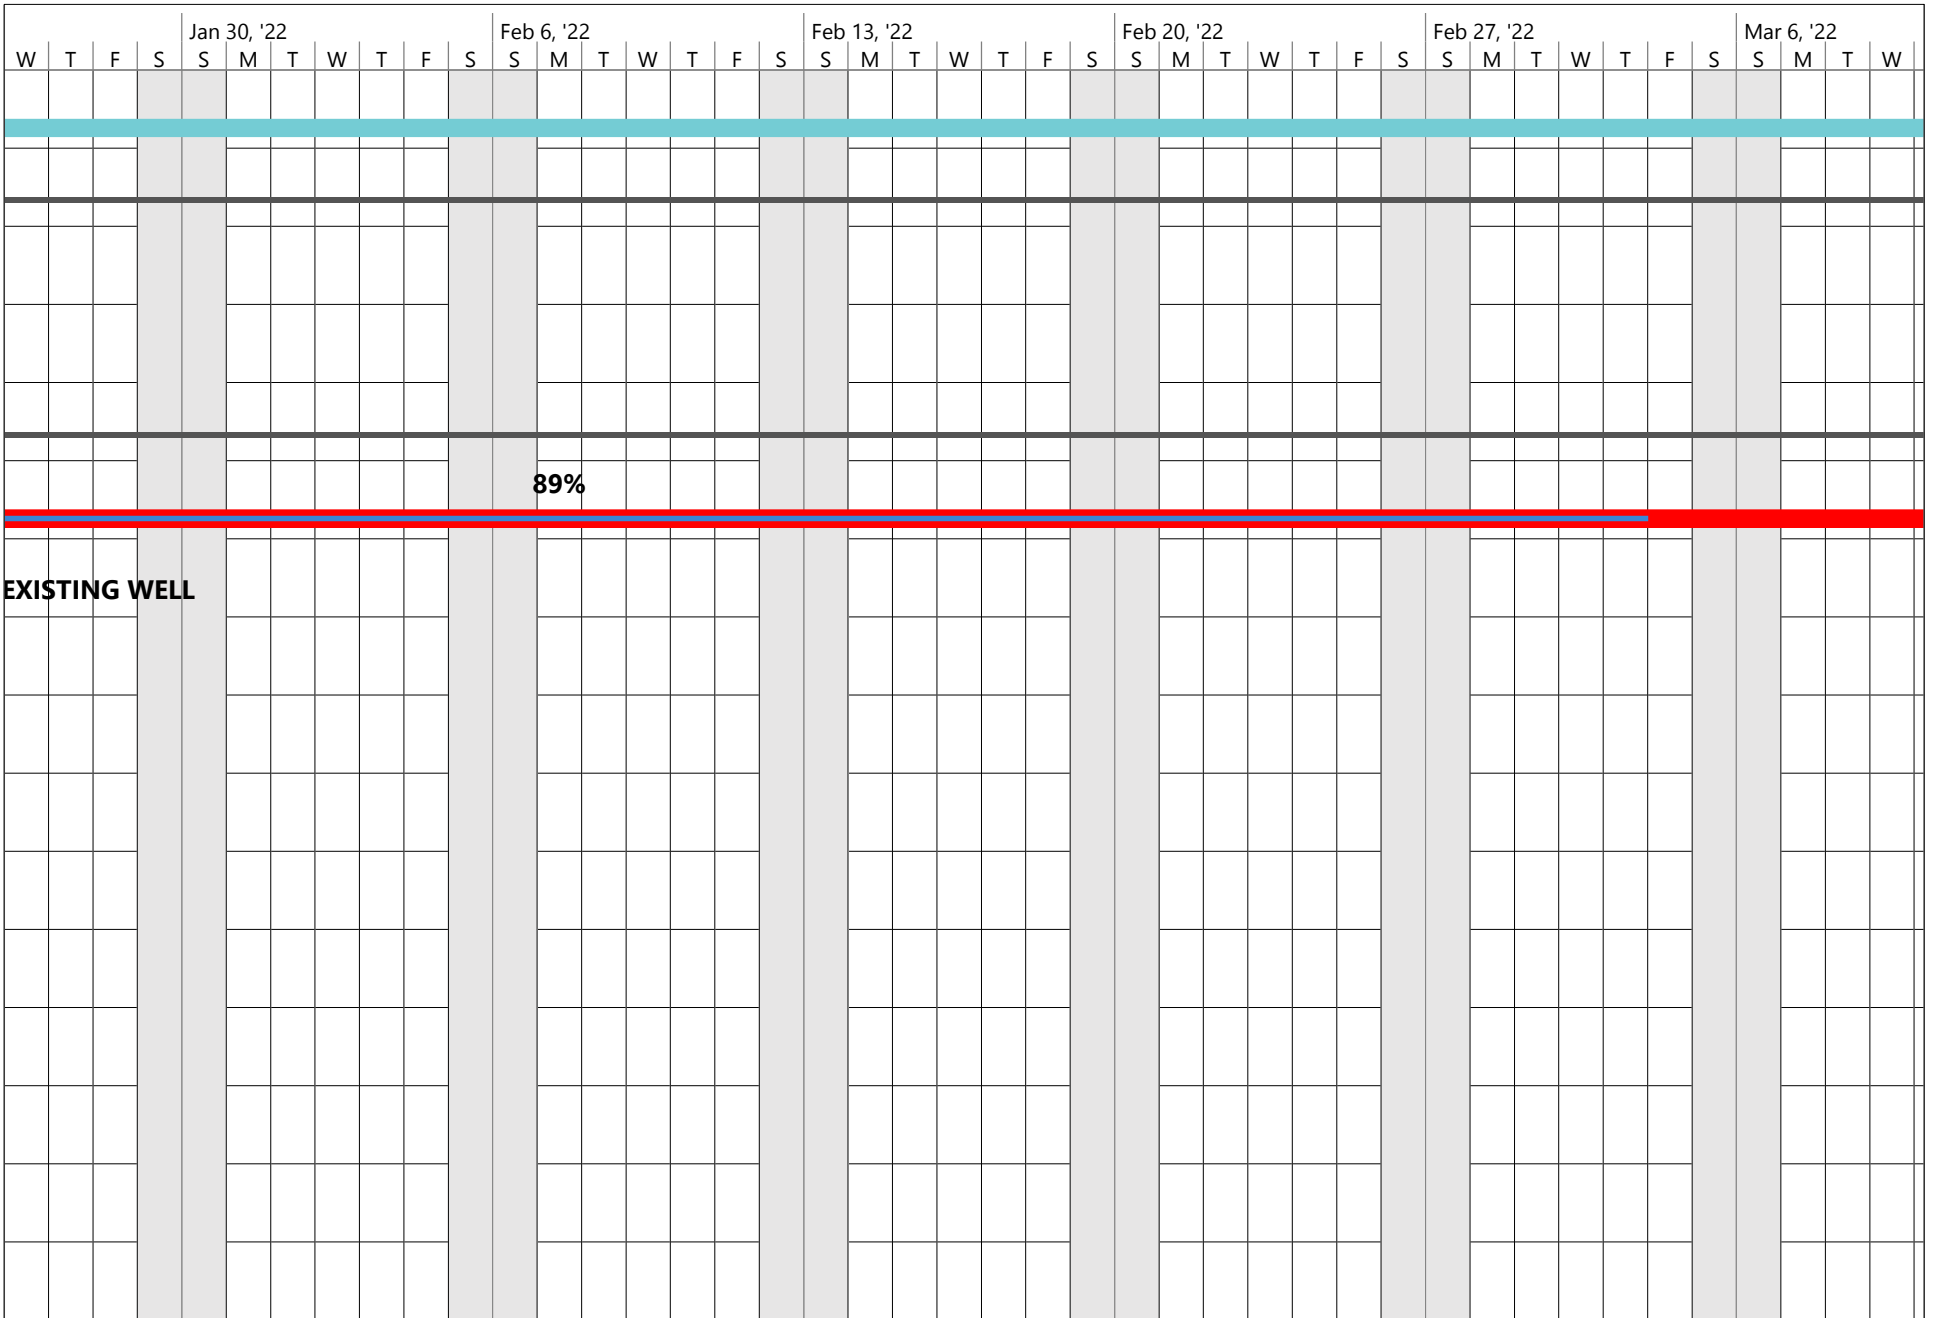



EXISTING WELL

89%


				Jan 30, '22					Feb 6, '22					Feb 13, '22					Feb 20, '22					Feb 27, '22					Mar 6, '22													
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W

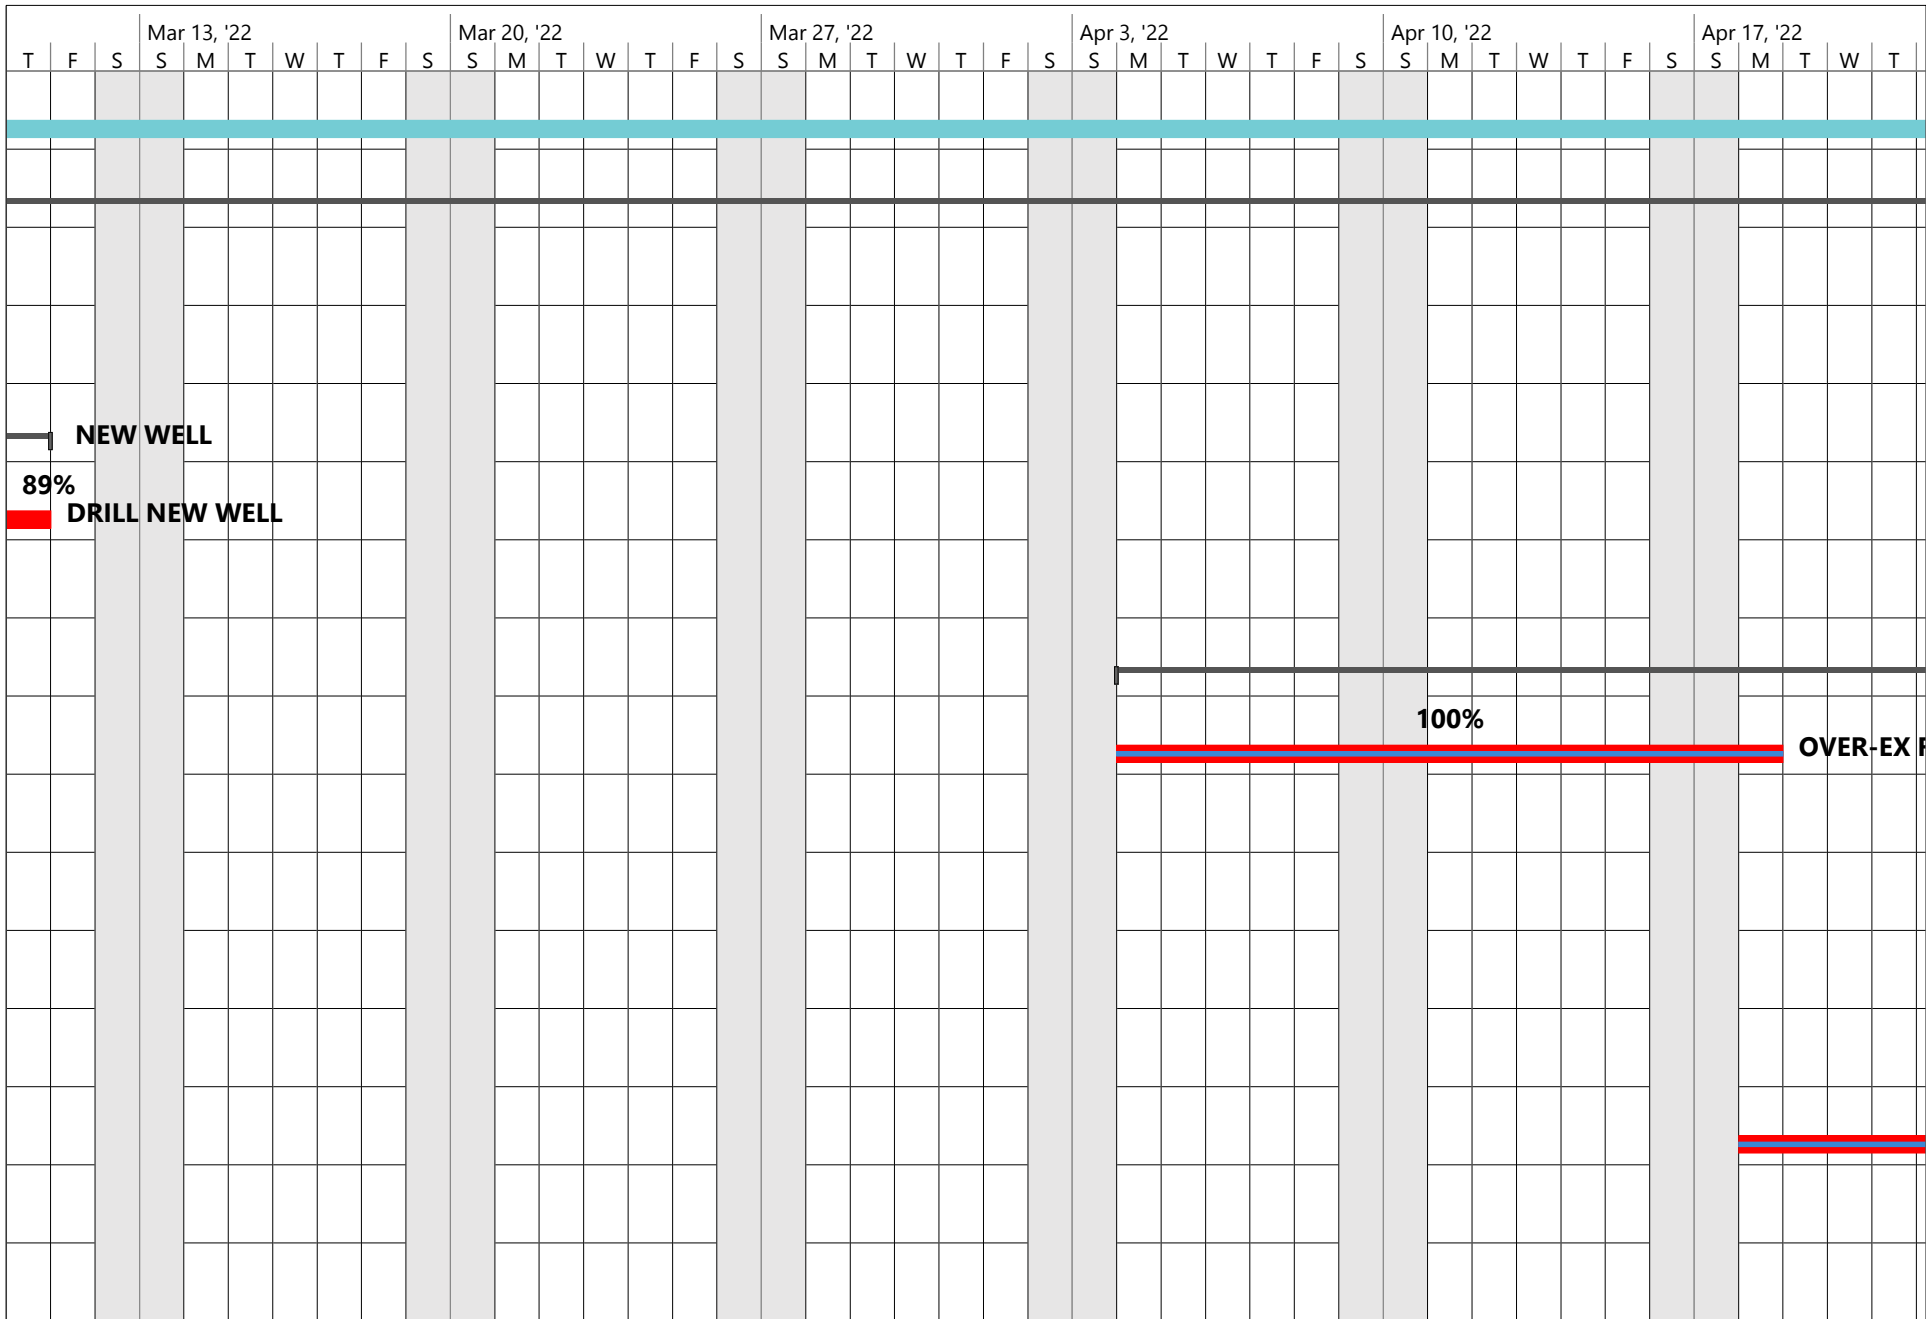


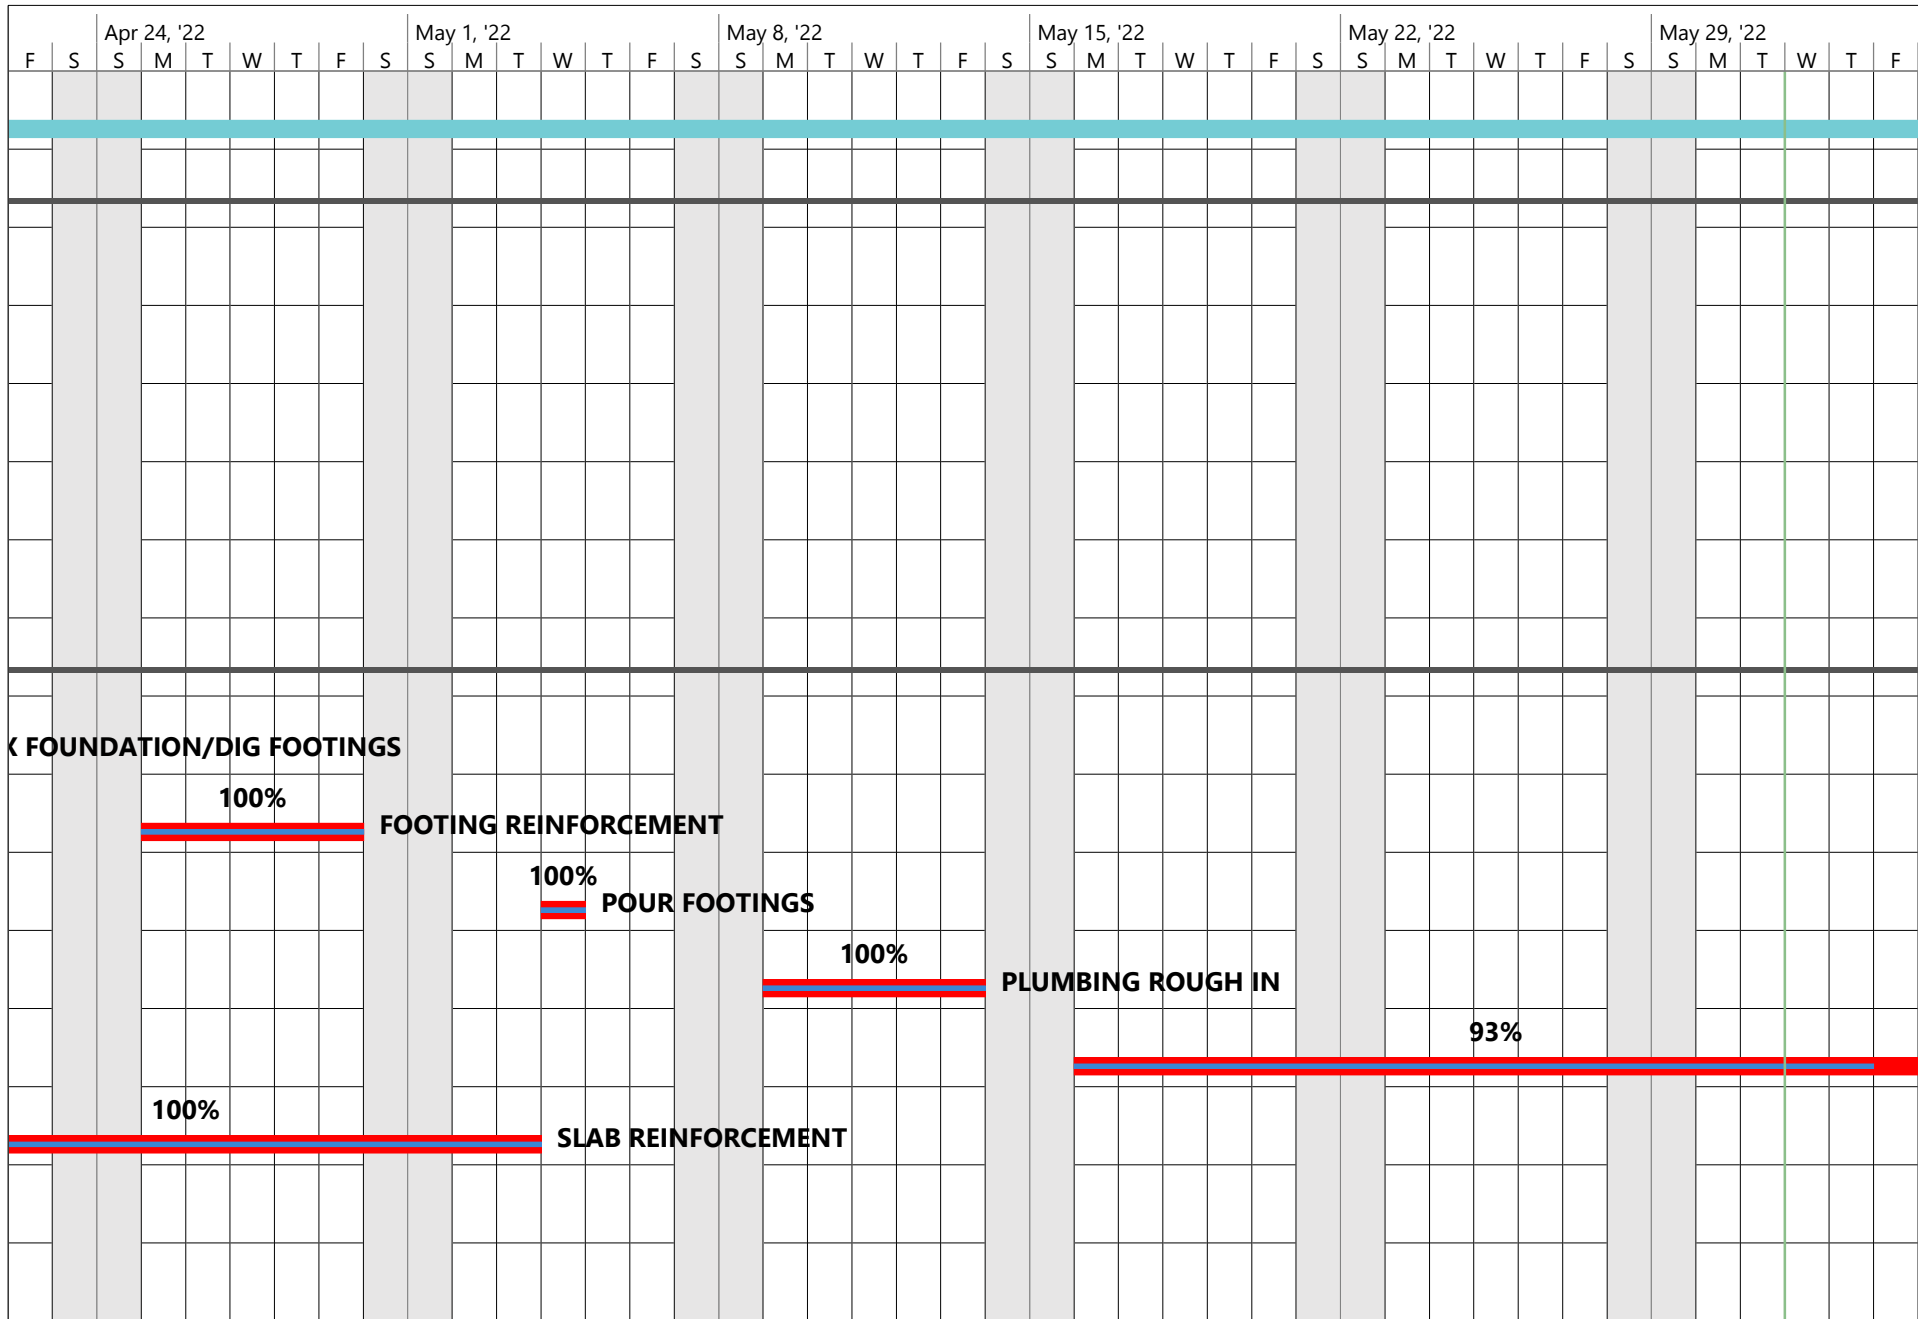


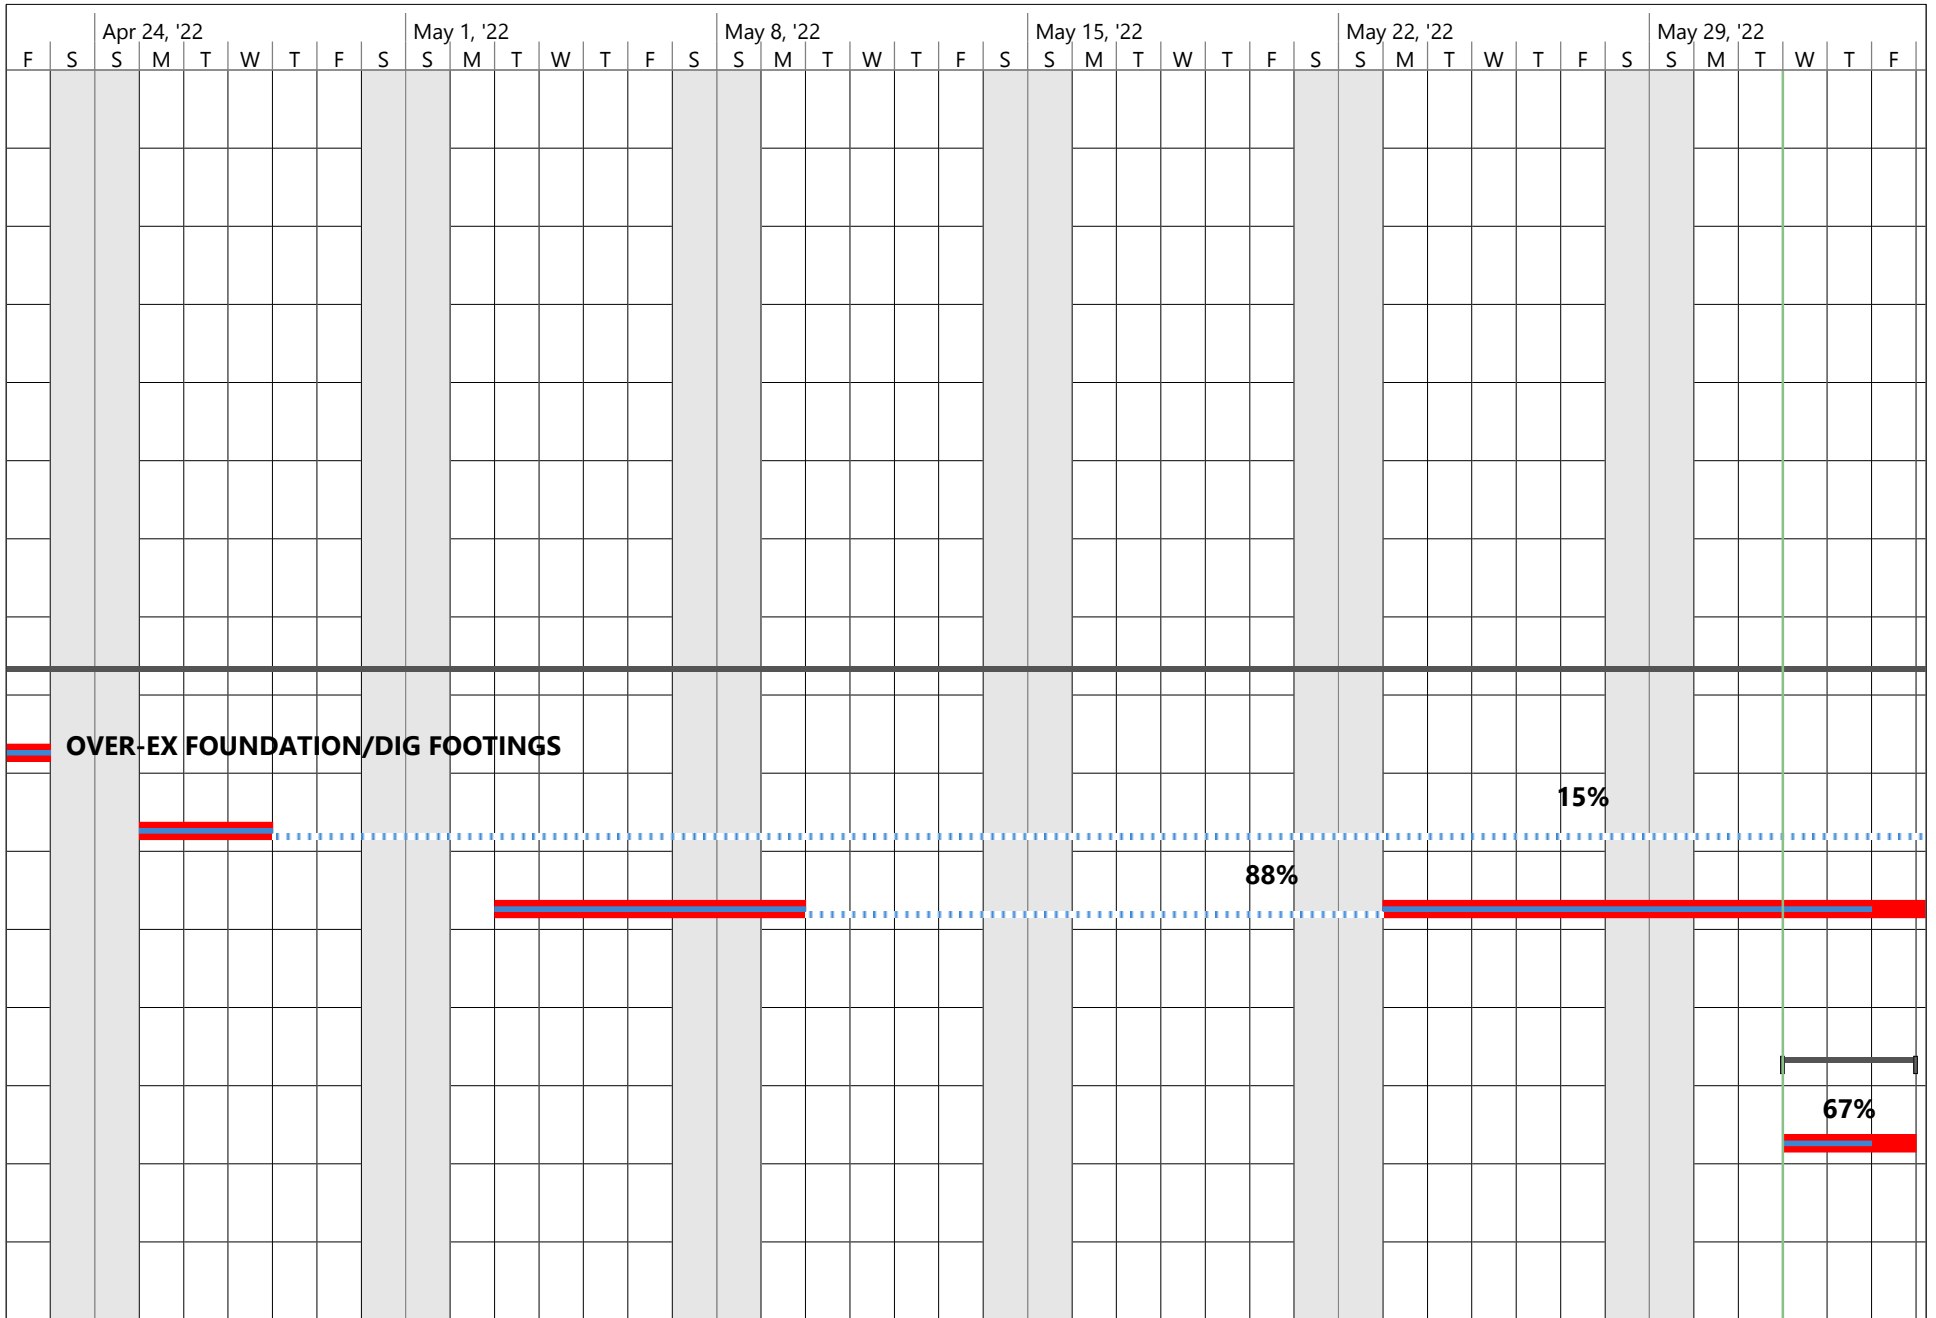



Apr 24, '22							May 1, '22							May 8, '22							May 15, '22							May 22, '22							May 29, '22						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F						

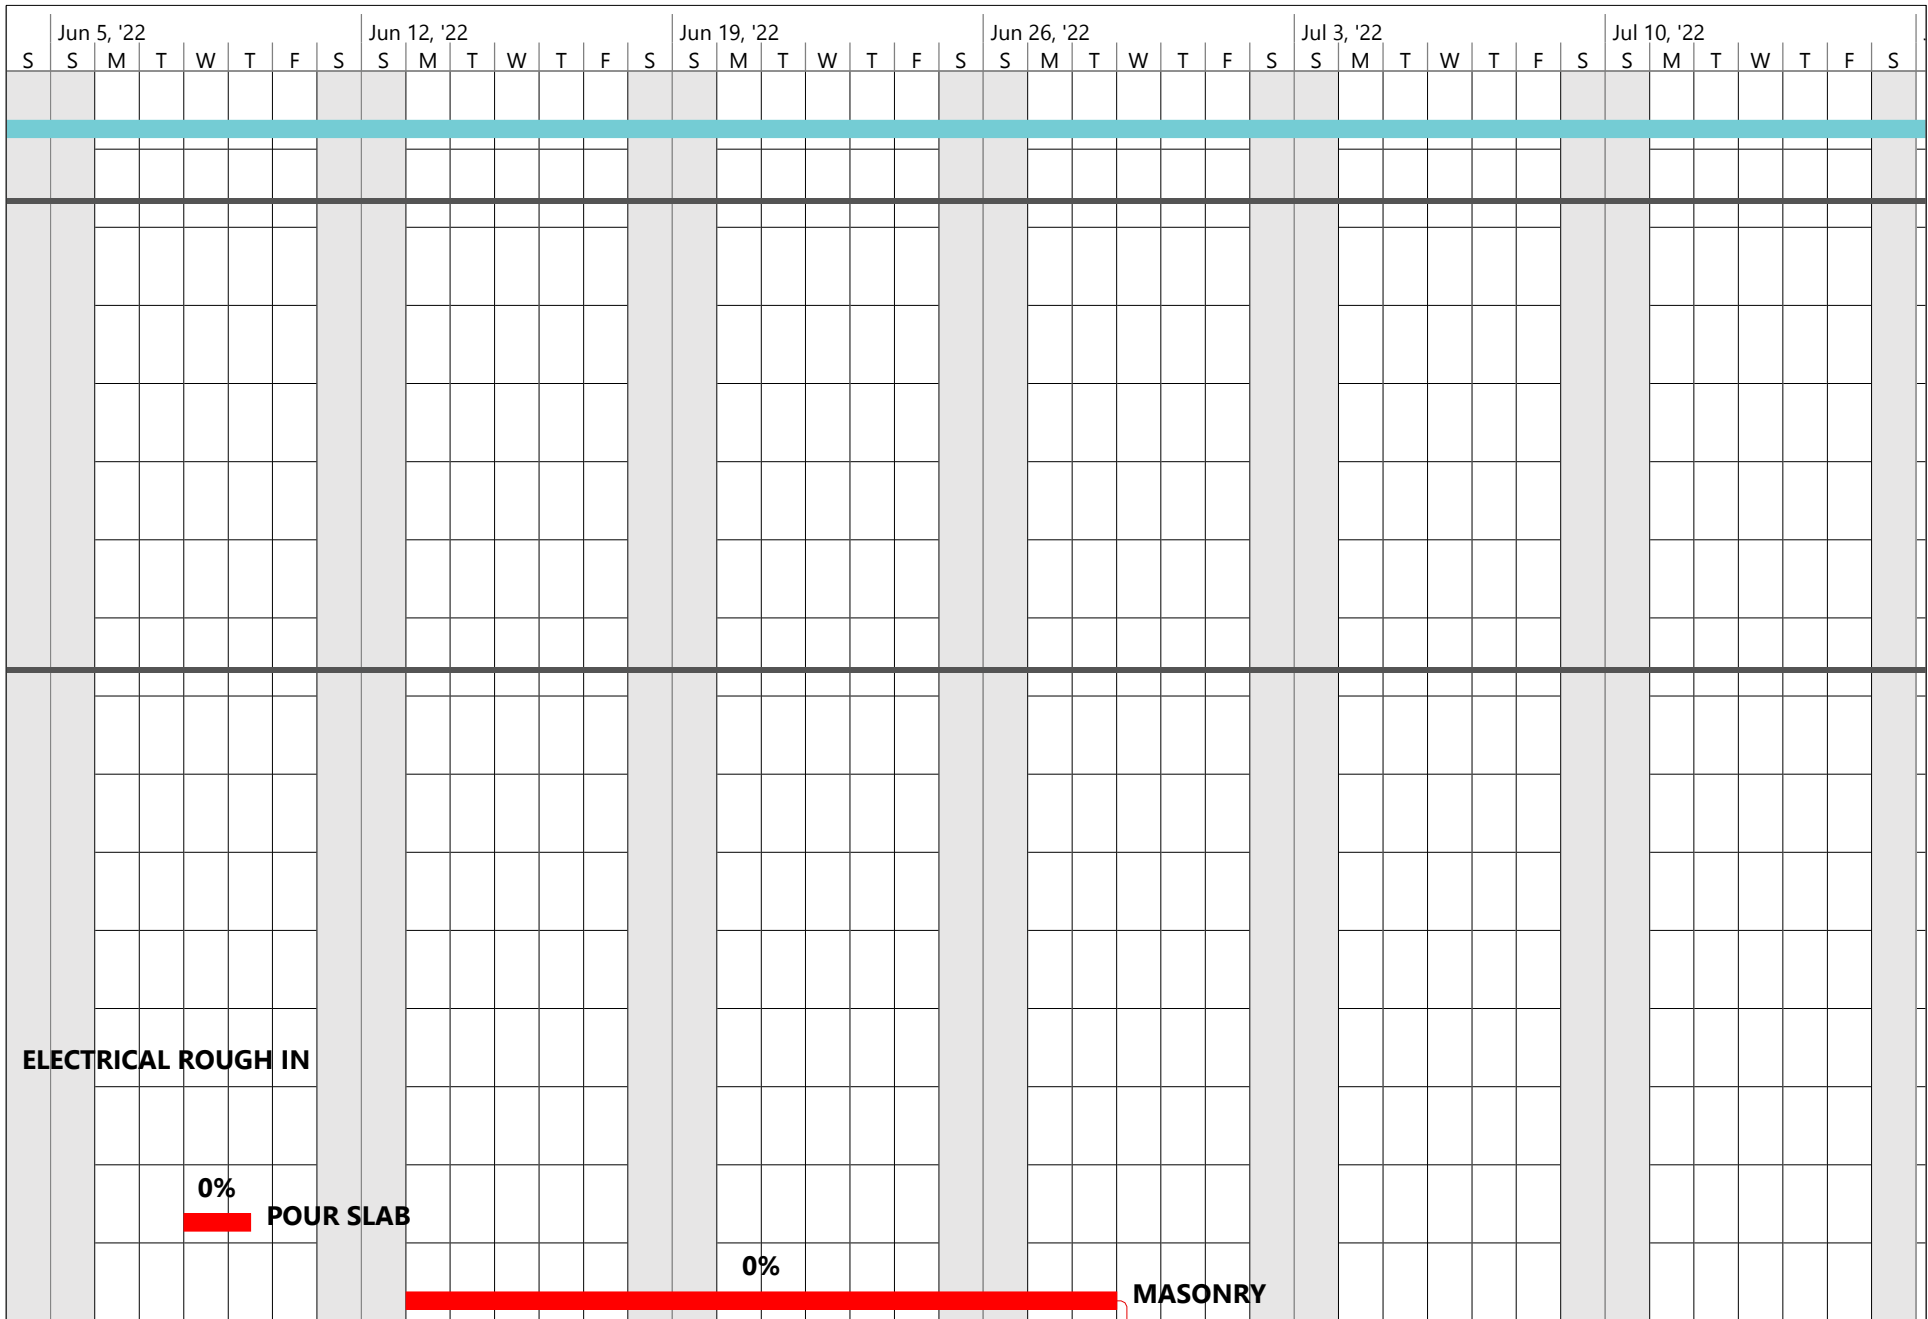

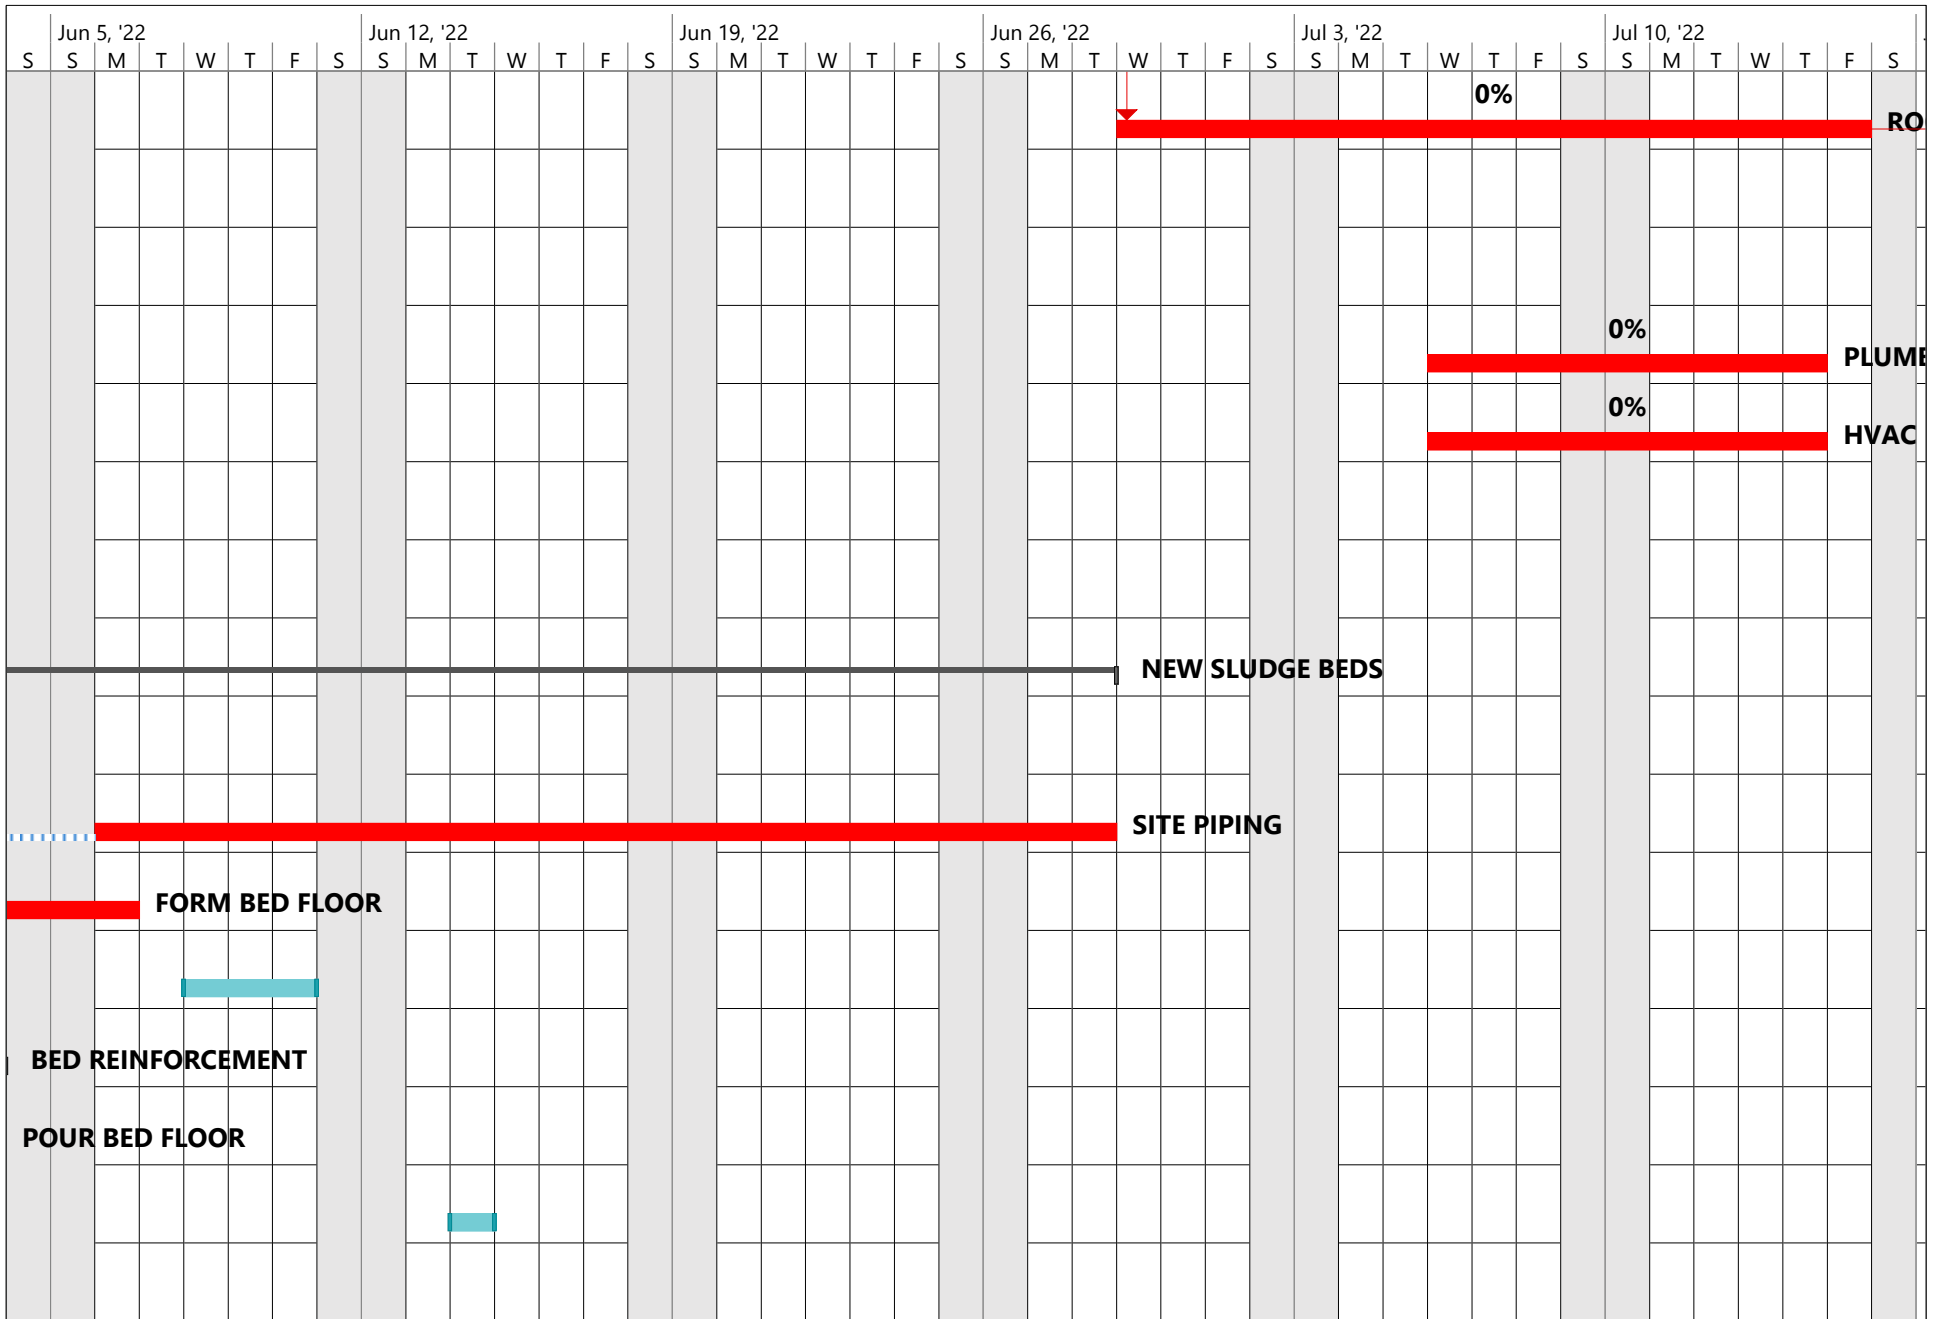

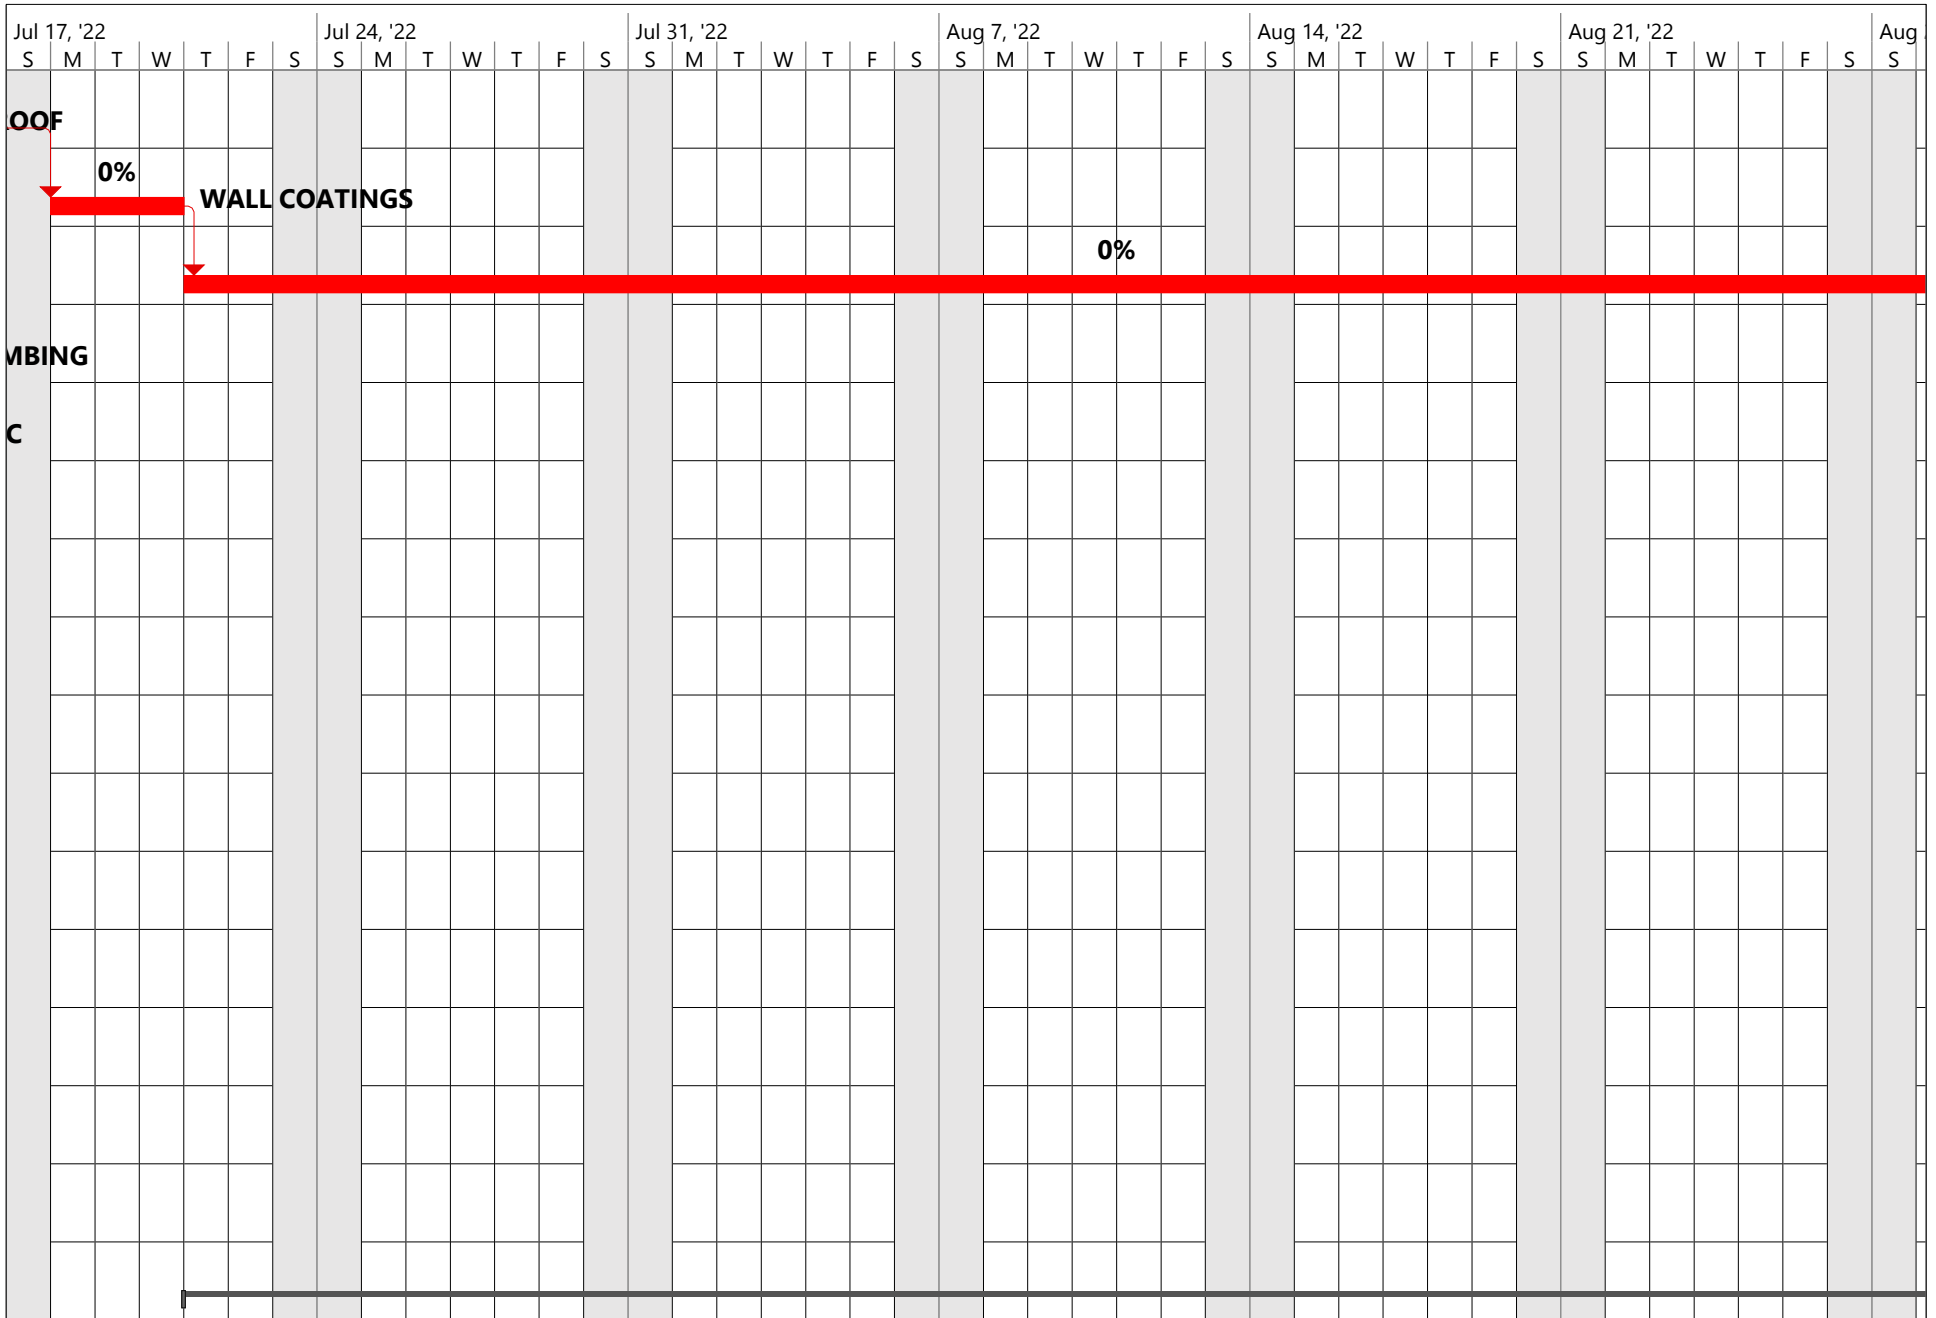

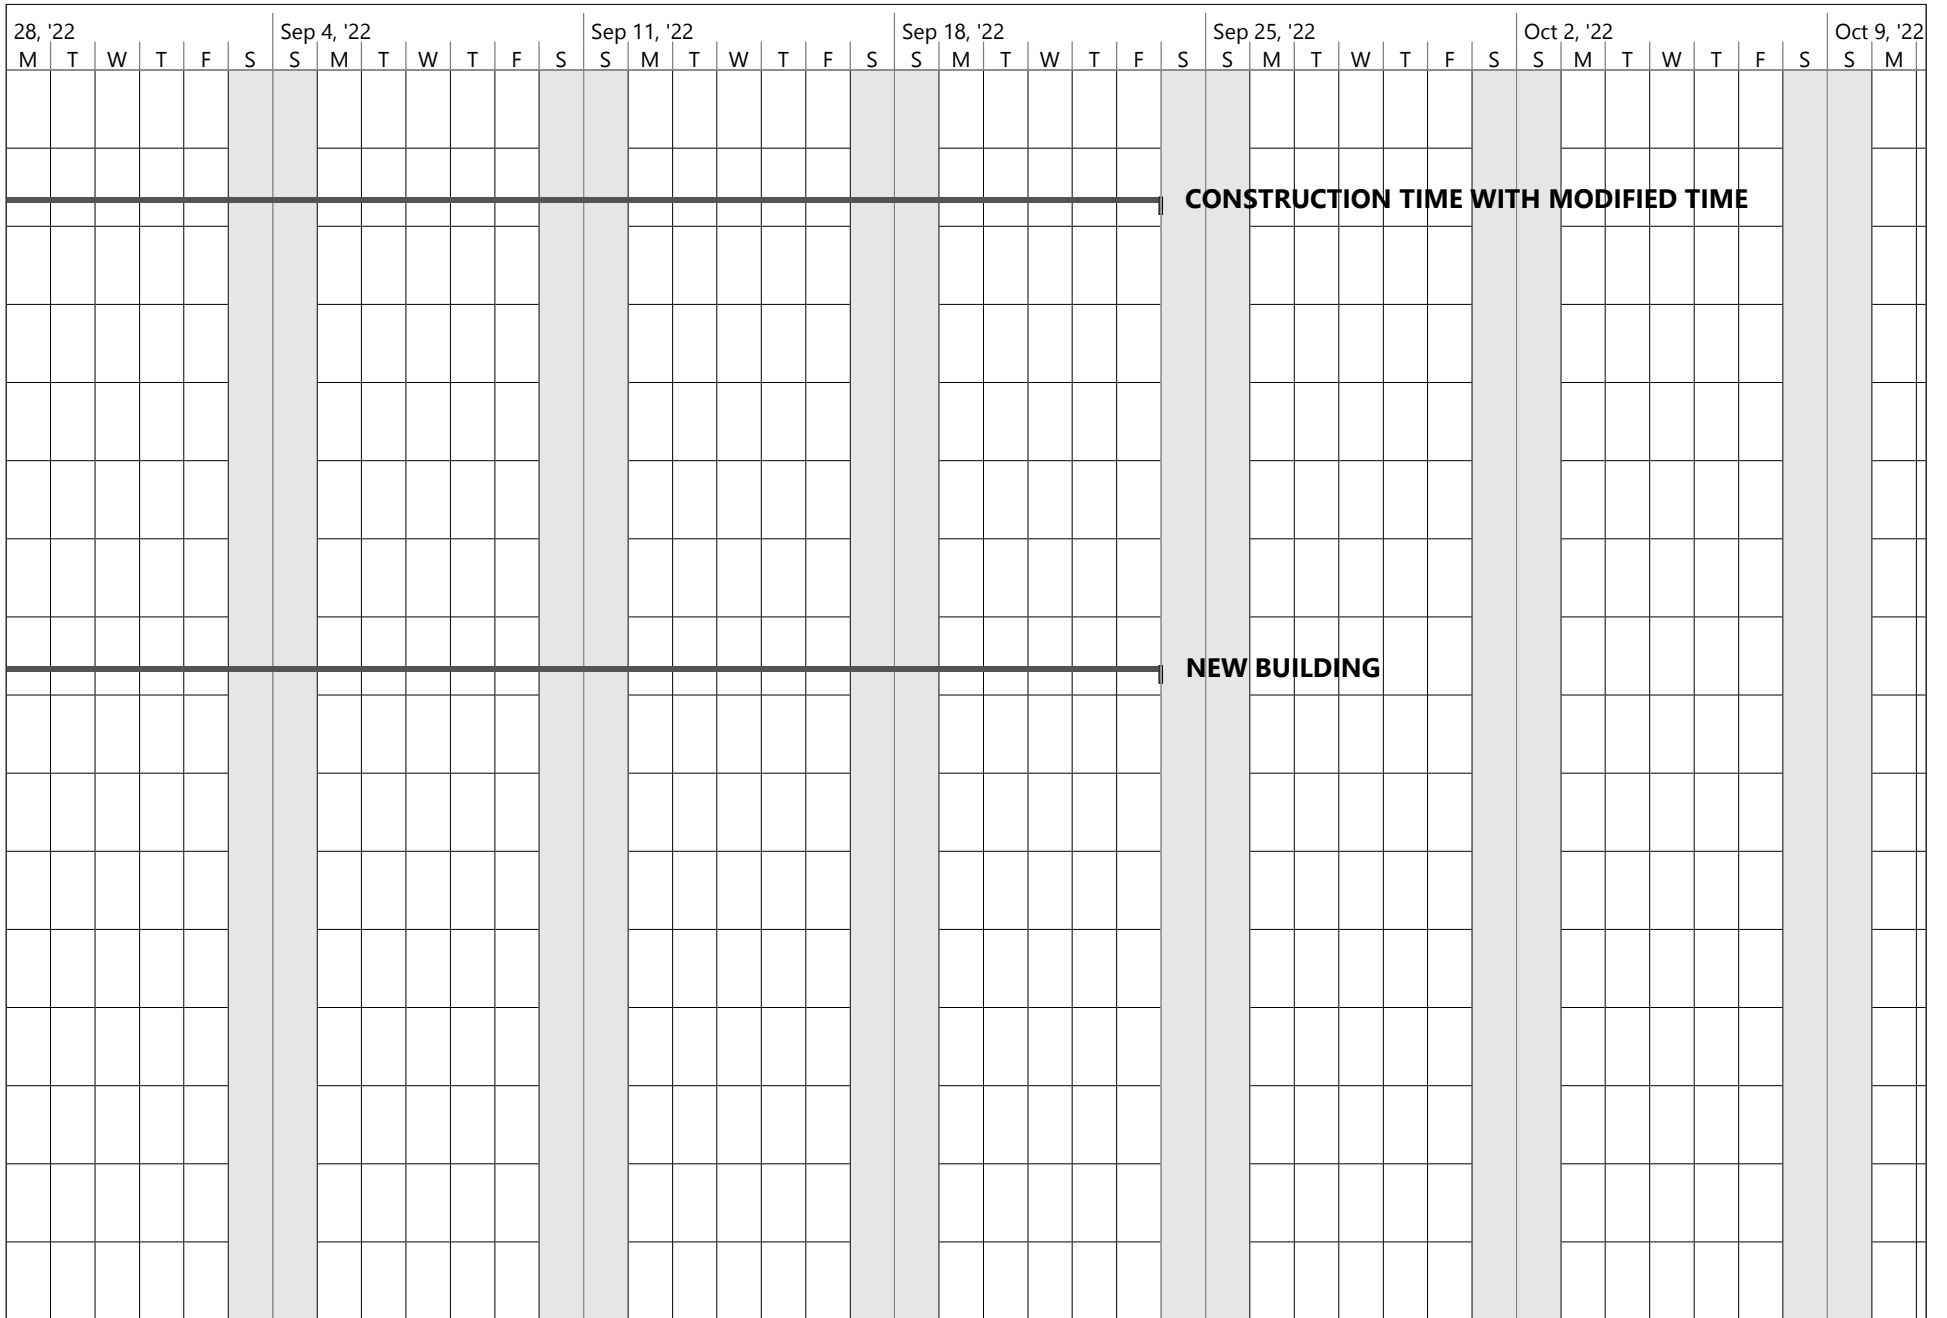

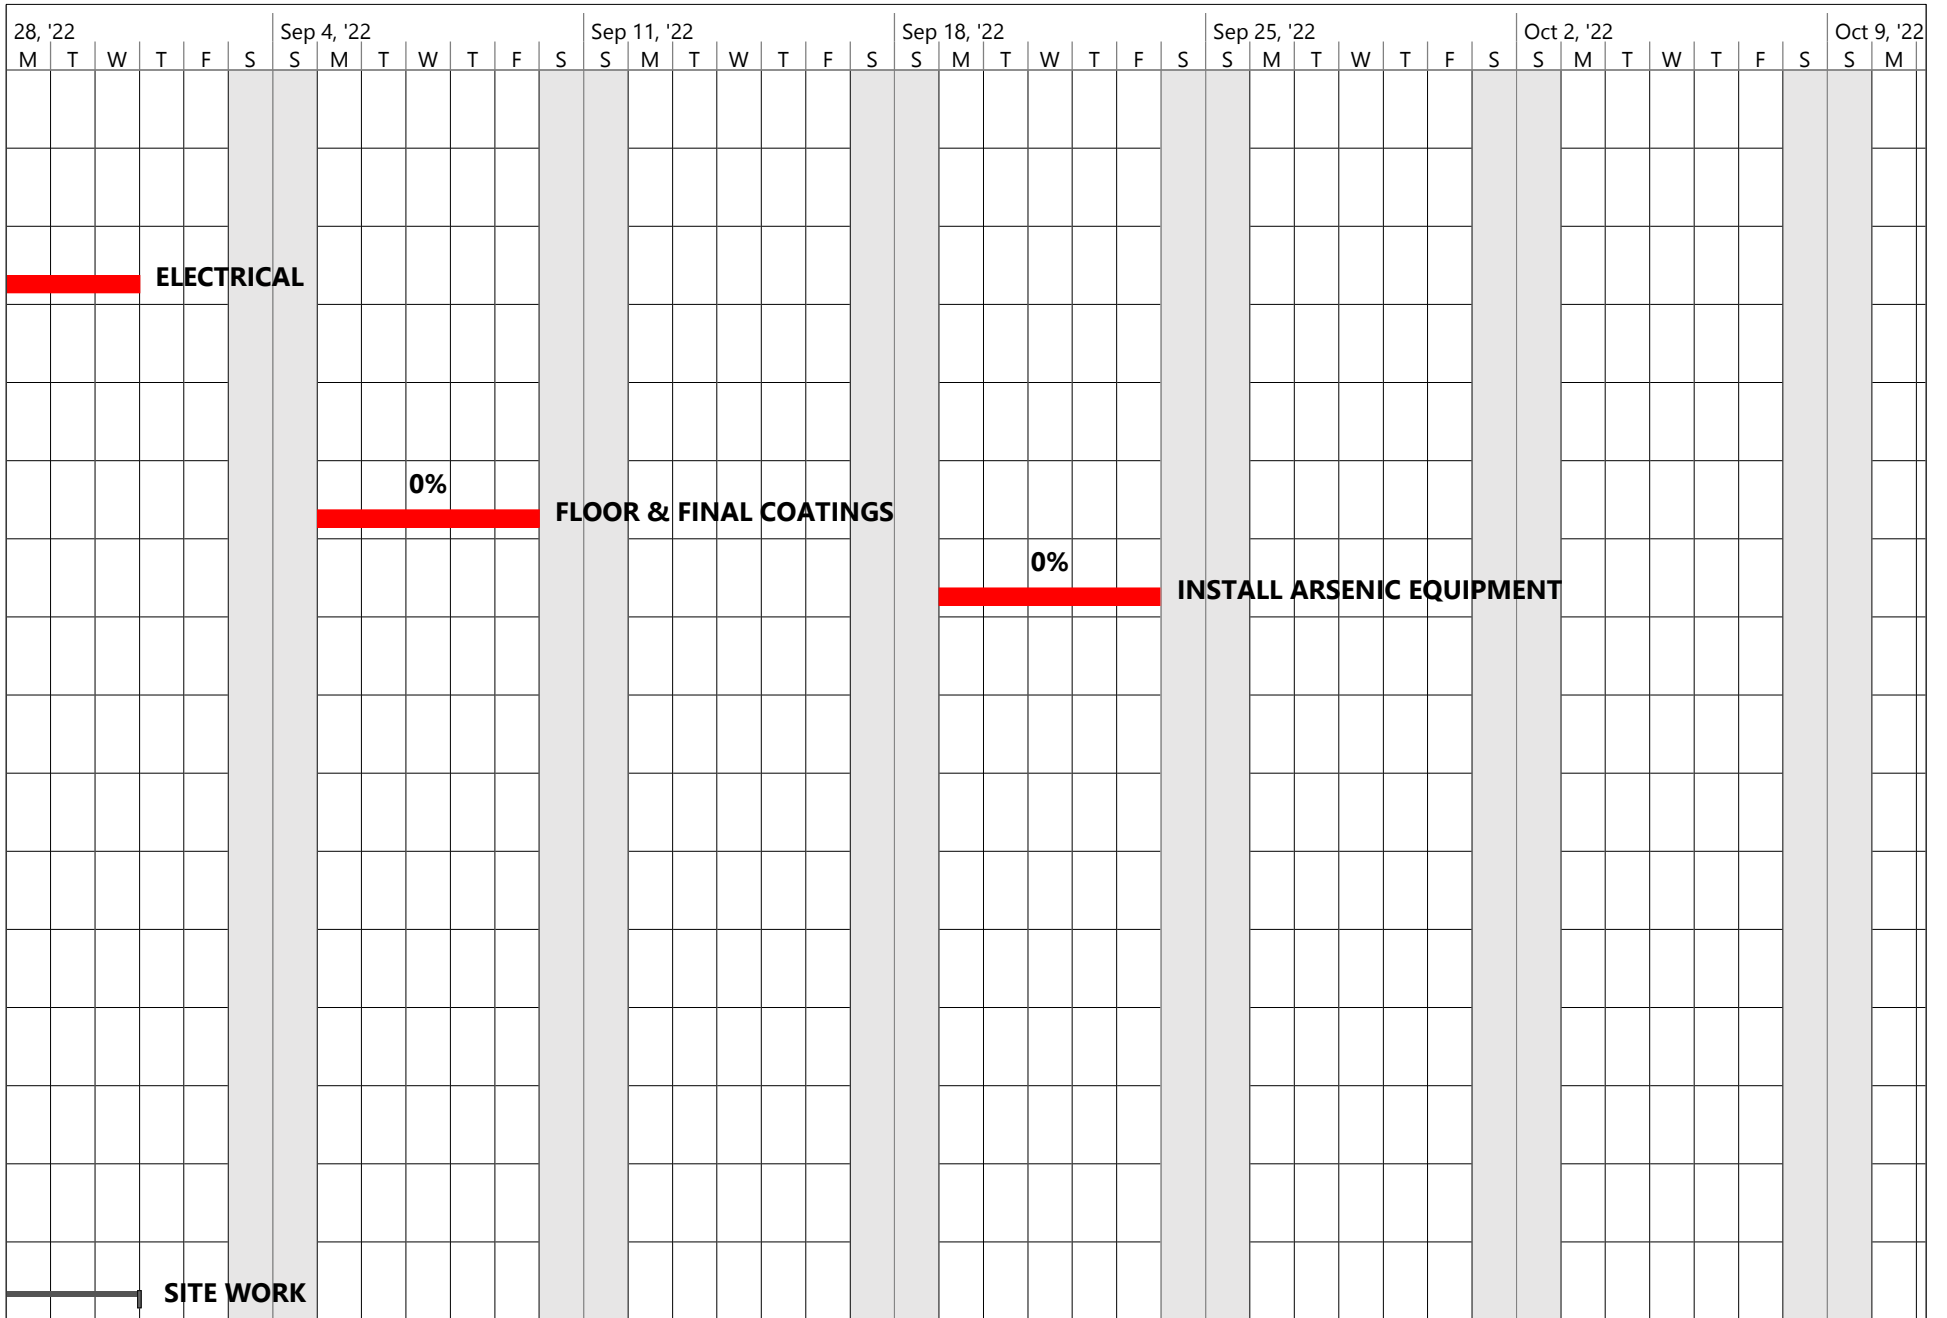

28, '22						Sep 4, '22						Sep 11, '22						Sep 18, '22						Sep 25, '22						Oct 2, '22						Oct 9, '22	
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M		
ONDS																																					
