

ID	% Compl		Task Mode	Task Name	Duration	Start	Finish	Predecessors
1	36%			<b>Mesquite-Brazito Wastewater System Imp - Project 2</b>	<b>226 days?</b>	<b>Wed 3/16/22</b>	<b>Wed 5/3/23</b>	
2	100%			NOA	0 days	Wed 3/16/22	Wed 3/16/22	
3	100%			NTP (tentative)	0 days	Mon 5/2/22	Mon 5/2/22	2FS+47 edays
4	58%			<b>Approvals</b>	<b>42 days?</b>	<b>Wed 3/16/22</b>	<b>Mon 5/30/22</b>	
5	66%			SWPPP (DAC Approval)	45 edays	Wed 3/16/22	Sat 4/30/22	2
6	50%			TCP (DAC Approval)	45 edays	Wed 3/16/22	Sat 4/30/22	2
7	30%			Roadway Survey (DAC Approval)	45 edays	Wed 3/16/22	Sat 4/30/22	2
8	0%			Building and Site Permits (DAC Approval)	30 edays	Sat 4/30/22	Mon 5/30/22	5
9	0%			Dewatering Permits (NM OSE /EBID Approval)	1 day?	Wed 3/16/22	Wed 3/16/22	
10	100%			Pipe	22 edays	Wed 3/16/22	Thu 4/7/22	2
11	100%			Pumps	22 edays	Wed 3/16/22	Thu 4/7/22	2
12	100%			Manholes	30 edays	Wed 3/16/22	Fri 4/15/22	2
13	58%			<b>Deliveries</b>	<b>67 days</b>	<b>Thu 4/7/22</b>	<b>Fri 8/5/22</b>	
14	100%			Pipe	25 edays	Thu 4/7/22	Mon 5/2/22	10
15	50%			Manholes	14 edays	Fri 4/15/22	Fri 4/29/22	12
16	50%			Pumps	120 edays	Thu 4/7/22	Fri 8/5/22	11
17	7%			<b>Base Bid - Lift Station 16</b>	<b>204 days</b>	<b>Mon 4/25/22</b>	<b>Wed 5/3/23</b>	
18	100%			<b>Mobilization</b>	<b>12 days</b>	<b>Mon 4/25/22</b>	<b>Mon 5/16/22</b>	
19	100%			Yard & Temporary Facilities	12 days	Mon 4/25/22	Mon 5/16/22	27SF
20	100%			Project Sign	1 day	Wed 4/27/22	Thu 4/28/22	21SF
21	100%			Construction Staking	8 days	Thu 4/28/22	Thu 5/12/22	22SF
22	100%			Proctor Native Material	1 day	Thu 5/12/22	Mon 5/16/22	24SF
23	100%			Pre-Construction Video	1 day	Thu 5/12/22	Mon 5/16/22	27SF

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

ID	% Compl		Task Mode	Task Name	Duration	Start	Finish	Predecessors
24	100%			SW3P BMP's In-Place	0 days	Mon 5/16/22	Mon 5/16/22	27SF
25	100%			Traffic Control In-Place	0 days	Mon 5/16/22	Mon 5/16/22	27SF
26	3%			<b>Lift Station 16</b>	<b>92 days</b>	<b>Mon 5/16/22</b>	<b>Wed 10/26/22</b>	
27	100%			Install Precast Wet Well	4 days	Mon 5/16/22	Thu 5/19/22	15
28	0%			Valve and Meter Vault	8 days	Mon 5/23/22	Mon 6/6/22	27
29	0%			Piping	12 days	Tue 6/7/22	Mon 6/27/22	28
30	0%			Pumps	4 days	Mon 8/8/22	Thu 8/11/22	16,29
31	0%			IBOX Odor Control Unit	4 days	Mon 8/15/22	Thu 8/18/22	30
32	0%			Building Underground	8 days	Tue 6/28/22	Tue 7/12/22	8,29
33	0%			Building Foundation	8 days	Wed 7/13/22	Tue 7/26/22	32
34	0%			CMU Walls	8 days	Wed 7/27/22	Tue 8/9/22	33
35	0%			Roof System	4 days	Wed 8/10/22	Tue 8/16/22	34
36	0%			Doors	4 days	Wed 8/17/22	Tue 8/23/22	35
37	0%			HVAC	4 days	Wed 8/24/22	Tue 8/30/22	36
38	0%			Mag/Hydroxide Odor Control System	4 days	Wed 8/31/22	Wed 9/7/22	37
39	0%			Electrical Service (EPEC)	0 days	Thu 9/8/22	Thu 9/8/22	40SF
40	0%			Electrical	24 days	Thu 9/8/22	Wed 10/19/22	38
41	0%			Painting	4 days	Thu 10/20/22	Wed 10/26/22	40
42	0%			Water service	4 days	Wed 8/17/22	Tue 8/23/22	35
43	0%			Site Fencing	32 days	Wed 8/24/22	Wed 10/19/22	42
44	0%			Site Gravel	4 days	Thu 10/20/22	Wed 10/26/22	43
45	11%			<b>Collection System</b>	<b>138 days</b>	<b>Mon 5/23/22</b>	<b>Mon 2/6/23</b>	
46	100%			<b>East Organ Alignment LS 16 - Sta 48+00 (1,000')</b>	<b>16 days</b>	<b>Mon 5/23/22</b>	<b>Mon 6/20/22</b>	

Project: msproj11  
Date: Thu 7/7/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Compl		Task Mode	Task Name	Duration	Start	Finish	Predecessors
47	100%			Mill Existing Asphalt	2 days	Mon 5/23/22	Tue 5/24/22	27
48	100%			Install 10" SAS and Manholes	10 days	Wed 5/25/22	Mon 6/13/22	47
49	100%			20" Bore Mesquite Drain Sta 48+62-49+97	4 days	Tue 6/14/22	Mon 6/20/22	48
50	80%			<b>BBQ/Picnic CT Alignment LS 16 - MH 049 (1405')</b>	<b>8 days</b>	<b>Tue 6/14/22</b>	<b>Mon 6/27/22</b>	
51	100%			Mill Existing Asphalt	2 days	Tue 6/14/22	Wed 6/15/22	48
52	75%			Install 8" SAS and Manholes	8 days	Tue 6/14/22	Mon 6/27/22	48
53	7%			<b>East Organ Alignment Sta 48+00 - 64+00 (1,600')</b>	<b>34 days</b>	<b>Thu 6/16/22</b>	<b>Tue 8/16/22</b>	
54	100%			Mill Existing Asphalt	2 days	Thu 6/16/22	Mon 6/20/22	51
55	0%			Install 10" SAS and Manholes	16 days	Tue 6/28/22	Tue 7/26/22	52
56	0%			Replace Asphalt Road	12 days	Wed 7/27/22	Tue 8/16/22	55
57	0%			<b>Valles/Relic Alignment LS 16 - MH 046 (1692')</b>	<b>16 days</b>	<b>Wed 7/27/22</b>	<b>Tue 8/23/22</b>	
58	0%			Mill Existing Asphalt	2 days	Wed 7/27/22	Thu 7/28/22	55
59	0%			Install 8" SAS and Manholes	8 days	Wed 7/27/22	Tue 8/9/22	55
60	0%			20" Bore Apache Lateral Sta 64+10-64+80	4 days	Wed 8/10/22	Tue 8/16/22	59
61	0%			Replace Asphalt Road	4 days	Wed 8/17/22	Tue 8/23/22	56
62	0%			<b>Primos CT/Relic CT Alignment LS 16 - MH 048 (1,296')</b>	<b>10 days</b>	<b>Wed 8/10/22</b>	<b>Thu 8/25/22</b>	
63	0%			Install 8" SAS and Manholes	6 days	Wed 8/10/22	Thu 8/18/22	59
64	0%			Replace Gravel Road	4 days	Mon 8/22/22	Thu 8/25/22	63
65	0%			<b>El Milagro rd. Alignment LS 16 - MH 040 (1242')</b>	<b>12 days</b>	<b>Mon 8/22/22</b>	<b>Mon 9/12/22</b>	
66	0%			Install 8" SAS and Manholes	8 days	Mon 8/22/22	Thu 9/1/22	63
67	0%			Replace Gravel Road	4 days	Tue 9/6/22	Mon 9/12/22	66
68	0%			<b>East Organ Alignment Sta 39+67 - 13+00 (2,700')</b>	<b>26 days</b>	<b>Wed 8/24/22</b>	<b>Mon 10/10/22</b>	
69	0%			Mill Existing Asphalt	4 days	Wed 8/24/22	Tue 8/30/22	61

Project: msproj11  
Date: Thu 7/7/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Compl	Task Mode	Task Name	Duration	Start	Finish	Predecessors
70	0%		Install 10" SAS and Manholes	16 days	Tue 9/6/22	Mon 10/3/22	66
71	0%		20" Bore Las Cruces Lateral Sta 11+94-12+74	4 days	Tue 10/4/22	Mon 10/10/22	70
72	0%		<b>Raging Bull Place Alignment LS 16 - MH 033 (1,150')</b>	<b>7 days</b>	<b>Tue 10/4/22</b>	<b>Thu 10/13/22</b>	
73	0%		Install 8" SAS and Manholes	5 days	Tue 10/4/22	Tue 10/11/22	70
74	0%		Replace Gravel Road	2 days	Wed 10/12/22	Thu 10/13/22	73
75	0%		<b>East Organ Sta 13+00/Calle Picasso Alignment (570')</b>	<b>19 days</b>	<b>Wed 10/12/22</b>	<b>Mon 11/14/22</b>	
76	0%		Install 10" SAS and Manholes	3 days	Wed 10/12/22	Mon 10/17/22	73
77	0%		Replace Asphalt Road	16 days	Tue 10/18/22	Mon 11/14/22	76
78	0%		<b>Guerrerro Alignment LS 16 - MH 025 (303')</b>	<b>3 days</b>	<b>Tue 10/18/22</b>	<b>Thu 10/20/22</b>	
79	0%		Install 8" SAS and Manholes	2 days	Tue 10/18/22	Wed 10/19/22	76
80	0%		Replace Gravel Road	1 day	Thu 10/20/22	Thu 10/20/22	79
81	0%		<b>Bar X Alignment LS 16 - MH 029 (1397')</b>	<b>24 days</b>	<b>Tue 10/18/22</b>	<b>Mon 12/5/22</b>	
82	0%		Mill Existing Asphalt	2 days	Tue 10/18/22	Thu 10/20/22	83SF
83	0%		Install 8" SAS and Manholes	8 days	Thu 10/20/22	Wed 11/2/22	79
84	0%		Replace Asphalt Road	8 days	Tue 11/15/22	Mon 12/5/22	77
85	0%		<b>4" C900 Force Main (3500')</b>	8 days	Wed 7/27/22	Tue 8/9/22	33
86	0%		<b>Private Services</b>	48 days	Thu 10/20/22	Wed 1/25/23	40
87	0%		<b>Septic Tank Abandonment</b>	24 days	Tue 12/20/22	Mon 2/6/23	86SS+30 days
88	7%		<b>ALT 3 - Lift Station 12</b>	<b>116 days</b>	<b>Wed 5/18/22</b>	<b>Mon 12/19/22</b>	
89	80%		<b>Mobilization</b>	<b>10 days</b>	<b>Wed 5/18/22</b>	<b>Tue 6/7/22</b>	
90	75%		Construction Staking	8 days	Wed 5/18/22	Thu 6/2/22	91SF
91	100%		Proctor Native Material	1 day	Thu 6/2/22	Mon 6/6/22	92SF
92	100%		Pre-Construction Video	1 day	Mon 6/6/22	Tue 6/7/22	93SF

Project: msproj11  
Date: Thu 7/7/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Compl		Task Mode	Task Name	Duration	Start	Finish	Predecessors
93	100%			SW3P BMP's In-Place	0 days	Tue 6/7/22	Tue 6/7/22	94SF
94	100%			Traffic Control In-Place	0 days	Tue 6/7/22	Tue 6/7/22	96SF
95	0%			<b>Lift Station 12</b>	<b>106 days</b>	<b>Tue 6/7/22</b>	<b>Mon 12/19/22</b>	
96	0%			Install Precast Wet Well	4 days	Tue 6/7/22	Mon 6/13/22	28
97	0%			Valve and Meter Vault	8 days	Tue 6/14/22	Mon 6/27/22	96
98	0%			Piping	12 days	Tue 6/28/22	Tue 7/19/22	97
99	0%			Pumps	4 days	Mon 8/8/22	Thu 8/11/22	98,16
100	0%			Electrical Service (EPEC)	0 days	Thu 8/11/22	Thu 8/11/22	99
101	0%			Electrical	24 days	Mon 8/15/22	Mon 9/26/22	100
102	0%			Painting	4 days	Tue 9/27/22	Mon 10/3/22	101
103	0%			Water service	4 days	Tue 10/4/22	Mon 10/10/22	102
104	0%			Site Chainlink Fencing	32 days	Tue 10/11/22	Mon 12/12/22	103
105	0%			Site Gravel	4 days	Tue 12/13/22	Mon 12/19/22	104
106	6%			<b>Collection System</b>	<b>81 days</b>	<b>Wed 6/8/22</b>	<b>Mon 10/31/22</b>	
107	0%			<b>HWY 478 Alignment LS 12 - MH 051 (1,600')</b>	<b>23 days</b>	<b>Wed 6/8/22</b>	<b>Tue 7/19/22</b>	
108	0%			Mill Existing Asphalt	3 days	Wed 6/8/22	Tue 6/14/22	109SF
109	0%			Install 10" SAS and Manholes	12 days	Tue 6/14/22	Tue 7/5/22	96
110	0%			Replace Asphalt Road	8 days	Wed 7/6/22	Tue 7/19/22	109
111	0%			<b>Memory Lane Alignment LS 12 - MH 61 (900')</b>	<b>6 days</b>	<b>Wed 7/6/22</b>	<b>Thu 7/14/22</b>	
112	0%			Install 8" SAS and Manholes	5 days	Wed 7/6/22	Wed 7/13/22	109
113	0%			Replace Gravel Road	1 day	Thu 7/14/22	Thu 7/14/22	112
114	0%			<b>Indian Lane Alignment LS 12 - MH 058 (850')</b>	<b>6 days</b>	<b>Thu 7/14/22</b>	<b>Mon 7/25/22</b>	
115	0%			Install 8" SAS and Manholes	5 days	Thu 7/14/22	Thu 7/21/22	112

Project: msproj11  
Date: Thu 7/7/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Compl	Task Mode	Task Name	Duration	Start	Finish	Predecessors
116	0%		Replace Gravel Road	1 day	Mon 7/25/22	Mon 7/25/22	115
117	40%		<b>Carnation CT Alignment LS 12 - MH 055 (1006')</b>	<b>10 days</b>	<b>Mon 7/25/22</b>	<b>Tue 8/9/22</b>	
118	50%		Install 8" SAS and Manholes	8 days	Mon 7/25/22	Thu 8/4/22	115
119	0%		Replace Gravel Road	2 days	Mon 8/8/22	Tue 8/9/22	118
120	0%		<b>Private Services</b>	16 days	Tue 9/27/22	Mon 10/24/22	101
121	0%		<b>Septic Tank Abandonment</b>	8 days	Tue 10/18/22	Mon 10/31/22	120SS+12 days
122	0%		<b>ALT 4 - Lift Station 11</b>	<b>174 days</b>	<b>Thu 6/16/22</b>	<b>Wed 5/3/23</b>	
123	0%		<b>Mobilization</b>	<b>10 days</b>	<b>Thu 6/16/22</b>	<b>Wed 7/6/22</b>	
124	0%		Construction Staking	8 days	Thu 6/16/22	Thu 6/30/22	125SF
125	0%		Proctor Native Material	1 day	Thu 6/30/22	Tue 7/5/22	126SF
126	0%		Pre-Construction Video	1 day	Tue 7/5/22	Wed 7/6/22	127SF
127	0%		SW3P BMP's In-Place	0 days	Wed 7/6/22	Wed 7/6/22	128SF
128	0%		Traffic Control In-Place	0 days	Wed 7/6/22	Wed 7/6/22	130SF
129	0%		<b>Lift Station 11</b>	<b>144 days</b>	<b>Wed 7/6/22</b>	<b>Wed 3/29/23</b>	
130	0%		Dewatering System In Place	8 days	Wed 7/6/22	Wed 7/20/22	131SF
131	0%		Install Precast Wet Well	4 days	Wed 7/20/22	Tue 7/26/22	98
132	0%		Valve and Meter Vault	8 days	Wed 7/27/22	Tue 8/9/22	131
133	0%		Piping	12 days	Wed 8/10/22	Tue 8/30/22	132
134	0%		Pumps	4 days	Wed 8/31/22	Wed 9/7/22	133
135	0%		Building Underground	8 days	Thu 9/8/22	Wed 9/21/22	134
136	0%		Building Foundation	8 days	Thu 9/22/22	Wed 10/5/22	135
137	0%		CMU Walls	8 days	Thu 10/6/22	Wed 10/19/22	136
138	0%		Roof System	4 days	Thu 10/20/22	Wed 10/26/22	137

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

ID	% Compl	Task Mode	Task Name	Duration	Start	Finish	Predecessors
139	0%		Doors	4 days	Thu 10/27/22	Wed 11/2/22	138
140	0%		HVAC	4 days	Thu 11/3/22	Wed 11/9/22	139
141	0%		Mag/Hydroxide Odor Control System	4 days	Thu 11/10/22	Wed 11/16/22	140
142	0%		Electrical Service (EPEC)	0 days	Wed 11/16/22	Wed 11/16/22	141
143	0%		Electrical	24 days	Thu 11/17/22	Wed 1/11/23	142
144	0%		Painting	4 days	Thu 1/12/23	Wed 1/18/23	143
145	0%		Water service	4 days	Thu 1/19/23	Wed 1/25/23	144
146	0%		Site Chainlink Fence	32 days	Thu 1/26/23	Wed 3/22/23	145
147	0%		Site Gravel	4 days	Thu 3/23/23	Wed 3/29/23	146
148	<b>0%</b>		<b>Collection System</b>	<b>63 days</b>	<b>Mon 8/22/22</b>	<b>Thu 12/15/22</b>	
149	<b>0%</b>		<b>Minter Rd Alignment LS 11 - MH 07 (2,380')</b>	<b>34 days</b>	<b>Mon 8/22/22</b>	<b>Wed 10/19/22</b>	
150	0%		Mill Existing Asphalt	6 days	Mon 8/22/22	Wed 8/31/22	151SF
151	0%		Install 8" SAS and Manholes	16 days	Wed 8/31/22	Wed 9/28/22	133
152	0%		Replace Asphalt Road	12 days	Thu 9/29/22	Wed 10/19/22	151
153	<b>0%</b>		<b>Contreras Alignment LS 11 - MH 035 (1,018')</b>	<b>8 days</b>	<b>Thu 9/29/22</b>	<b>Wed 10/12/22</b>	
154	0%		Install 8" SAS and Manholes	6 days	Thu 9/29/22	Mon 10/10/22	151
155	0%		Replace Gravel Road	2 days	Tue 10/11/22	Wed 10/12/22	154
156	<b>0%</b>		<b>Peppermint PL Alignment LS 11 - MH 41 (596')</b>	<b>5 days</b>	<b>Tue 10/11/22</b>	<b>Tue 10/18/22</b>	
157	0%		Install 8" SAS and Manholes	4 days	Tue 10/11/22	Mon 10/17/22	154
158	0%		Replace Gravel Road	1 day	Tue 10/18/22	Tue 10/18/22	157
159	<b>0%</b>		<b>Tarin/Segovia Lane Alignment LS 11 - MH 045 (1,473')</b>	<b>11 days</b>	<b>Tue 10/18/22</b>	<b>Thu 11/3/22</b>	
160	0%		Install 8" SAS and Manholes	8 days	Tue 10/18/22	Mon 10/31/22	157
161	0%		Replace Gravel Road	3 days	Tue 11/1/22	Thu 11/3/22	160

Project: msproj11  
Date: Thu 7/7/22




Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	






















ID	% Compl	Task Mode	Task Name	Duration	Start	Finish	Predecessors
162	0%		<b>Sanchez/Jarmon Rd Alignment LS 11 - MH 1 (1,975')</b>	<b>16 days</b>	<b>Tue 11/1/22</b>	<b>Mon 12/5/22</b>	
163	0%		Install 8" SAS and Manholes	12 days	Tue 11/1/22	Mon 11/28/22	160
164	0%		Replace Gravel Road	4 days	Tue 11/29/22	Mon 12/5/22	163
165	0%		<b>Hatheway Ln Alignment LS 11 - MH 013 (500')</b>	<b>4 days</b>	<b>Tue 11/29/22</b>	<b>Mon 12/5/22</b>	
166	0%		Install 8" SAS and Manholes	3 days	Tue 11/29/22	Thu 12/1/22	163
167	0%		Replace Gravel Road	1 day	Mon 12/5/22	Mon 12/5/22	166
168	0%		<b>Brenna Rd Alignment LS 11 - MH 15 (369')</b>	<b>3 days</b>	<b>Mon 12/5/22</b>	<b>Wed 12/7/22</b>	
169	0%		Install 8" SAS and Manholes	2 days	Mon 12/5/22	Tue 12/6/22	166
170	0%		Replace Gravel Road	1 day	Wed 12/7/22	Wed 12/7/22	169
171	0%		<b>Wanabe Rd Alignment LS 11 - MH 019 (740')</b>	<b>4 days</b>	<b>Wed 12/7/22</b>	<b>Tue 12/13/22</b>	
172	0%		Install 8" SAS and Manholes	3 days	Wed 12/7/22	Mon 12/12/22	169
173	0%		Replace Gravel Road	1 day	Tue 12/13/22	Tue 12/13/22	172
174	0%		<b>Munoz Alignment LS 11 - MH 9 (356')</b>	<b>3 days</b>	<b>Tue 12/13/22</b>	<b>Thu 12/15/22</b>	
175	0%		Install 8" SAS and Manholes	2 days	Tue 12/13/22	Wed 12/14/22	172
176	0%		Replace Gravel Road	1 day	Thu 12/15/22	Thu 12/15/22	175
177	0%		<b>Lift Station No. 4 Forcemain Alignment (5,100')</b>	<b>28 days</b>	<b>Thu 12/15/22</b>	<b>Wed 2/8/23</b>	
178	0%		12" Bore HWY 192 44+33-44+93	4 days	Thu 12/15/22	Wed 12/21/22	175
179	0%		12" Bore Del Rio Drain 43+20-43+90	4 days	Thu 12/22/22	Wed 1/4/23	178
180	0%		Install 4" SAS Ductile Iron (3,400')	10 days	Thu 1/5/23	Mon 1/23/23	179
181	0%		Install 4" SAS C900 (1,700')	5 days	Tue 1/24/23	Tue 1/31/23	180
182	0%		Air Release Valve Vault	1 day	Wed 2/1/23	Wed 2/1/23	181
183	0%		Install 6" SAS Ductile Iron Forcemain (620')	3 days	Thu 2/2/23	Tue 2/7/23	182
184	0%		Install 6" SAS C900 (120')	1 day	Wed 2/8/23	Wed 2/8/23	183


Project: msproj11  
Date: Thu 7/7/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	




ID	% Compl	Task Mode	Task Name	Duration	Start	Finish	Predecessors
185	0%		<b>Private Services</b>	48 days	Thu 2/9/23	Wed 5/3/23	184
186	0%		<b>Septic Tank Abandonment</b>	24 days	Thu 3/23/23	Wed 5/3/23	185SS+24 days
187	0%		Substantial Completion (450 Calendar Days)	0 days	Wed 5/3/23	Wed 5/3/23	186


Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

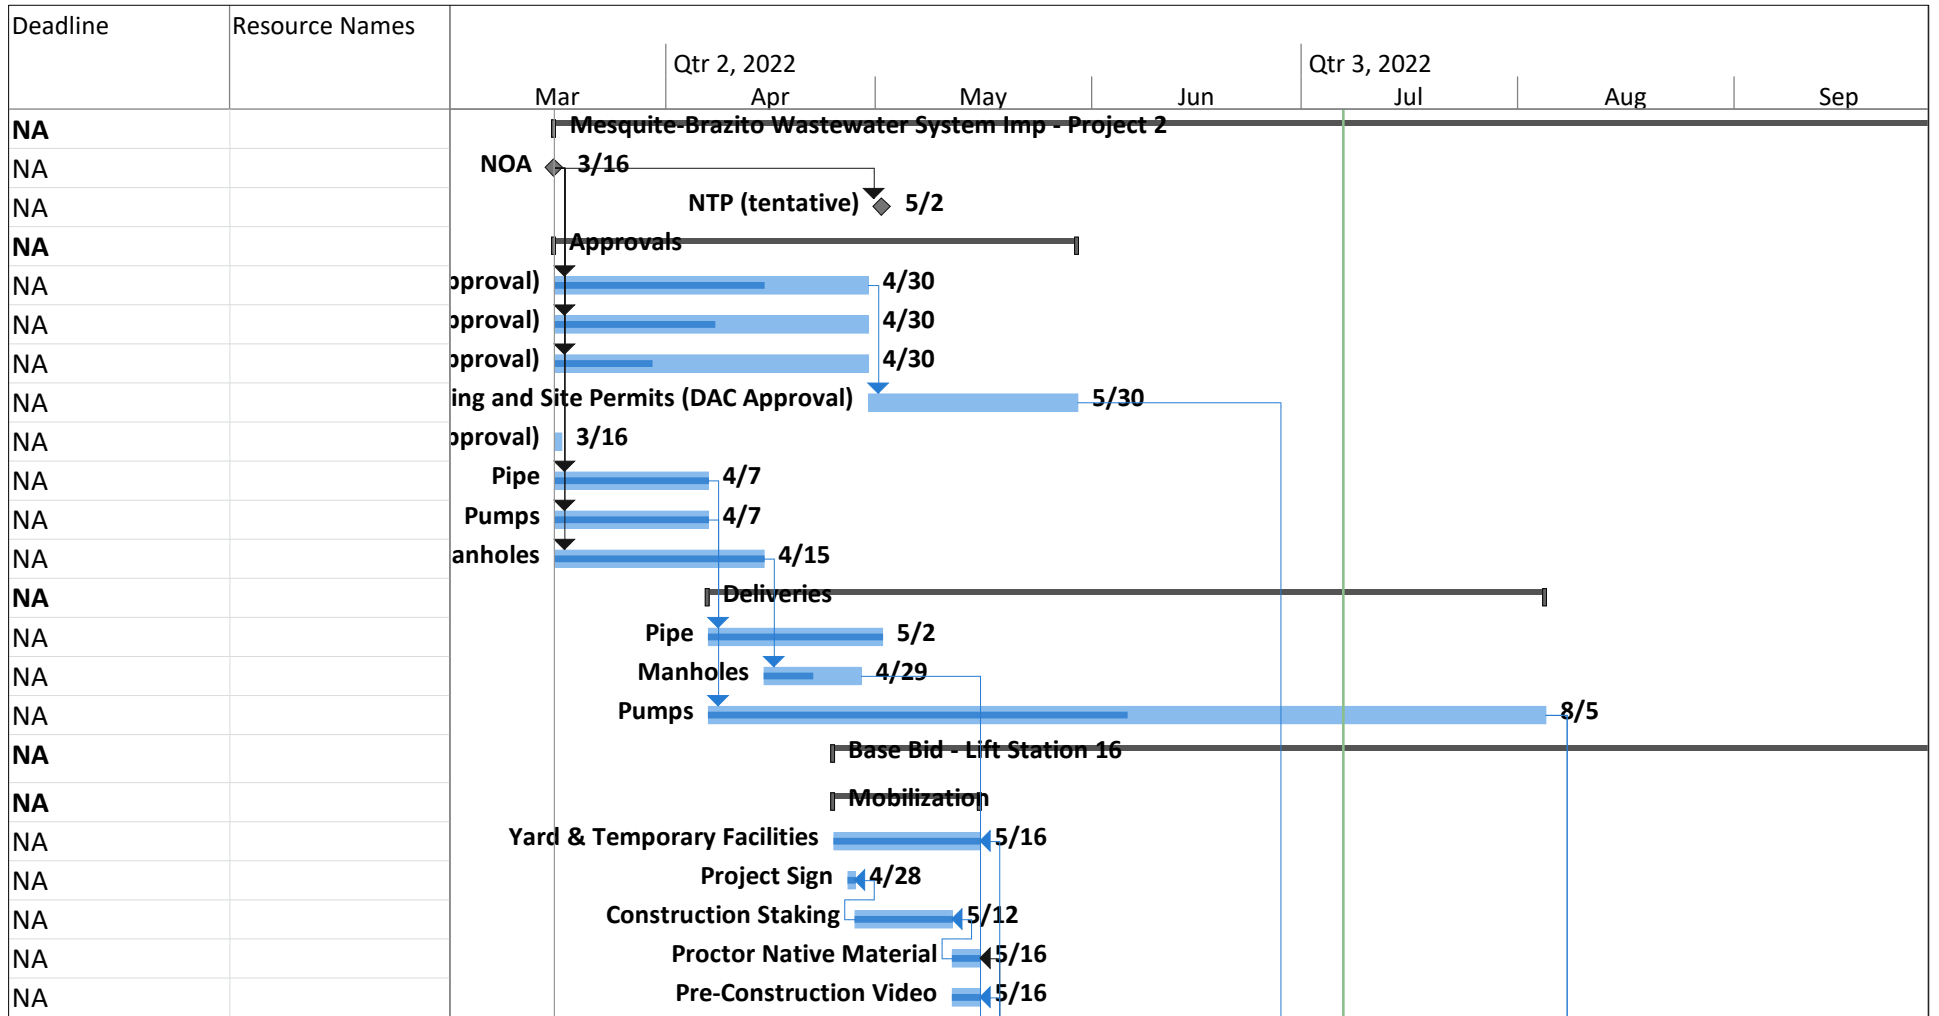


Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

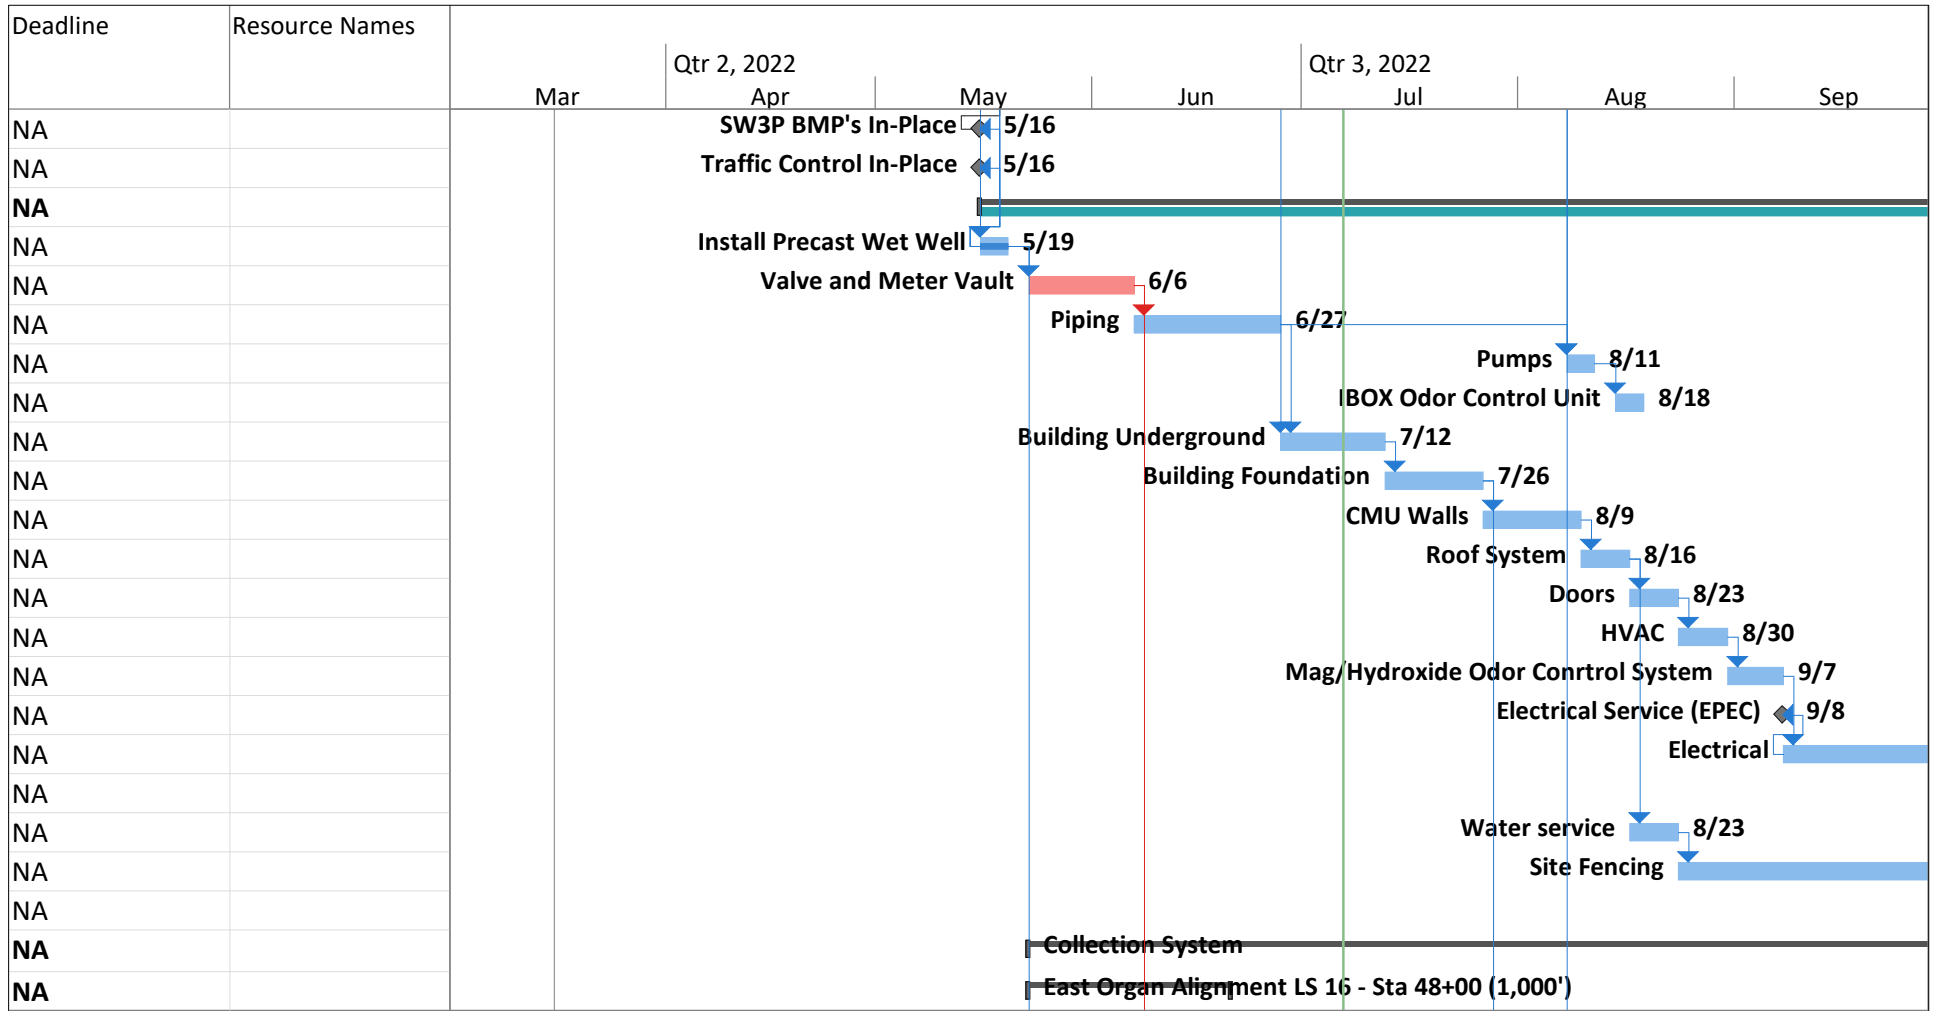


Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

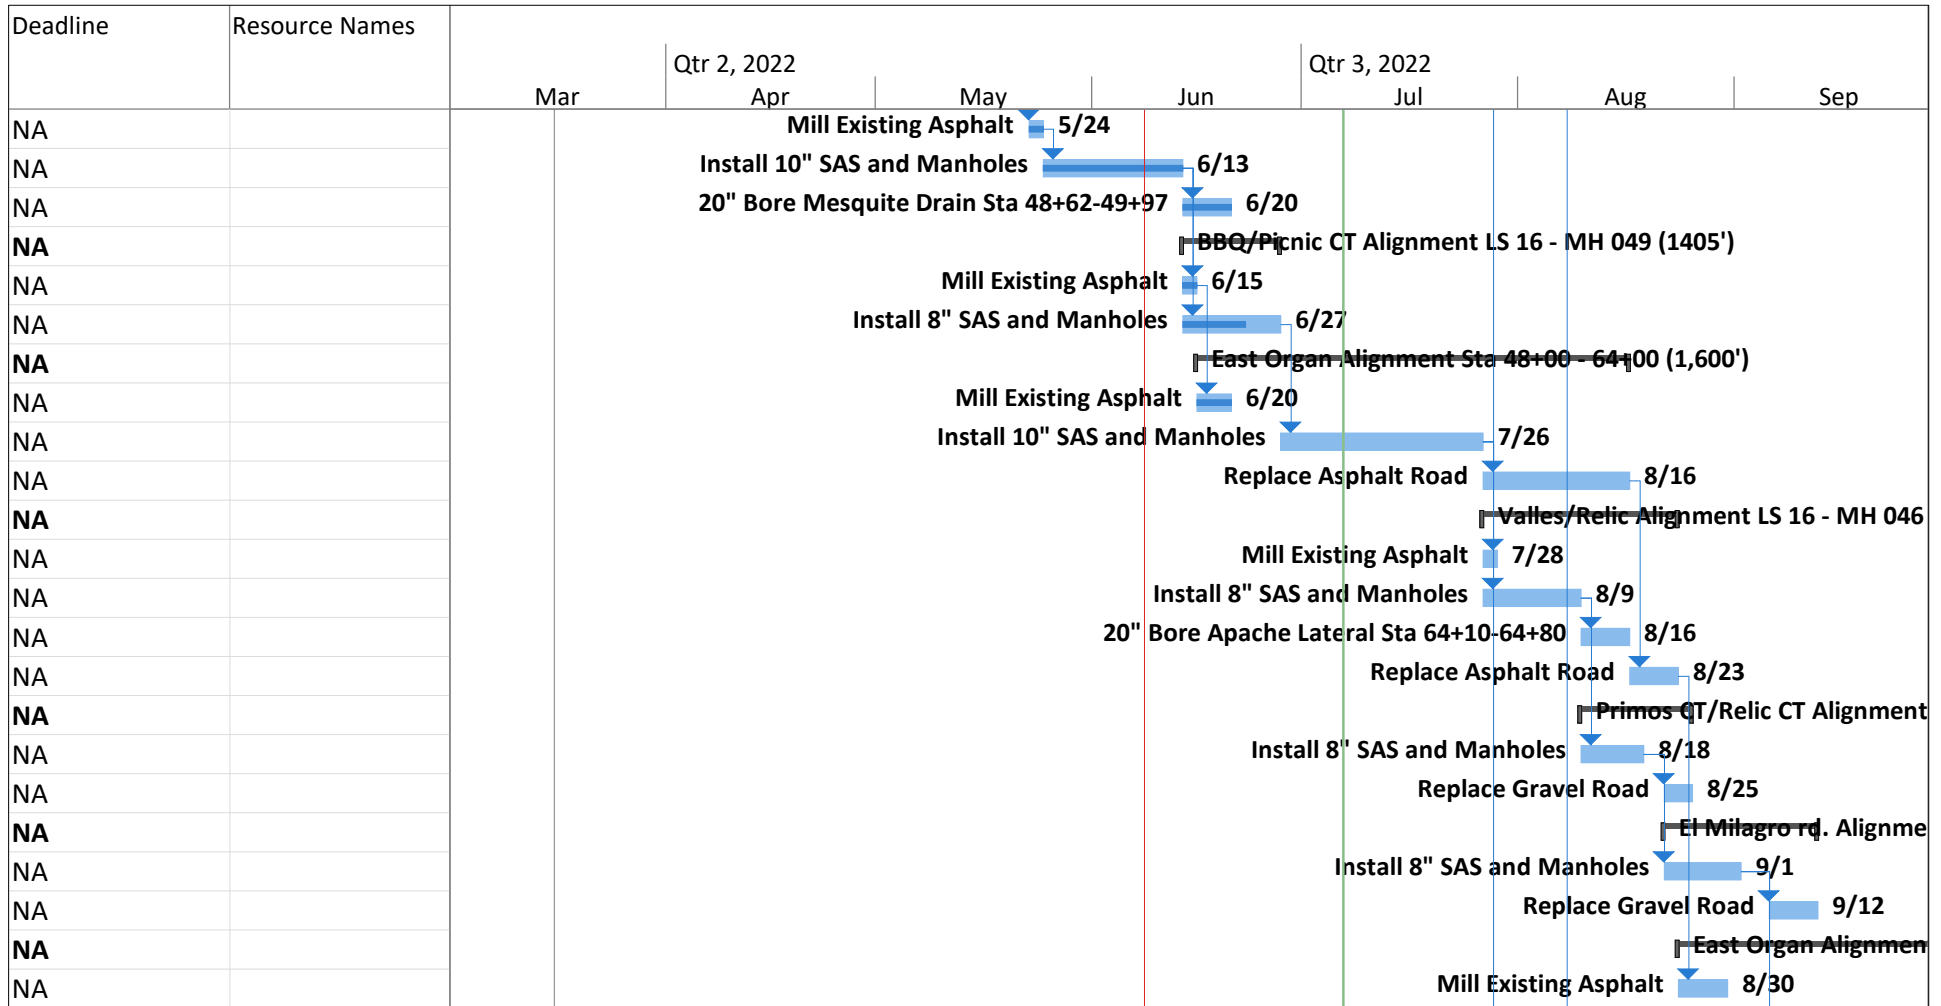


Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

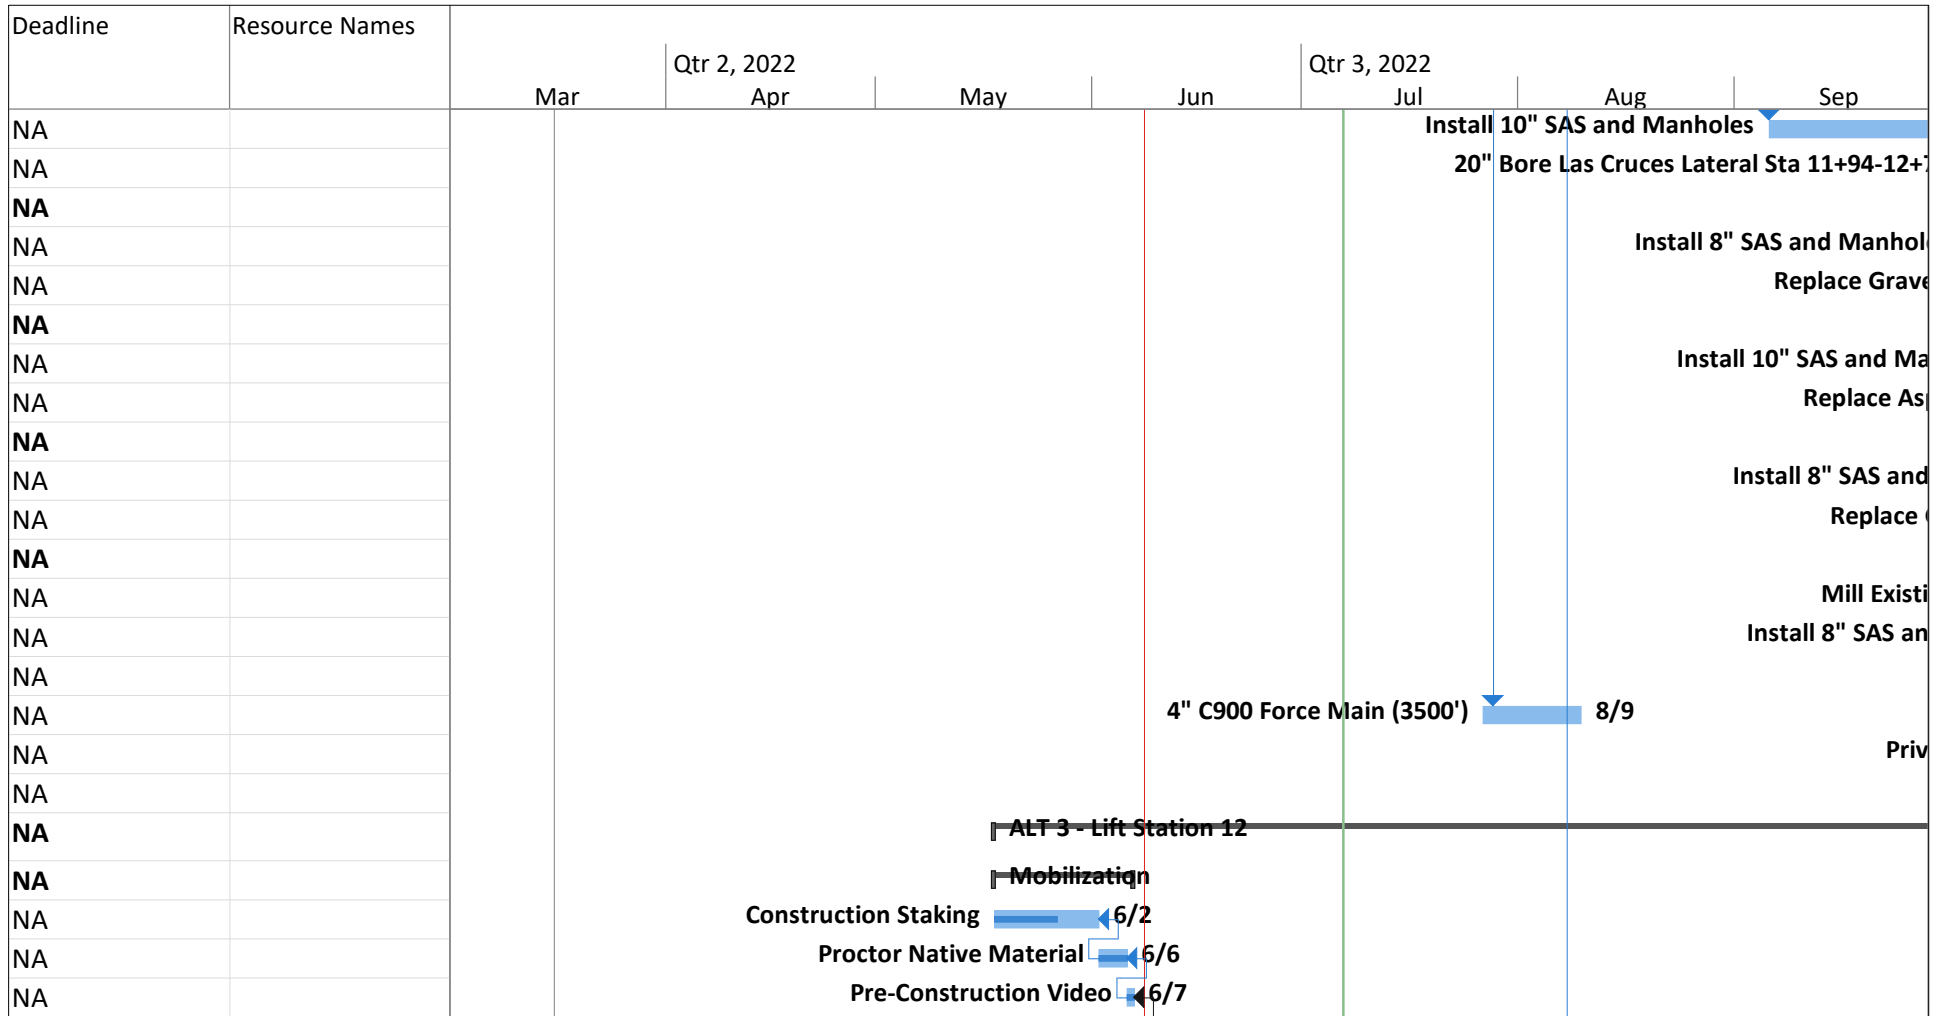

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

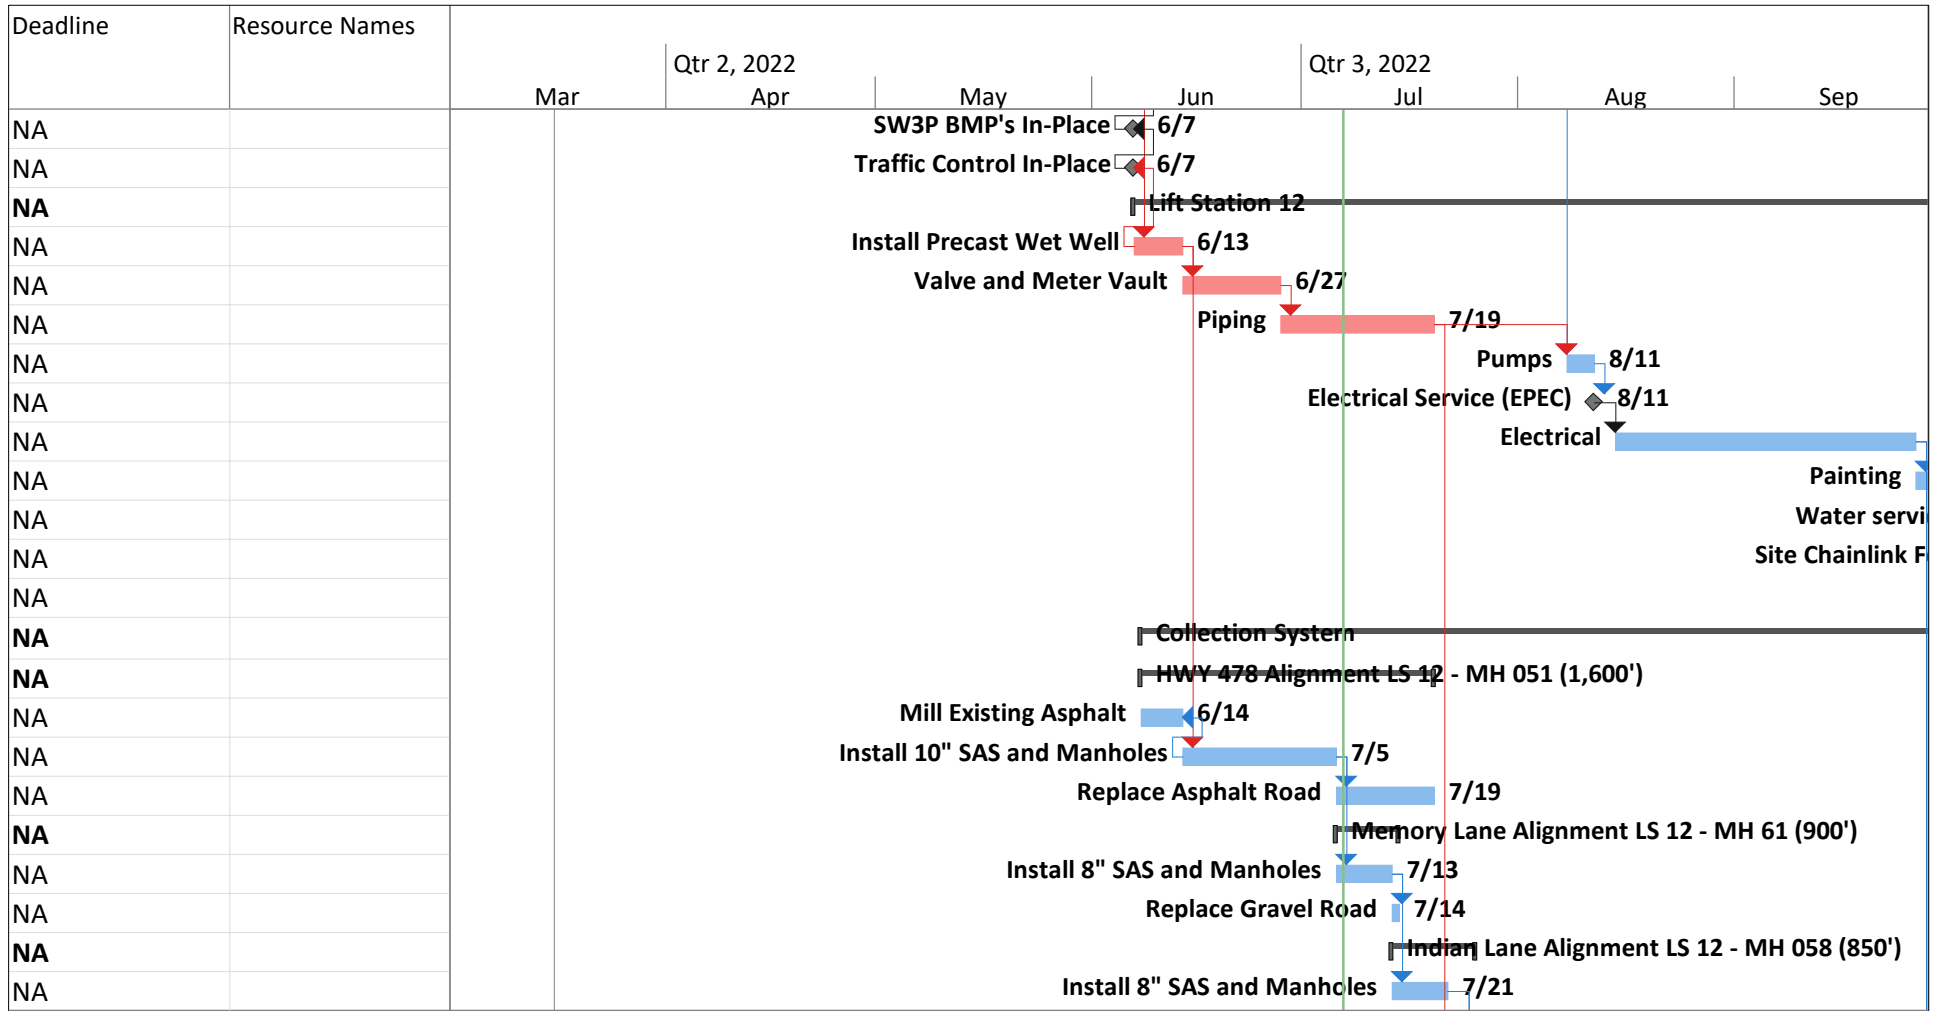

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

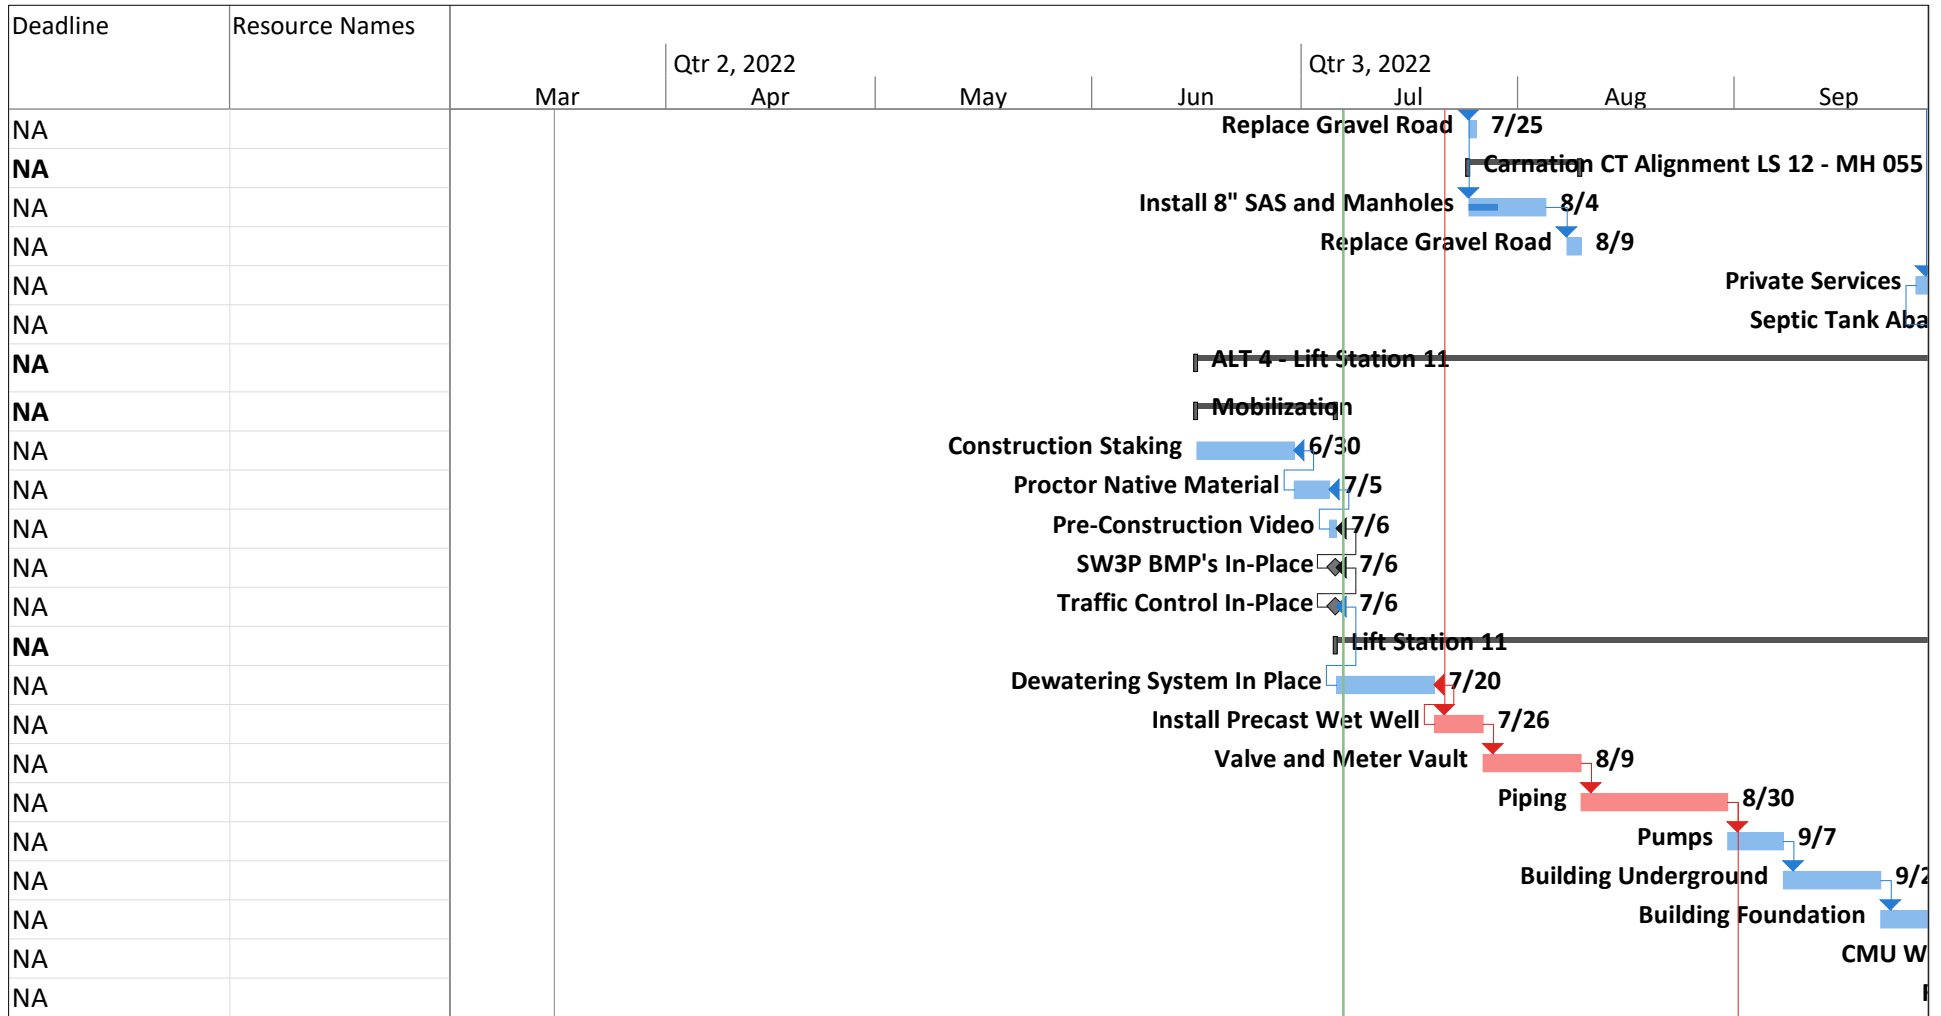

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

Deadline	Resource Names	Qtr 2, 2022				Qtr 3, 2022			
		Mar	Apr	May	Jun	Jul	Aug	Sep	
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									
NA									

Mag/Hydroxi

Collection System

Minter Rd Alignment

Mill Existing Asphalt 8/31

Install 8" SAS and Manholes

Replace Asphalt Road

Install 8" SAS and Manholes

Replace Grave

Install 8" SAS and Manholes

Replace G

Install 8" SAS and

R

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	




Deadline	Resource Names	Qtr 2, 2022				Qtr 3, 2022		
		Mar	Apr	May	Jun	Jul	Aug	Sep
<b>NA</b>		<b>Install 8"</b>						
NA								
NA								
<b>NA</b>								
NA								
NA								
<b>NA</b>								
NA								
NA								
<b>NA</b>								
NA								
NA								
<b>NA</b>								
NA								
NA								
<b>NA</b>								
NA								
NA								
<b>NA</b>								
NA								

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	


Deadline	Resource Names		Qtr 2, 2022		Qtr 3, 2022			
		Mar	Apr	May	Jun	Jul	Aug	Sep
NA								
NA								
Wed 7/26/23								



Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	




Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

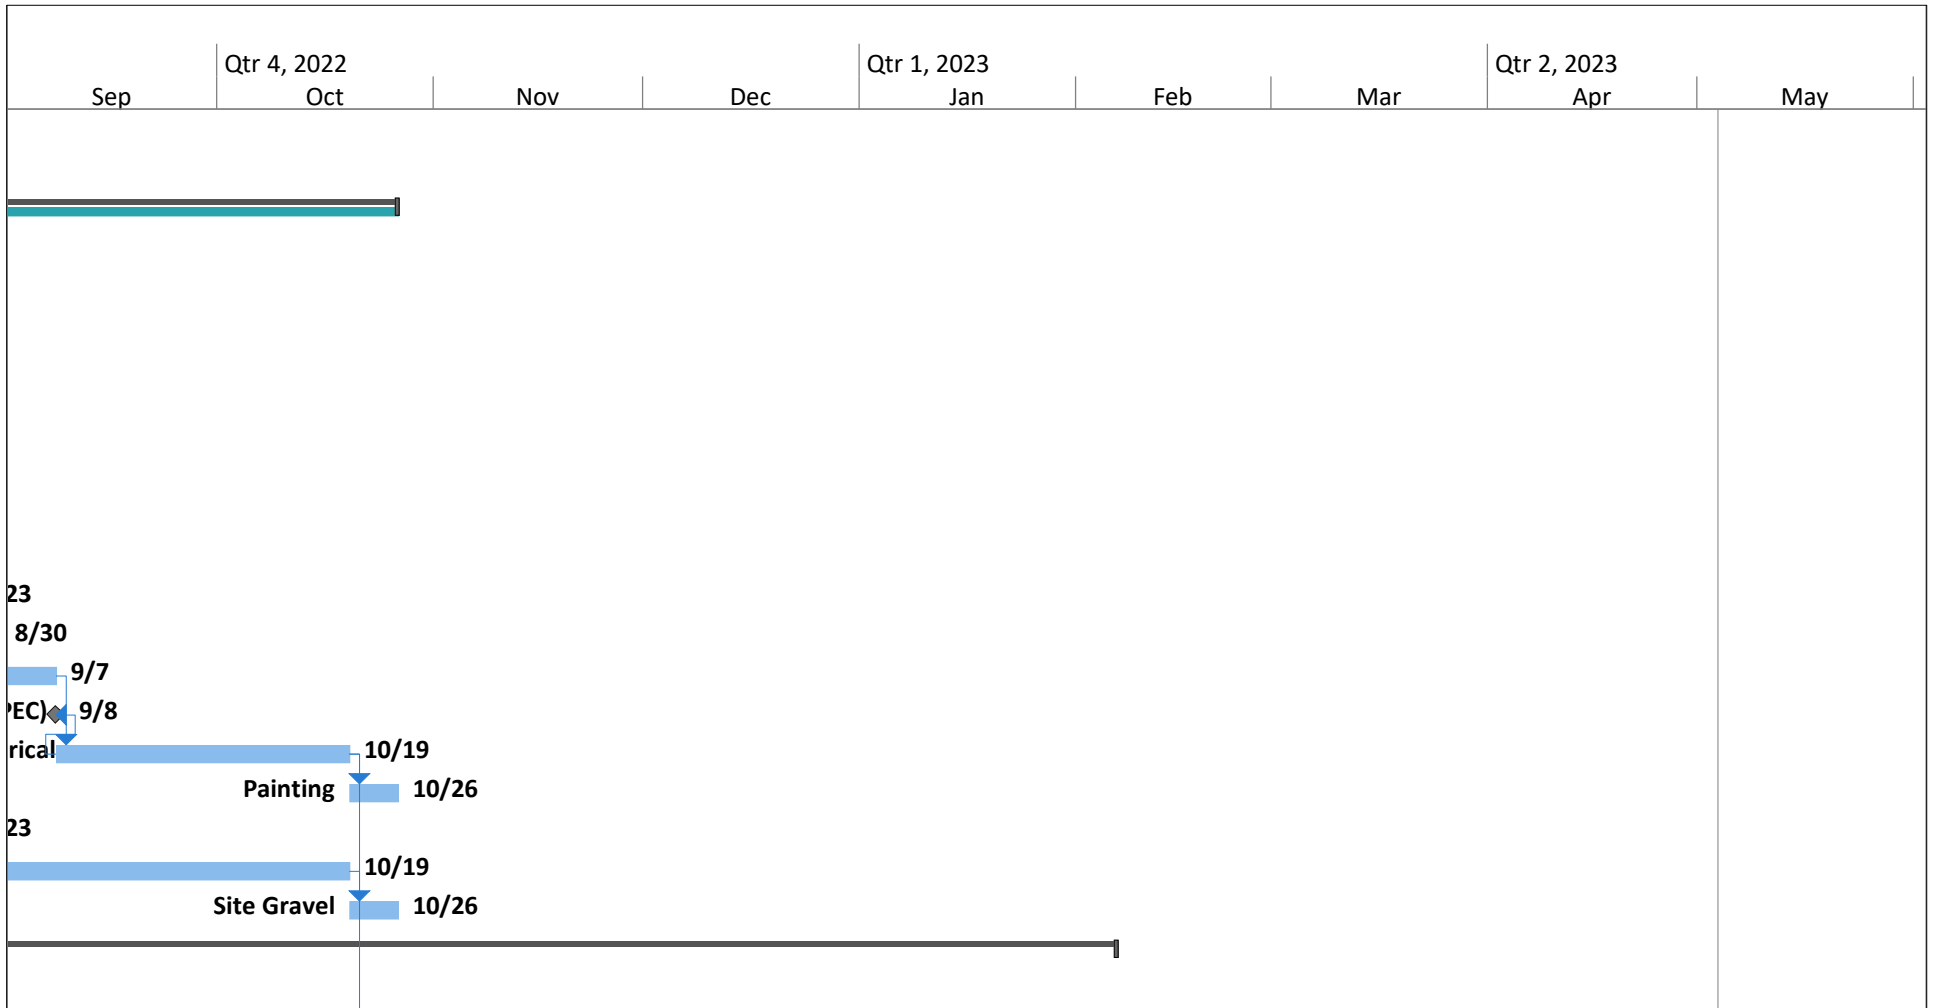


Project: msproj11  
Date: Thu 7/7/22


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

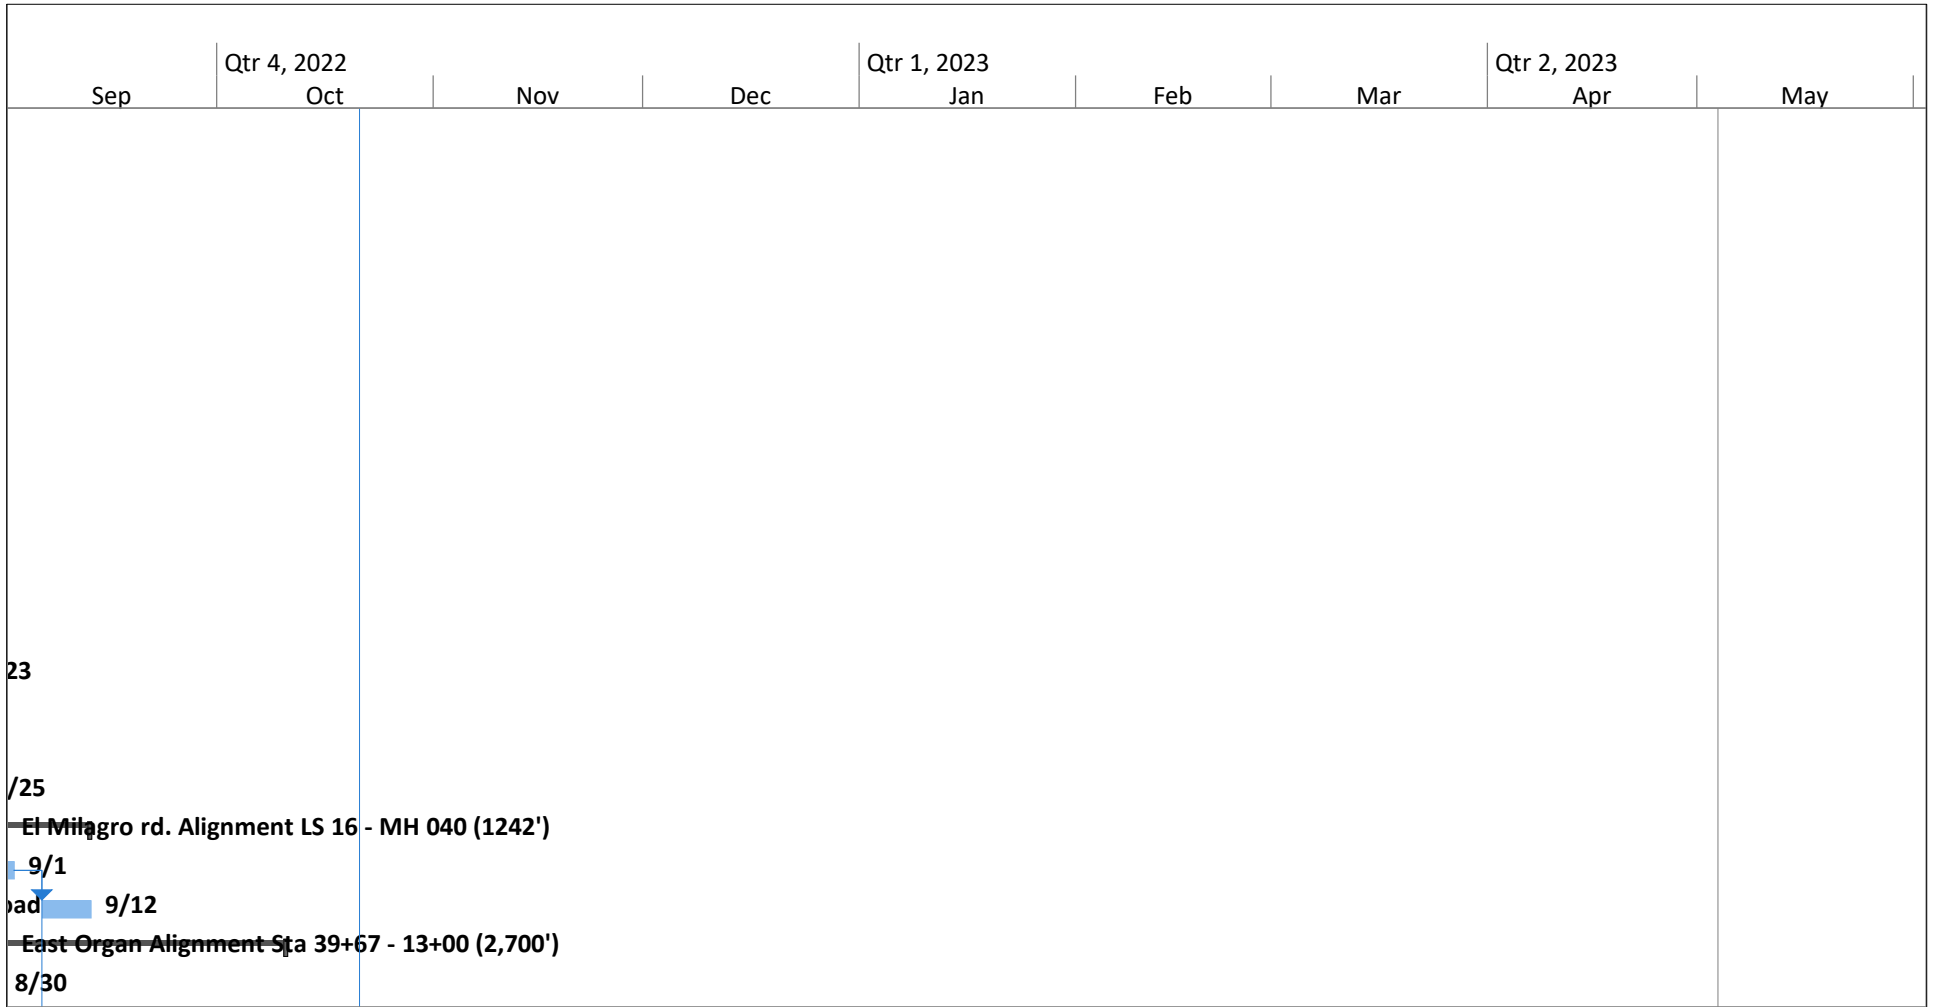


Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

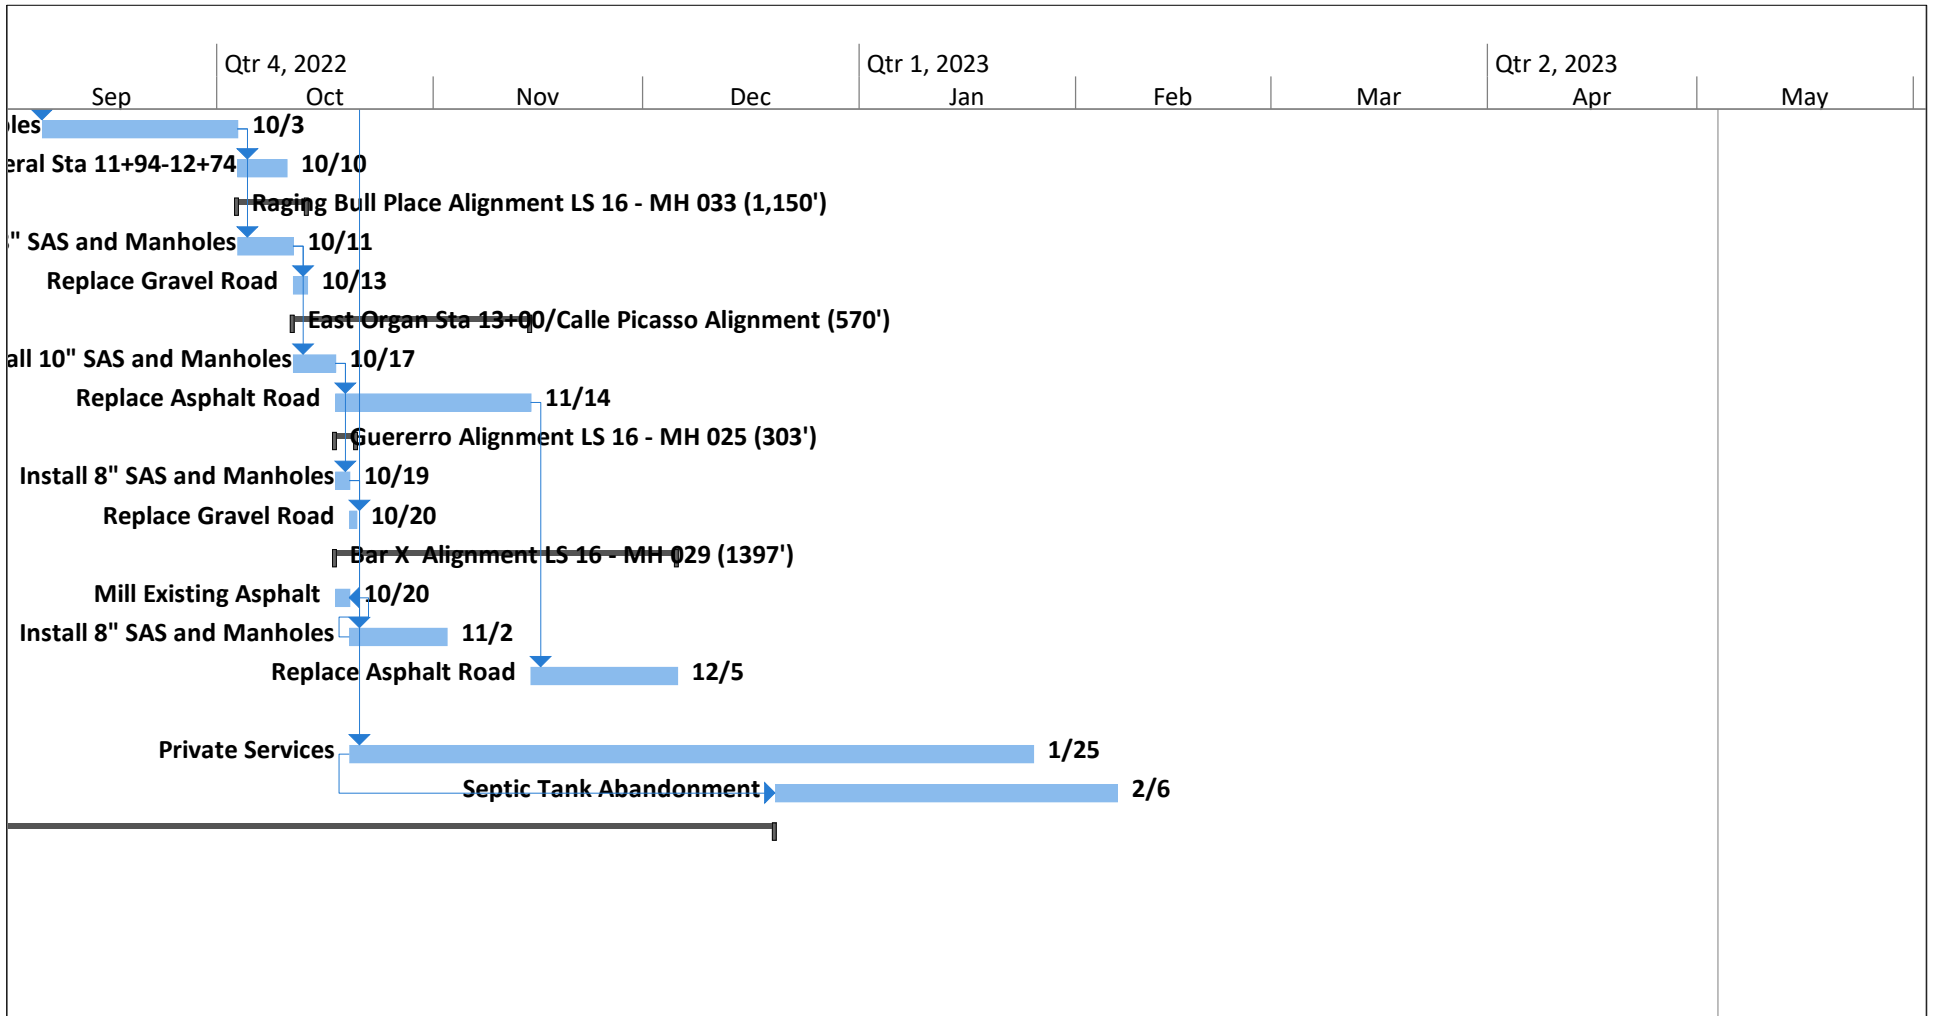

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

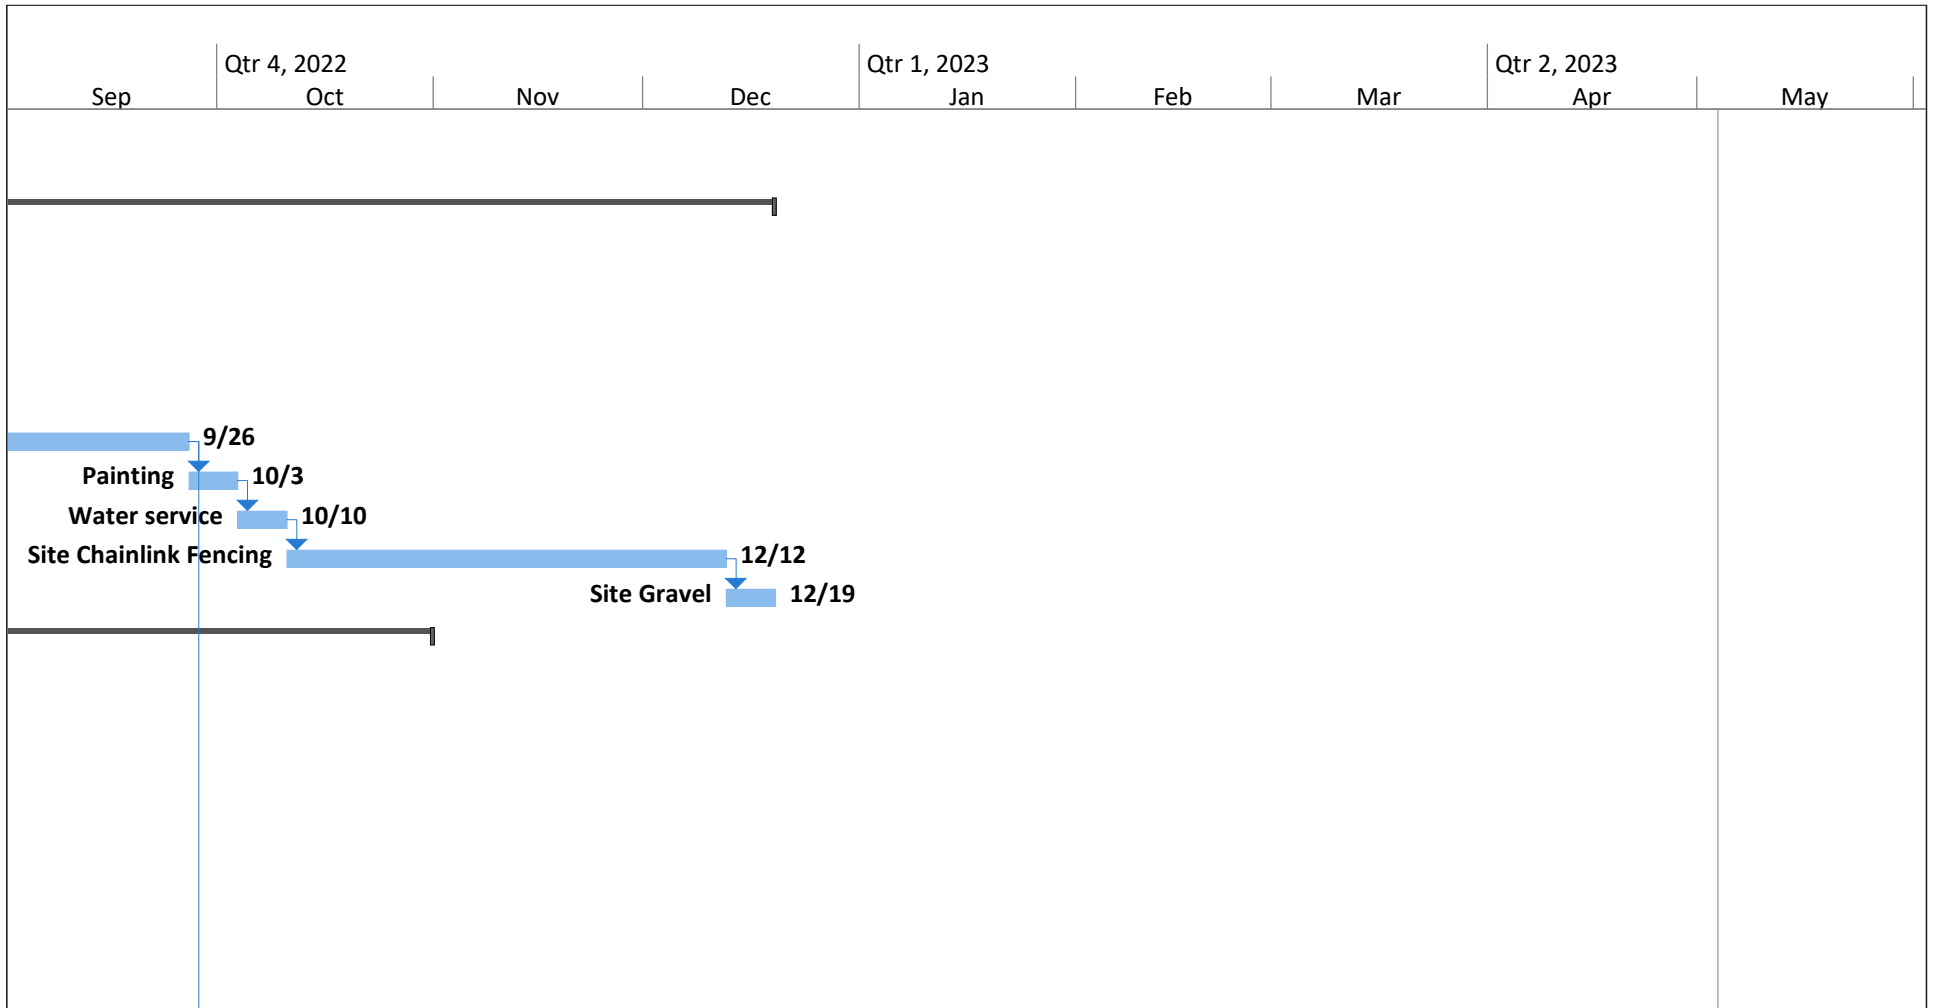


Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

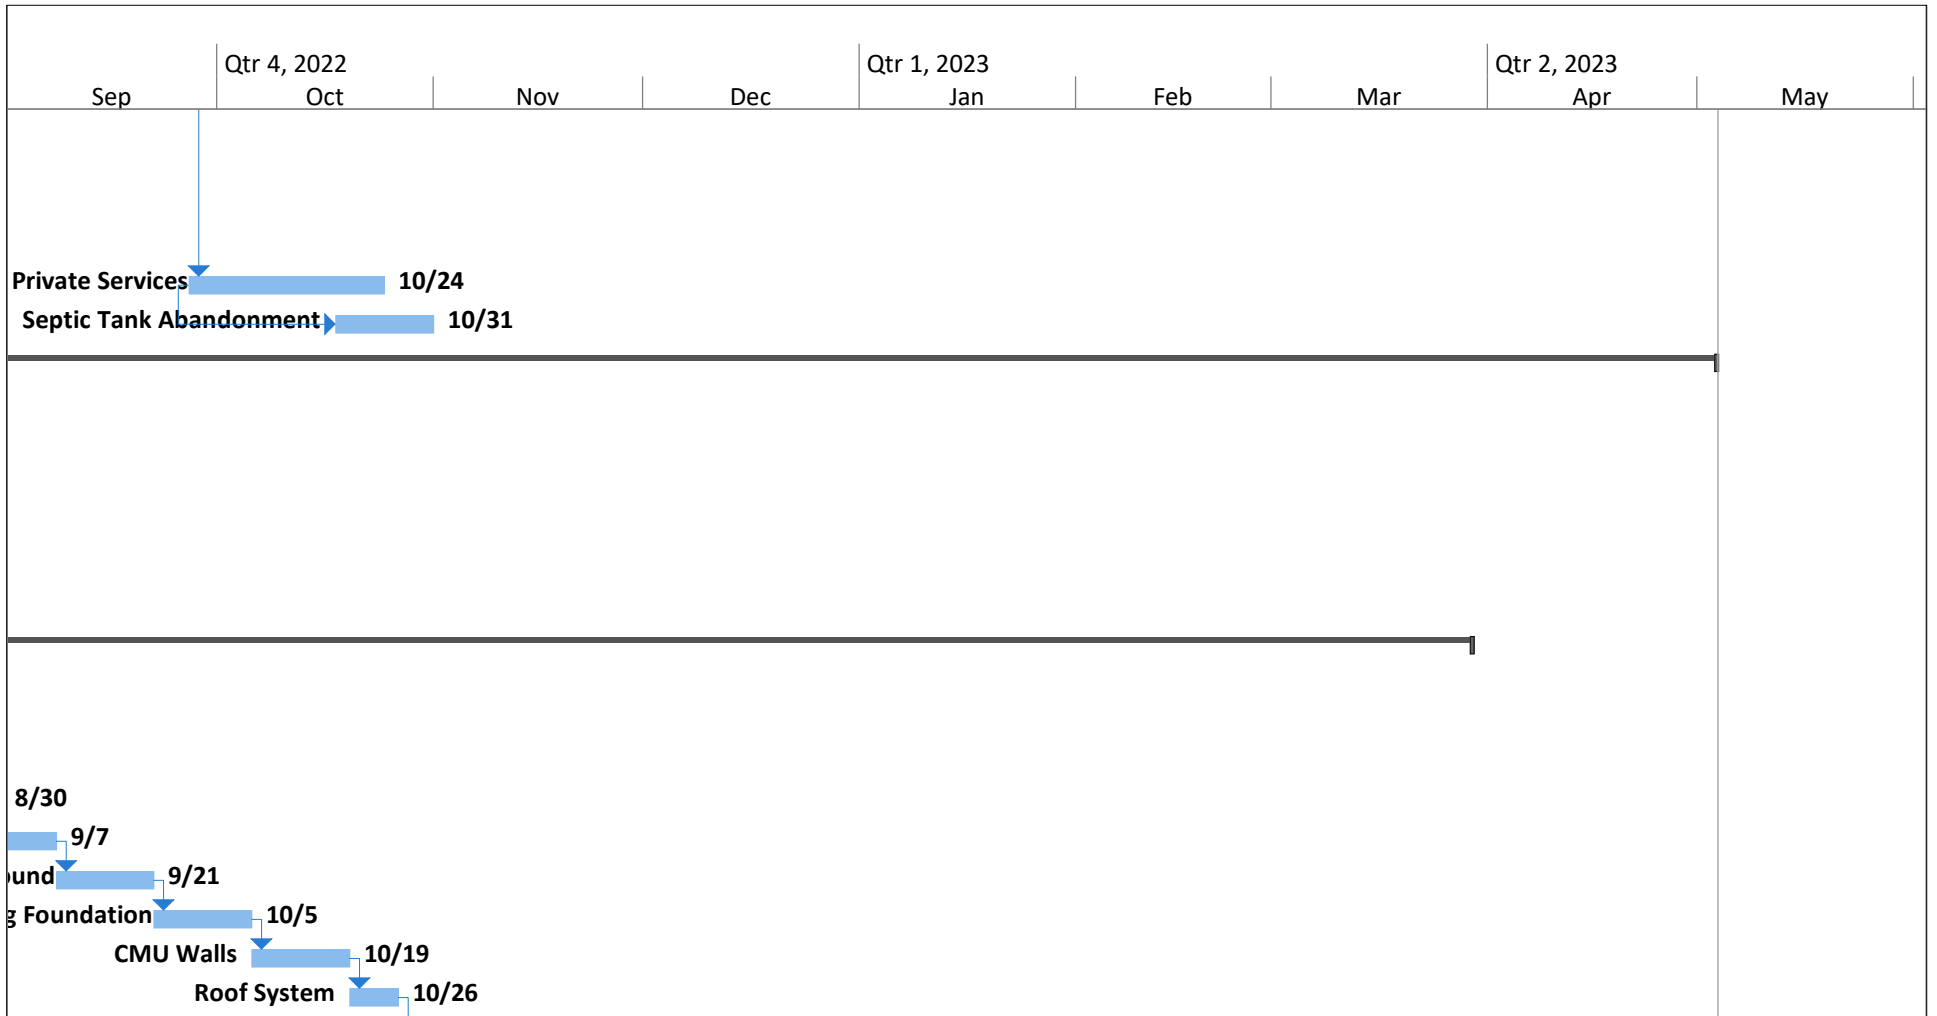


Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	




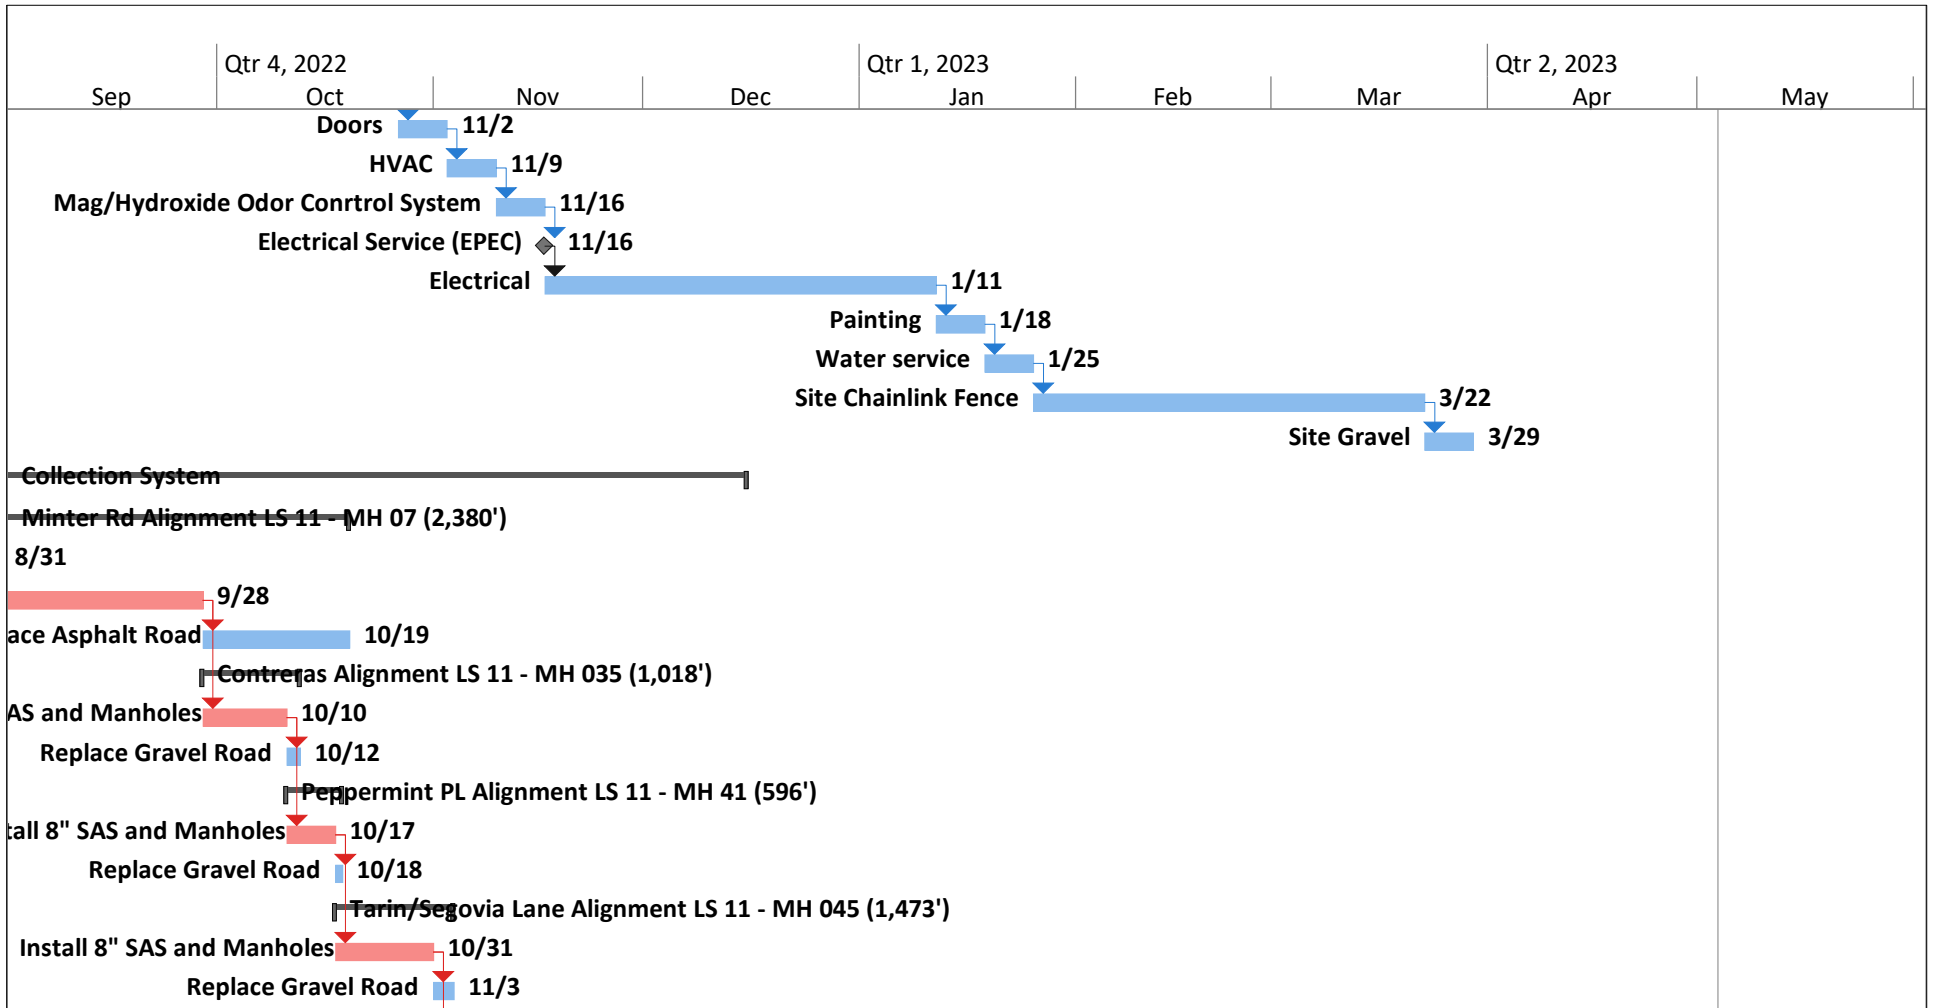

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

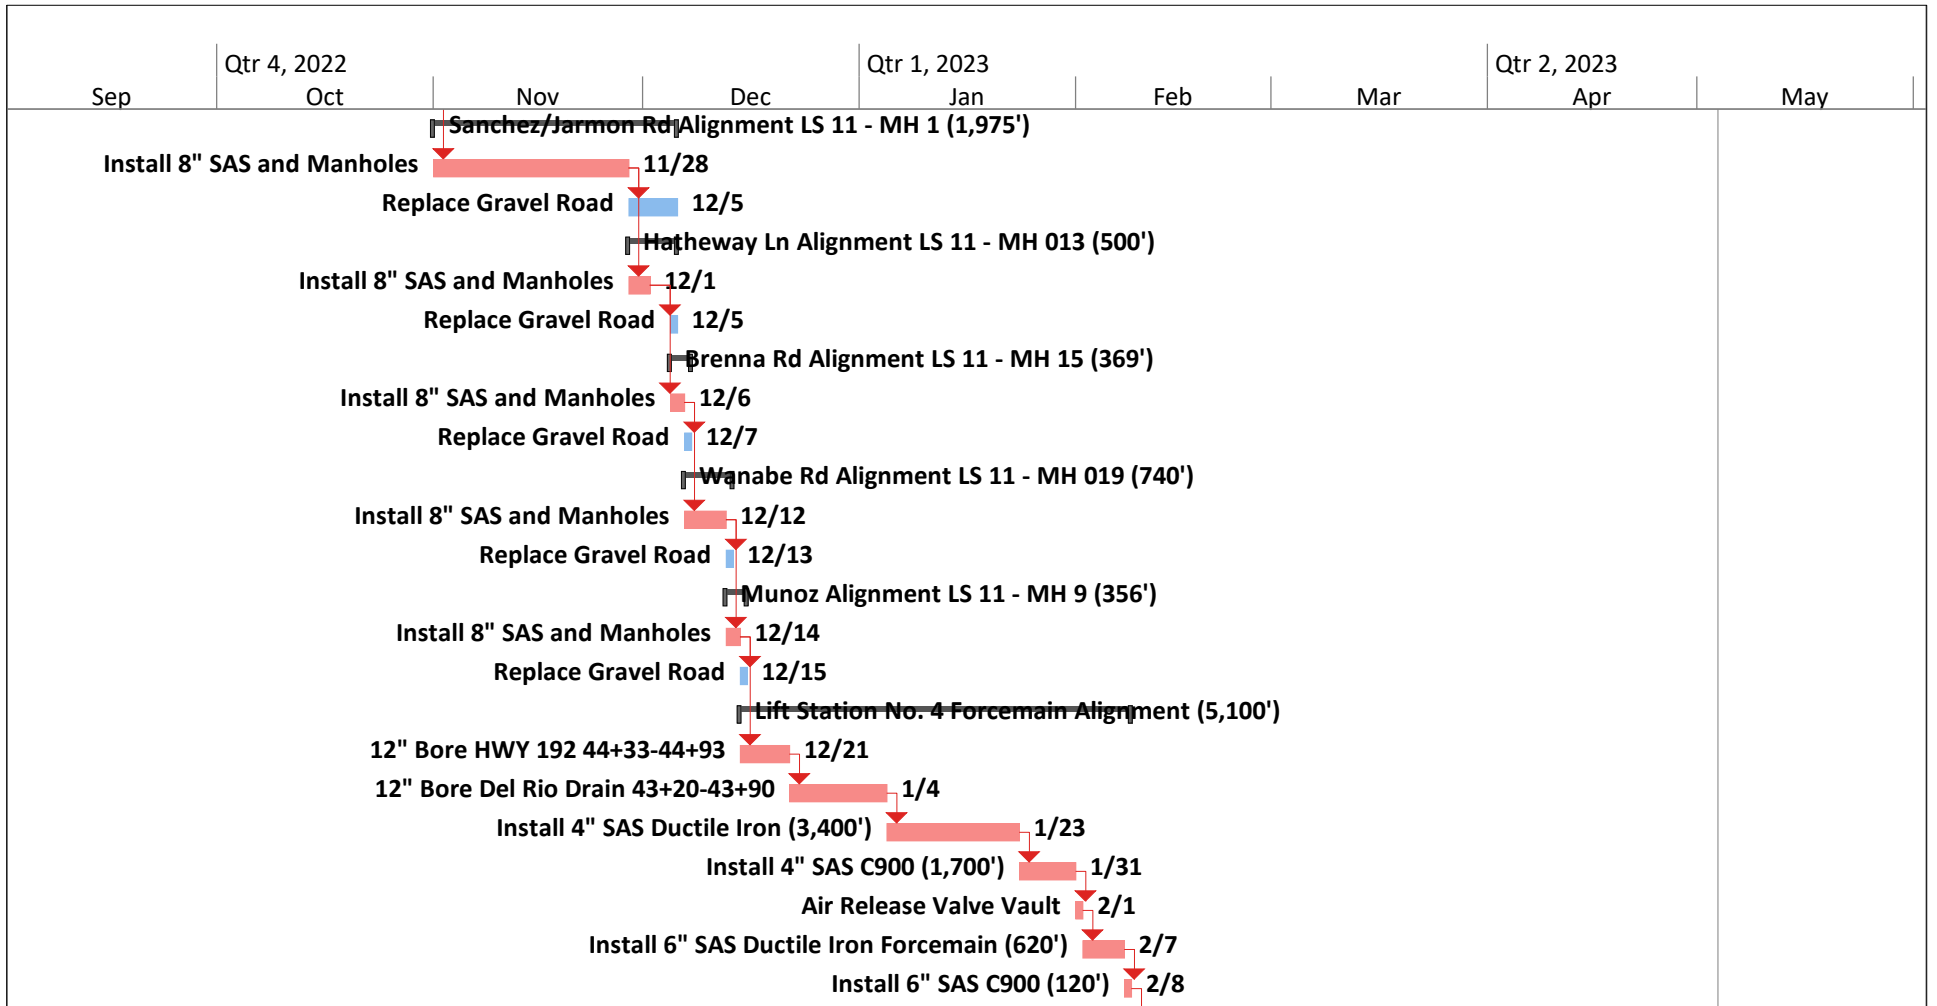

Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	



Project: msproj11 Date: Thu 7/7/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	
