


























































ID	% Comp		Task Mode	Task Name	Duration	Start	Finish	Predecessors
1	36%			Mesquite-Brazito Wastewater System Imp - Project 2	284 days?	Wed 3/16/22	Mon 8/14/23	
2	10...			NOA	0 days	Wed 3/16/22	Wed 3/16/22	
3	10...			NTP (tentative)	0 days	Mon 5/2/22	Mon 5/2/22	2FS+47 edays
4	58%			Approvals	42 days?	Wed 3/16/22	Mon 5/30/22	
5	66%			SWPPP (DAC Approval)	45 edays	Wed 3/16/22	Sat 4/30/22	2
6	50%			TCP (DAC Approval)	45 edays	Wed 3/16/22	Sat 4/30/22	2
7	30%			Roadway Survey (DAC Approval)	45 edays	Wed 3/16/22	Sat 4/30/22	2
8	0%			Building and Site Permits (CID Approval)	30 edays	Sat 4/30/22	Mon 5/30/22	5
9	0%			Dewatering Permits (NM OSE /EBID Approval)	1 day?	Wed 3/16/22	Wed 3/16/22	
10	10...			Pipe	22 edays	Wed 3/16/22	Thu 4/7/22	2
11	10...			Pumps	22 edays	Wed 3/16/22	Thu 4/7/22	2
12	10...			Manholes	30 edays	Wed 3/16/22	Fri 4/15/22	2
13	58%			Deliveries	67 days	Thu 4/7/22	Fri 8/5/22	
14	10...			Pipe	25 edays	Thu 4/7/22	Mon 5/2/22	10
15	50%			Manholes	14 edays	Fri 4/15/22	Fri 4/29/22	12
16	50%			Pumps	120 edays	Thu 4/7/22	Fri 8/5/22	11
17	8%			Base Bid - Lift Station 16	262 days	Mon 4/25/22	Mon 8/14/23	
18	10...			Mobilization	12 days	Mon 4/25/22	Mon 5/16/22	
19	10...			Yard & Temporary Facilities	12 days	Mon 4/25/22	Mon 5/16/22	27SF
20	10...			Project Sign	1 day	Wed 4/27/22	Thu 4/28/22	21SF
21	10...			Construction Staking	8 days	Thu 4/28/22	Thu 5/12/22	22SF
22	10...			Proctor Native Material	1 day	Thu 5/12/22	Mon 5/16/22	24SF
23	10...			Pre-Construction Video	1 day	Thu 5/12/22	Mon 5/16/22	27SF

Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	






















ID	% Comp		Task Mode	Task Name	Duration	Start	Finish	Predecessors
24	10...			SW3P BMP's In-Place	0 days	Mon 5/16/22	Mon 5/16/22	27SF
25	10...			Traffic Control In-Place	0 days	Mon 5/16/22	Mon 5/16/22	27SF
26	3%			Lift Station 16	92 days	Mon 5/16/22	Wed 10/26/22	
27	10...			Install Precast Wet Well	4 days	Mon 5/16/22	Thu 5/19/22	15
28	0%			Valve Vault	8 days	Mon 5/23/22	Mon 6/6/22	27
29	0%			Piping	12 days	Tue 6/7/22	Mon 6/27/22	28
30	0%			Pumps	4 days	Mon 8/8/22	Thu 8/11/22	16,29
31	0%			IBOX Odor Control Unit	4 days	Mon 8/15/22	Thu 8/18/22	30
32	0%			Building Underground	8 days	Tue 6/28/22	Tue 7/12/22	8,29
33	0%			Building Foundation	8 days	Wed 7/13/22	Tue 7/26/22	32
34	0%			CMU Walls	8 days	Wed 7/27/22	Tue 8/9/22	33
35	0%			Roof System	4 days	Wed 8/10/22	Tue 8/16/22	34
36	0%			Doors	4 days	Wed 8/17/22	Tue 8/23/22	35
37	0%			HVAC	4 days	Wed 8/24/22	Tue 8/30/22	36
38	0%			Mag/Hydroxide Odor Control System	4 days	Wed 8/31/22	Wed 9/7/22	37
39	0%			Electrical Service (EPEC)	0 days	Thu 9/8/22	Thu 9/8/22	40SF
40	0%			Electrical	24 days	Thu 9/8/22	Wed 10/19/22	38
41	0%			Painting	4 days	Thu 10/20/22	Wed 10/26/22	40
42	0%			Water service	4 days	Wed 8/17/22	Tue 8/23/22	35
43	0%			Site Fencing	32 days	Wed 8/24/22	Wed 10/19/22	42
44	0%			Site Gravel	4 days	Thu 10/20/22	Wed 10/26/22	43
45	11%			Collection System	138 days	Mon 5/23/22	Mon 2/6/23	
46	10...			East Organ Alignment LS 16 - Sta 48+00 (1,000')	16 days	Mon 5/23/22	Mon 6/20/22	
47	10...			Mill Existing Asphalt	2 days	Mon 5/23/22	Tue 5/24/22	27

Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Comp		Task Mode	Task Name	Duration	Start	Finish	Predecessors
48	10...			Install 10" SAS and Manholes	10 days	Wed 5/25/22	Mon 6/13/22	47
49	10...			20" Bore Mesquite Drain Sta 48+62-49+97	4 days	Tue 6/14/22	Mon 6/20/22	48
50	10...			BBQ/Picnic CT Alignment LS 16 - MH 049 (1405')	8 days	Tue 6/14/22	Mon 6/27/22	
51	10...			Mill Existing Asphalt	2 days	Tue 6/14/22	Wed 6/15/22	48
52	10...			Install 8" SAS and Manholes	8 days	Tue 6/14/22	Mon 6/27/22	48
53	6%			East Organ Alignment Sta 48+00 - 64+00 (1,600')	43 days	Mon 6/27/22	Mon 9/12/22	
54	10...			Mill Existing Asphalt	2 days	Mon 6/27/22	Tue 6/28/22	51
55	0%			Install 10" SAS and Manholes	16 days	Mon 7/25/22	Thu 8/18/22	
56	0%			Replace Asphalt Road	12 days	Mon 8/22/22	Mon 9/12/22	55
57	0%			20" Bore Apache Lateral Sta 64+10-64+80	4 days	Mon 8/22/22	Thu 8/25/22	55
58	0%			Valles/Relic Alignment LS 16 - MH 046 (1692')	16 days	Mon 8/22/22	Mon 9/19/22	
59	0%			Mill Existing Asphalt	2 days	Mon 8/22/22	Tue 8/23/22	55
60	0%			Install 8" SAS and Manholes	8 days	Mon 8/22/22	Thu 9/1/22	55
61	0%			Replace Asphalt Road	4 days	Tue 9/13/22	Mon 9/19/22	56
62	0%			Primos CT/Relic CT Alignment LS 16 - MH 048 (1,296')	10 days	Tue 9/6/22	Wed 9/21/22	
63	0%			Install 8" SAS and Manholes	6 days	Tue 9/6/22	Wed 9/14/22	60
64	0%			Replace Gravel Road	4 days	Thu 9/15/22	Wed 9/21/22	63
65	0%			El Milagro rd. Alignment LS 16 - MH 040 (1242')	12 days	Mon 8/22/22	Mon 9/12/22	
66	0%			Install 8" SAS and Manholes	8 days	Mon 8/22/22	Thu 9/1/22	55
67	0%			Replace Gravel Road	4 days	Tue 9/6/22	Mon 9/12/22	66
68	0%			East Organ Alignment Sta 39+67 - 13+00 (2,700')	20 days	Tue 9/6/22	Mon 10/10/22	
69	0%			Mill Existing Asphalt	4 days	Tue 9/20/22	Mon 9/26/22	61
70	0%			Install 10" SAS and Manholes	16 days	Tue 9/6/22	Mon 10/3/22	66
71	0%			20" Bore Las Cruces Lateral Sta 11+94-12+74	4 days	Tue 10/4/22	Mon 10/10/22	70

Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Comp		Task Mode	Task Name	Duration	Start	Finish	Predecessors
72	0%			Raging Bull Place Alignment LS 16 - MH 033 (1,150')	7 days	Tue 10/4/22	Thu 10/13/22	
73	0%			Install 8" SAS and Manholes	5 days	Tue 10/4/22	Tue 10/11/22	70
74	0%			Replace Gravel Road	2 days	Wed 10/12/22	Thu 10/13/22	73
75	0%			East Organ Sta 13+00/Calle Picasso Alignment (570')	19 days	Wed 10/12/22	Mon 11/14/22	
76	0%			Install 10" SAS and Manholes	3 days	Wed 10/12/22	Mon 10/17/22	73
77	0%			Replace Asphalt Road	16 days	Tue 10/18/22	Mon 11/14/22	76
78	0%			Guererro Alignment LS 16 - MH 025 (303')	3 days	Tue 10/18/22	Thu 10/20/22	
79	0%			Install 8" SAS and Manholes	2 days	Tue 10/18/22	Wed 10/19/22	76
80	0%			Replace Gravel Road	1 day	Thu 10/20/22	Thu 10/20/22	79
81	0%			Bar X Alignment LS 16 - MH 029 (1397')	24 days	Tue 10/18/22	Mon 12/5/22	
82	0%			Mill Existing Asphalt	2 days	Tue 10/18/22	Thu 10/20/22	83SF
83	0%			Install 8" SAS and Manholes	8 days	Thu 10/20/22	Wed 11/2/22	79
84	0%			Replace Asphalt Road	8 days	Tue 11/15/22	Mon 12/5/22	77
85	0%			4" C900 Force Main (3500')	8 days	Wed 7/27/22	Tue 8/9/22	33
86	0%			Private Services	48 days	Thu 10/20/22	Wed 1/25/23	40
87	0%			Septic Tank Abandonment	24 days	Tue 12/20/22	Mon 2/6/23	86SS+30 days
88	13%			ALT 3 - Lift Station 12	116 days	Wed 5/18/22	Mon 12/19/22	
89	80%			Mobilization	10 days	Wed 5/18/22	Tue 6/7/22	
90	75%			Construction Staking	8 days	Wed 5/18/22	Thu 6/2/22	91SF
91	10...			Proctor Native Material	1 day	Thu 6/2/22	Mon 6/6/22	92SF
92	10...			Pre-Construction Video	1 day	Mon 6/6/22	Tue 6/7/22	93SF
93	10...			SW3P BMP's In-Place	0 days	Tue 6/7/22	Tue 6/7/22	94SF
94	10...			Traffic Control In-Place	0 days	Tue 6/7/22	Tue 6/7/22	96SF

Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Comp		Task Mode	Task Name	Duration	Start	Finish	Predecessors
95	4%			Lift Station 12	106 days	Tue 6/7/22	Mon 12/19/22	
96	10...			Install Precast Wet Well	4 days	Tue 6/7/22	Mon 6/13/22	28
97	0%			Valve and Meter Vault	8 days	Tue 6/14/22	Mon 6/27/22	96
98	0%			Piping	12 days	Tue 6/28/22	Tue 7/19/22	97
99	0%			Pumps	4 days	Mon 8/8/22	Thu 8/11/22	98,16
100	0%			Electrical Service (EPEC)	0 days	Thu 8/11/22	Thu 8/11/22	99
101	0%			Electrical	24 days	Mon 8/15/22	Mon 9/26/22	100
102	0%			Painting	4 days	Tue 9/27/22	Mon 10/3/22	101
103	0%			Water service	4 days	Tue 10/4/22	Mon 10/10/22	102
104	0%			Site Chainlink Fencing	32 days	Tue 10/11/22	Mon 12/12/22	103
105	0%			Site Gravel	4 days	Tue 12/13/22	Mon 12/19/22	104
106	14%			Collection System	81 days	Wed 6/8/22	Mon 10/31/22	
107	0%			HWY 478 Alignment LS 12 - MH 051 (1,600')	23 days	Wed 6/8/22	Tue 7/19/22	
108	0%			Mill Existing Asphalt	3 days	Wed 6/8/22	Tue 6/14/22	109SF
109	0%			Install 10" SAS and Manholes	12 days	Tue 6/14/22	Tue 7/5/22	96
110	0%			Replace Asphalt Road	8 days	Wed 7/6/22	Tue 7/19/22	109
111	0%			Memory Lane Alignment LS 12 - MH 61 (900')	6 days	Wed 7/6/22	Thu 7/14/22	
112	0%			Install 8" SAS and Manholes	5 days	Wed 7/6/22	Wed 7/13/22	109
113	0%			Replace Gravel Road	1 day	Thu 7/14/22	Thu 7/14/22	112
114	0%			Indian Lane Alignment LS 12 - MH 058 (850')	6 days	Thu 7/14/22	Mon 7/25/22	
115	0%			Install 8" SAS and Manholes	5 days	Thu 7/14/22	Thu 7/21/22	112
116	0%			Replace Gravel Road	1 day	Mon 7/25/22	Mon 7/25/22	115
117	10...			Carnation CT Alignment LS 12 - MH 055 (1006')	10 days	Mon 7/25/22	Tue 8/9/22	
118	10...			Install 8" SAS and Manholes	8 days	Mon 7/25/22	Thu 8/4/22	115

Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Comp		Task Mode	Task Name	Duration	Start	Finish	Predecessors
119	10...			Replace Gravel Road	2 days	Mon 8/8/22	Tue 8/9/22	118
120	0%			Private Services	16 days	Tue 9/27/22	Mon 10/24/22	101
121	0%			Septic Tank Abandonment	8 days	Tue 10/18/22	Mon 10/31/22	120SS+12 days
122	0%			ALT 4 - Lift Station 11	164 days	Tue 10/18/22	Mon 8/14/23	
123	0%			Mobilization	8 days	Mon 10/31/22	Mon 11/14/22	121
124	0%			Construction Staking	8 days	Tue 11/1/22	Mon 11/14/22	125SF
125	0%			Proctor Native Material	1 day	Tue 11/1/22	Tue 11/1/22	126SF
126	0%			Pre-Construction Video	1 day	Tue 11/1/22	Tue 11/1/22	127SF
127	0%			SW3P BMP's In-Place	0 days	Mon 10/31/22	Mon 10/31/22	128SF
128	0%			Traffic Control In-Place	0 days	Mon 10/31/22	Mon 10/31/22	130SF
129	0%			Lift Station 11	144 days	Tue 10/18/22	Mon 7/10/23	
130	0%			Dewatering System In Place	8 days	Tue 10/18/22	Tue 11/1/22	131SF
131	0%			Install Precast Wet Well	4 days	Tue 11/1/22	Mon 11/7/22	121
132	0%			Valve and Meter Vault	8 days	Tue 11/8/22	Mon 11/28/22	131
133	0%			Piping	12 days	Tue 11/29/22	Mon 12/19/22	132
134	0%			Pumps	4 days	Tue 12/20/22	Mon 1/2/23	133
135	0%			Building Underground	8 days	Tue 1/3/23	Mon 1/16/23	134
136	0%			Building Foundation	8 days	Tue 1/17/23	Mon 1/30/23	135
137	0%			CMU Walls	8 days	Tue 1/31/23	Mon 2/13/23	136
138	0%			Roof System	4 days	Tue 2/14/23	Mon 2/20/23	137
139	0%			Doors	4 days	Tue 2/21/23	Mon 2/27/23	138
140	0%			HVAC	4 days	Tue 2/28/23	Mon 3/6/23	139
141	0%			Mag/Hydroxide Odor Control System	4 days	Tue 3/7/23	Mon 3/13/23	140

Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Comp	Task Mode	Task Name	Duration	Start	Finish	Predecessors
142	0%		Electrical Service (EPEC)	0 days	Mon 3/13/23	Mon 3/13/23	141
143	0%		Electrical	24 days	Tue 3/14/23	Mon 4/24/23	142
144	0%		Painting	4 days	Tue 4/25/23	Mon 5/1/23	143
145	0%		Water service	4 days	Tue 5/2/23	Mon 5/8/23	144
146	0%		Site Chainlink Fence	32 days	Tue 5/9/23	Mon 7/3/23	145
147	0%		Site Gravel	4 days	Tue 7/4/23	Mon 7/10/23	146
148	0%		Collection System	63 days	Thu 12/8/22	Tue 4/4/23	
149	0%		Minter Rd Alignment LS 11 - MH 07 (2,380')	34 days	Thu 12/8/22	Mon 2/13/23	
150	0%		Mill Existing Asphalt	6 days	Thu 12/8/22	Tue 12/20/22	151SF
151	0%		Install 8" SAS and Manholes	16 days	Tue 12/20/22	Mon 1/23/23	133
152	0%		Replace Asphalt Road	12 days	Tue 1/24/23	Mon 2/13/23	151
153	0%		Contreras Alignment LS 11 - MH 035 (1,018')	8 days	Tue 1/24/23	Mon 2/6/23	
154	0%		Install 8" SAS and Manholes	6 days	Tue 1/24/23	Wed 2/1/23	151
155	0%		Replace Gravel Road	2 days	Thu 2/2/23	Mon 2/6/23	154
156	0%		Peppermint PL Alignment LS 11 - MH 41 (596')	5 days	Thu 2/2/23	Thu 2/9/23	
157	0%		Install 8" SAS and Manholes	4 days	Thu 2/2/23	Wed 2/8/23	154
158	0%		Replace Gravel Road	1 day	Thu 2/9/23	Thu 2/9/23	157
159	0%		Tarin/Segovia Lane Alignment LS 11 - MH 045 (1,473')	11 days	Thu 2/9/23	Tue 2/28/23	
160	0%		Install 8" SAS and Manholes	8 days	Thu 2/9/23	Wed 2/22/23	157
161	0%		Replace Gravel Road	3 days	Thu 2/23/23	Tue 2/28/23	160
162	0%		Sanchez/Jarmon Rd Alignment LS 11 - MH 1 (1,975')	16 days	Thu 2/23/23	Wed 3/22/23	
163	0%		Install 8" SAS and Manholes	12 days	Thu 2/23/23	Wed 3/15/23	160
164	0%		Replace Gravel Road	4 days	Thu 3/16/23	Wed 3/22/23	163
165	0%		Hatheway Ln Alignment LS 11 - MH 013 (500')	4 days	Thu 3/16/23	Wed 3/22/23	


Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

ID	% Comp	Task Mode	Task Name	Duration	Start	Finish	Predecessors
166	0%		Install 8" SAS and Manholes	3 days	Thu 3/16/23	Tue 3/21/23	163
167	0%		Replace Gravel Road	1 day	Wed 3/22/23	Wed 3/22/23	166
168	0%		Brenna Rd Alignment LS 11 - MH 15 (369')	3 days	Wed 3/22/23	Mon 3/27/23	
169	0%		Install 8" SAS and Manholes	2 days	Wed 3/22/23	Thu 3/23/23	166
170	0%		Replace Gravel Road	1 day	Mon 3/27/23	Mon 3/27/23	169
171	0%		Wanabe Rd Alignment LS 11 - MH 019 (740')	4 days	Mon 3/27/23	Thu 3/30/23	
172	0%		Install 8" SAS and Manholes	3 days	Mon 3/27/23	Wed 3/29/23	169
173	0%		Replace Gravel Road	1 day	Thu 3/30/23	Thu 3/30/23	172
174	0%		Munoz Alignment LS 11 - MH 9 (356')	3 days	Thu 3/30/23	Tue 4/4/23	
175	0%		Install 8" SAS and Manholes	2 days	Thu 3/30/23	Mon 4/3/23	172
176	0%		Replace Gravel Road	1 day	Tue 4/4/23	Tue 4/4/23	175
177	0%		Lift Station No. 4 Forcemain Alignment (5,100')	28 days	Tue 4/4/23	Mon 5/22/23	
178	0%		12" Bore HWY 192 44+33-44+93	4 days	Tue 4/4/23	Mon 4/10/23	175
179	0%		12" Bore Del Rio Drain 43+20-43+90	4 days	Tue 4/11/23	Mon 4/17/23	178
180	0%		Install 4" SAS Ductile Iron (3,400')	10 days	Tue 4/18/23	Wed 5/3/23	179
181	0%		Install 4" SAS C900 (1,700')	5 days	Thu 5/4/23	Thu 5/11/23	180
182	0%		Air Release Valve Vault	1 day	Mon 5/15/23	Mon 5/15/23	181
183	0%		Install 6" SAS Ductile Iron Forcemain (620')	3 days	Tue 5/16/23	Thu 5/18/23	182
184	0%		Install 6" SAS C900 (120')	1 day	Mon 5/22/23	Mon 5/22/23	183
185	0%		Private Services	48 days	Tue 5/23/23	Mon 8/14/23	184
186	0%		Septic Tank Abandonment	24 days	Tue 7/4/23	Mon 8/14/23	185SS+24 days
187	0%		Substantial Completion (450 Calendar Days)	0 days	Mon 8/14/23	Mon 8/14/23	186


Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

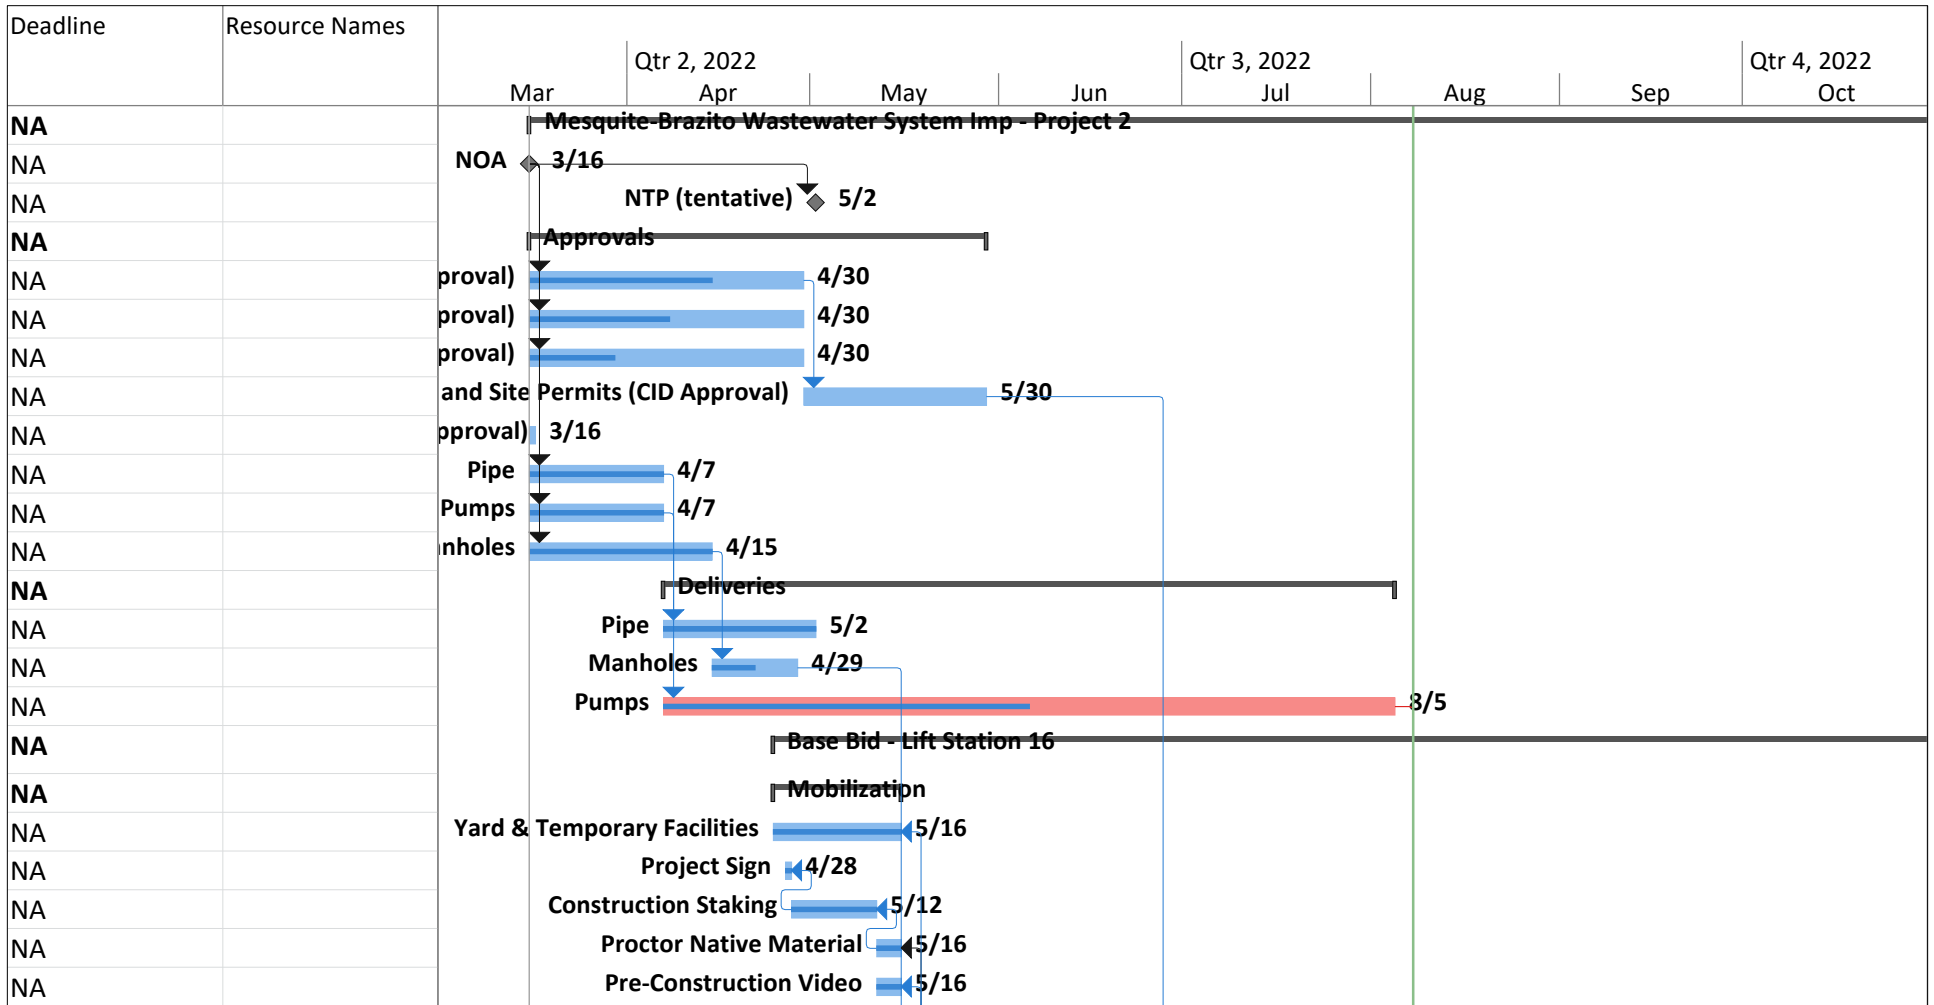


Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

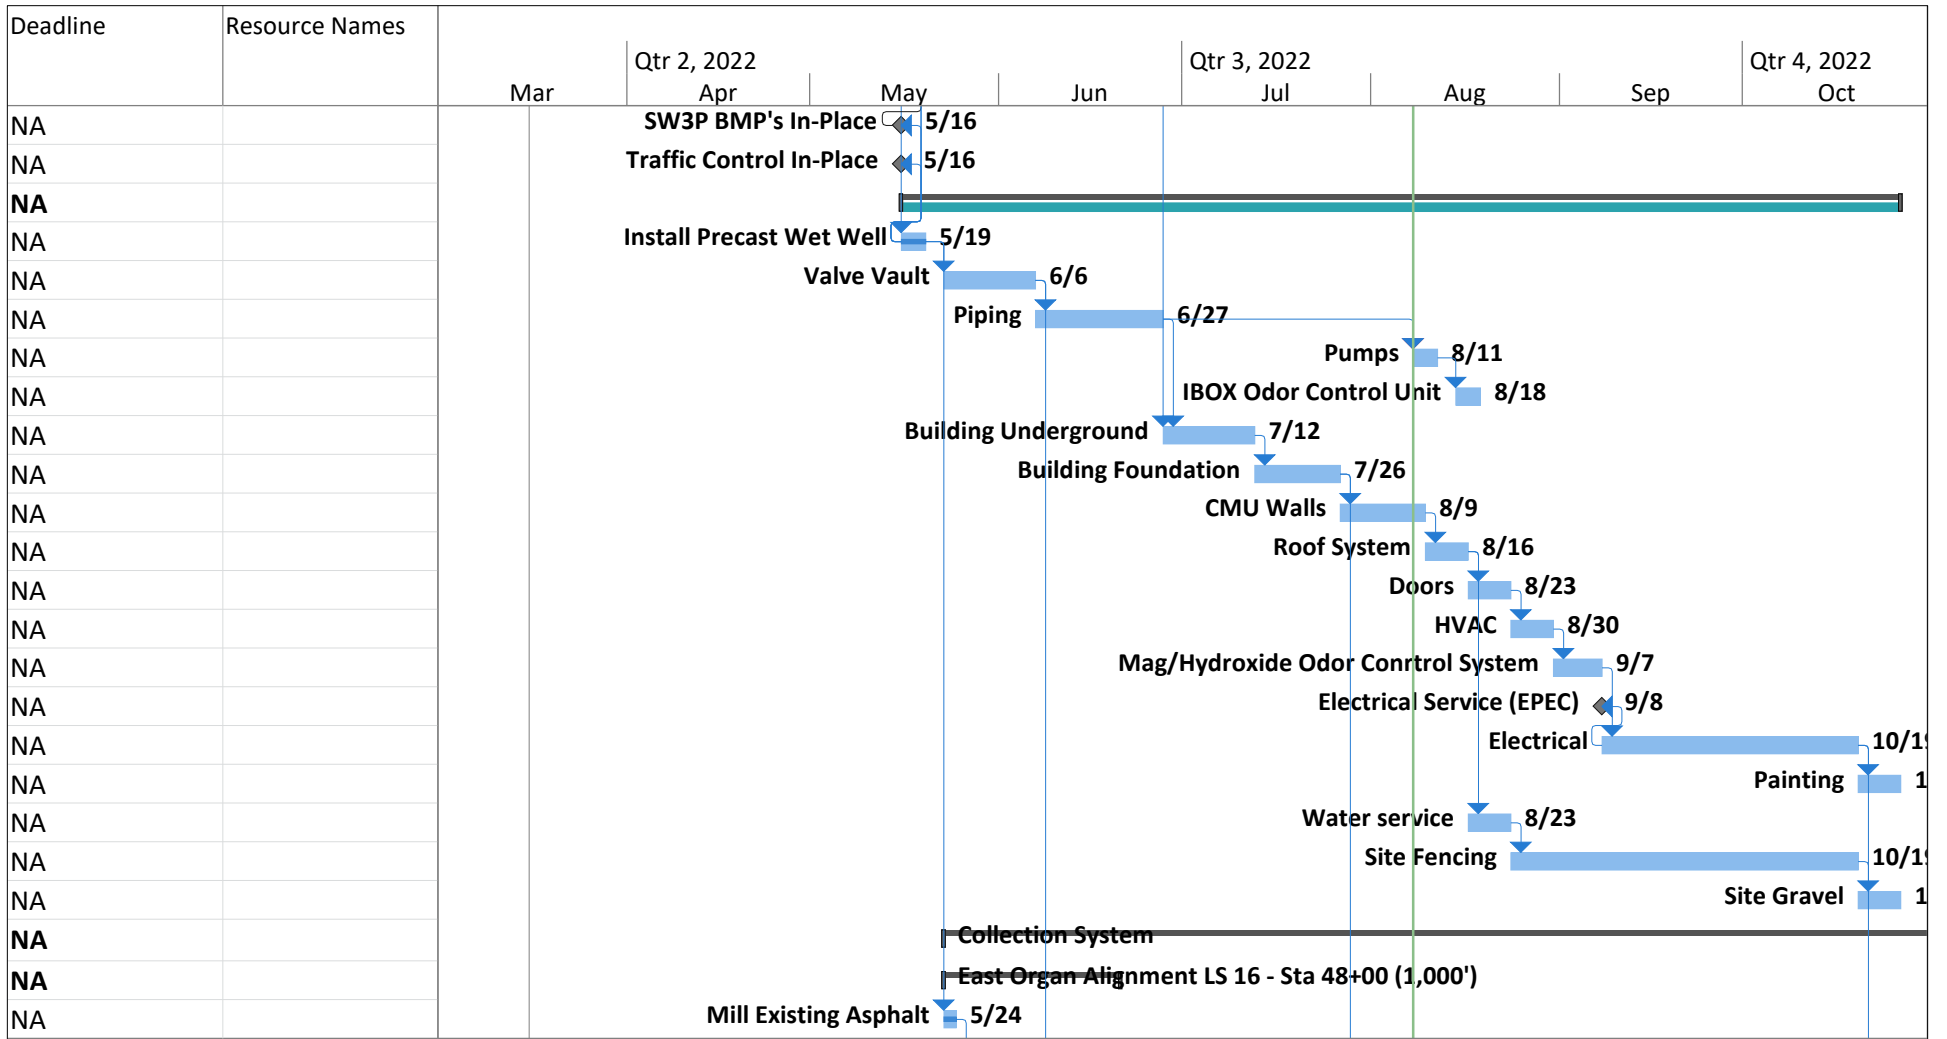


Project: msproj11
Date: Mon 8/8/22


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

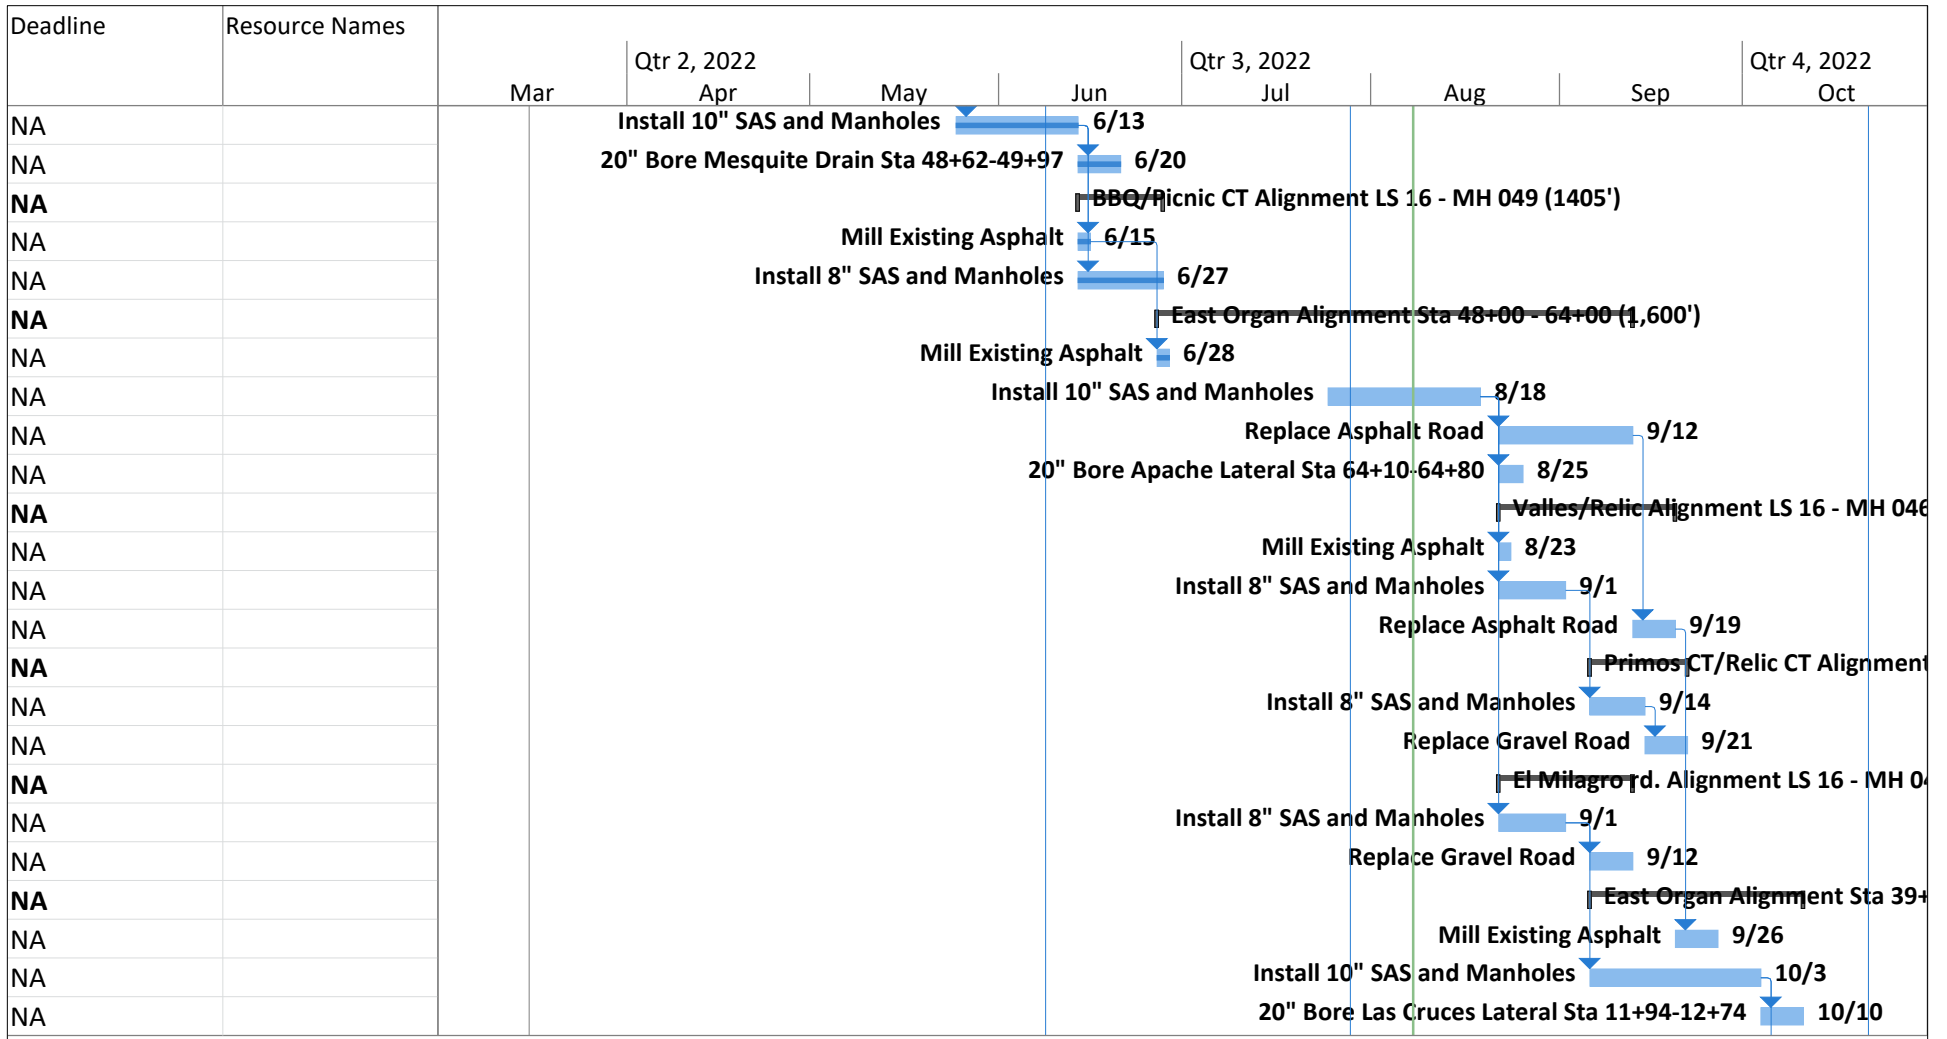


Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

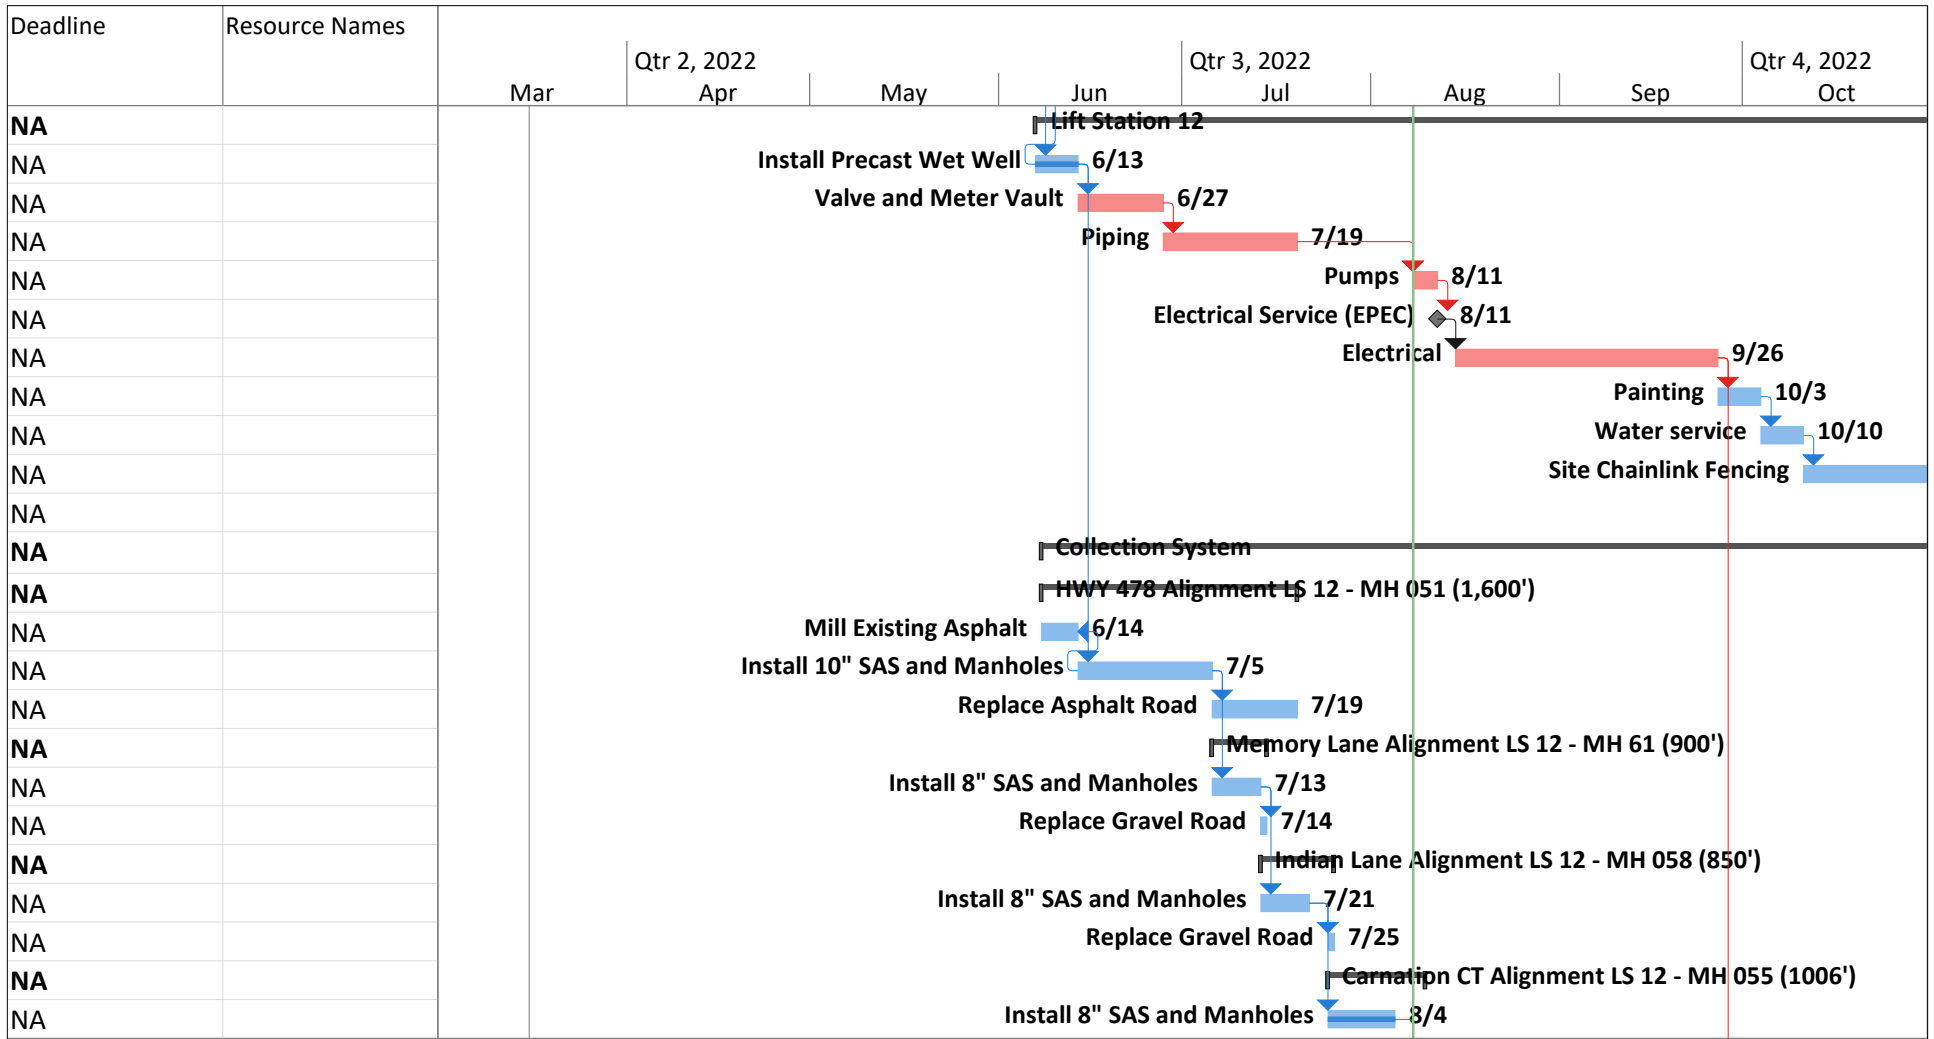

Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

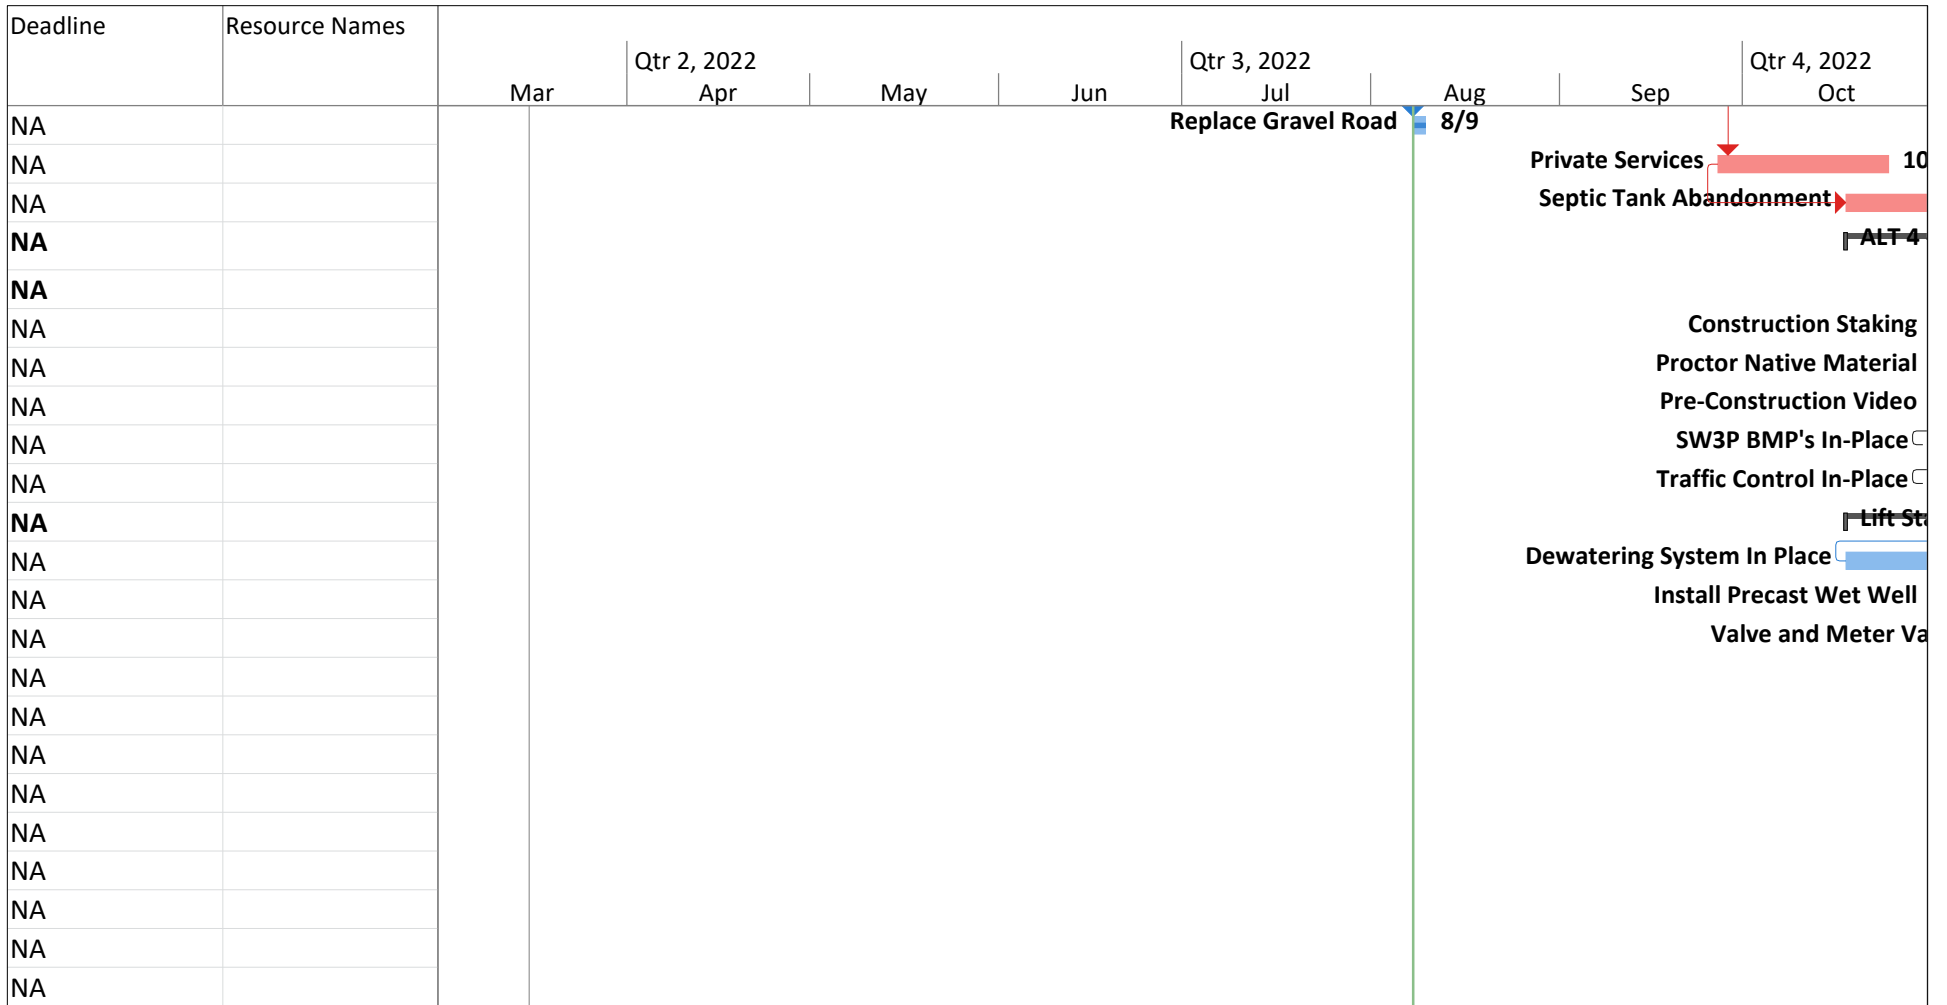


Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	



Project: msproj11
 Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

Qtr 4, 2022 Qtr 1, 2023 Qtr 2, 2023 Qtr 3, 2023
 Oct Nov Dec Jan Feb Mar Apr May Jun Jul



Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

Qtr 4, 2022
Oct

Nov

Dec

Qtr 1, 2023
Jan

Feb

Mar

Qtr 2, 2023
Apr

May

Jun

Qtr 3, 2023
Jul

9
21






















East Organ Alignment Sta 39+67 - 13+00 (2,700')


9/26

10/3

10/10


Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	

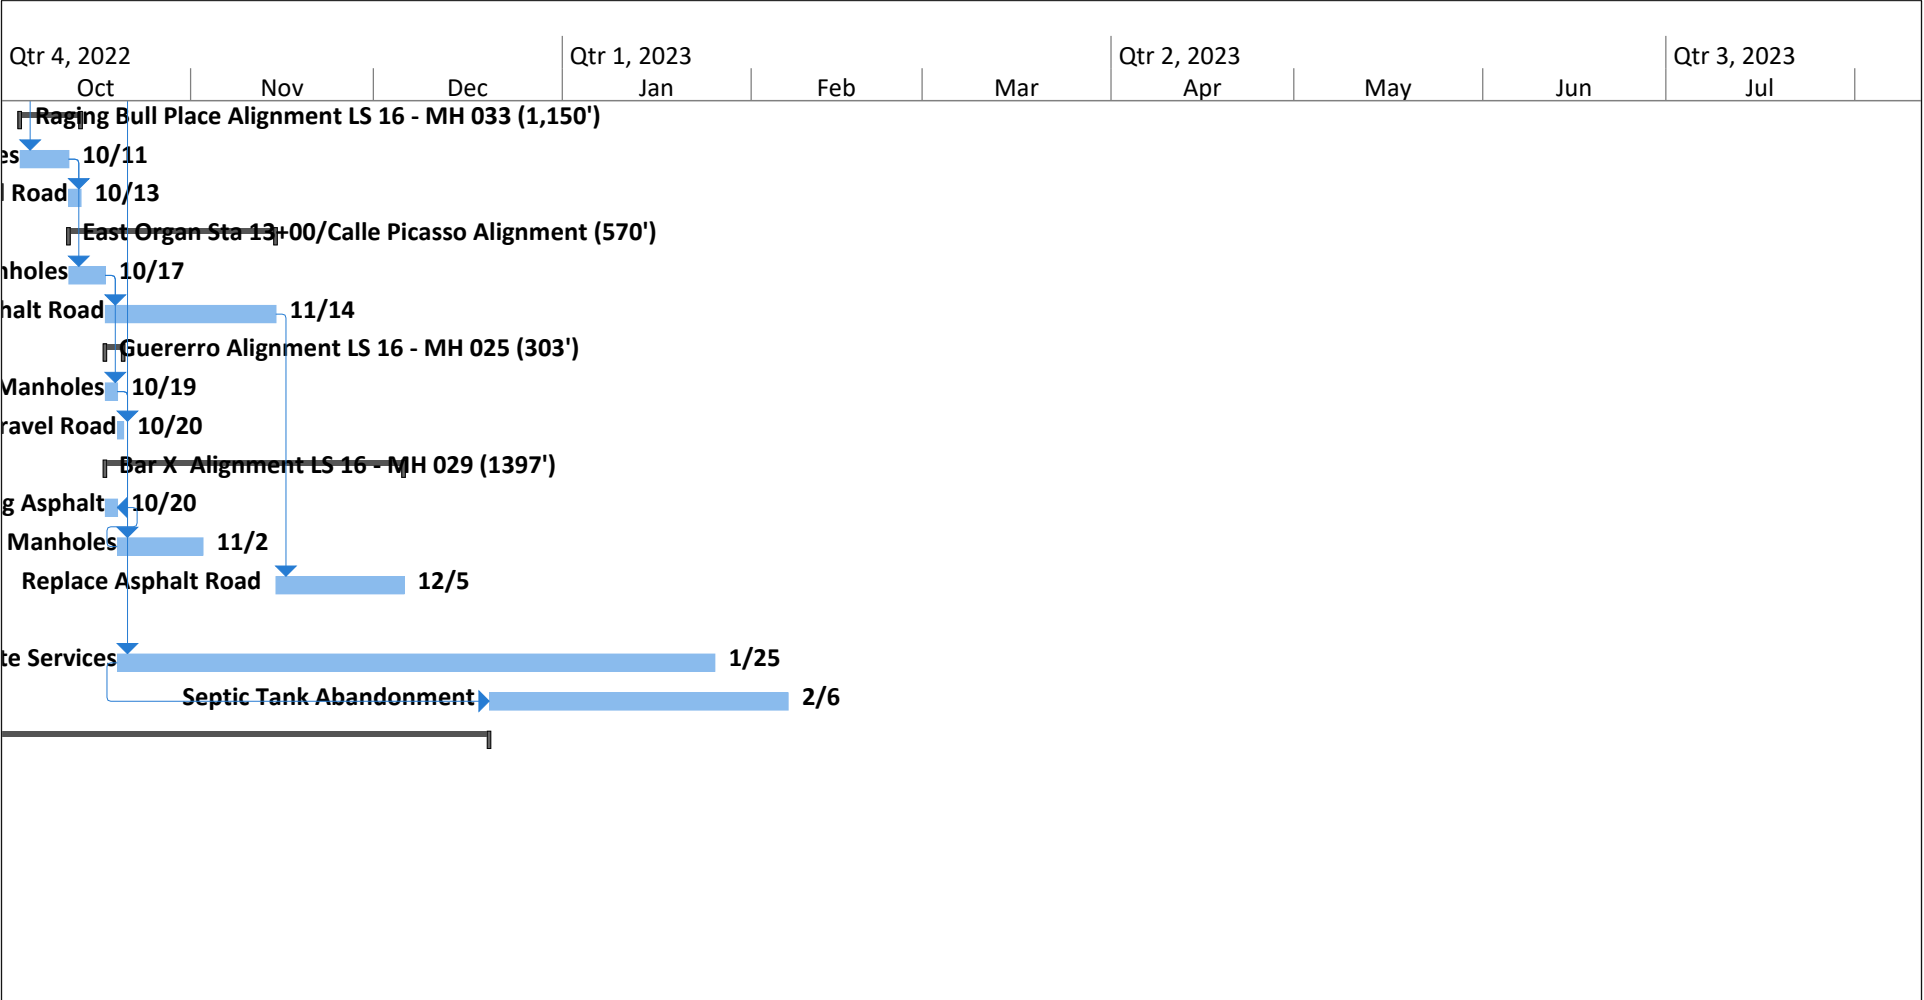


Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

Qtr 4, 2022 Qtr 1, 2023 Qtr 2, 2023 Qtr 3, 2023
 Oct Nov Dec Jan Feb Mar Apr May Jun Jul




Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

Qtr 4, 2022 Qtr 1, 2023 Qtr 2, 2023 Qtr 3, 2023
 Oct Nov Dec Jan Feb Mar Apr May Jun Jul

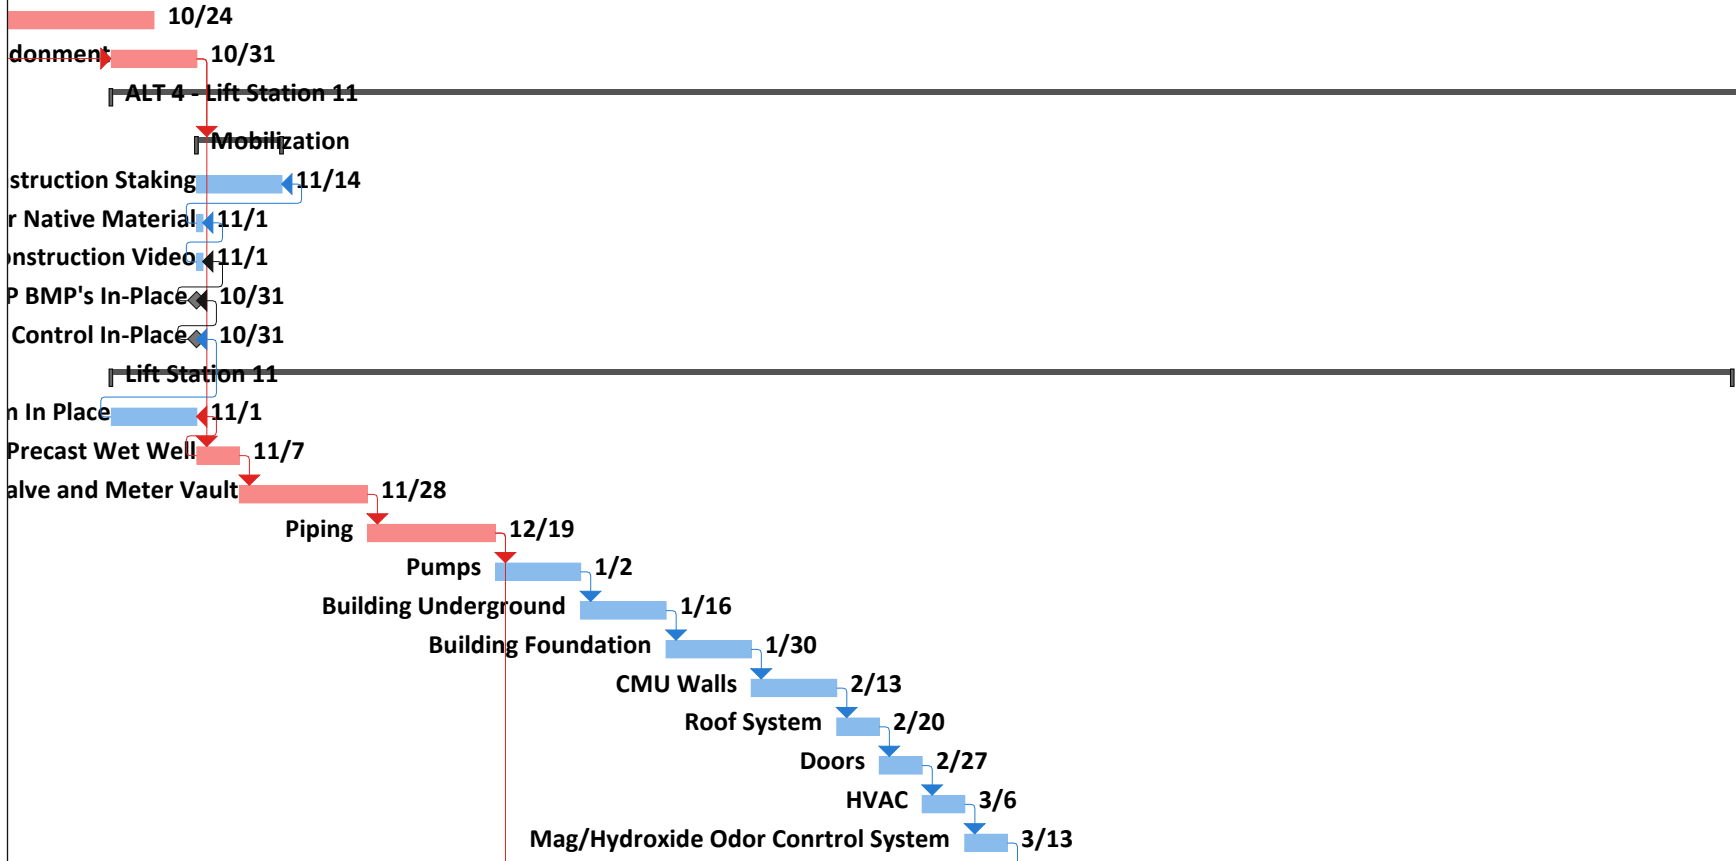


Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

Qtr 4, 2022 Oct Nov Dec Qtr 1, 2023 Jan Feb Mar Qtr 2, 2023 Apr May Jun Qtr 3, 2023 Jul

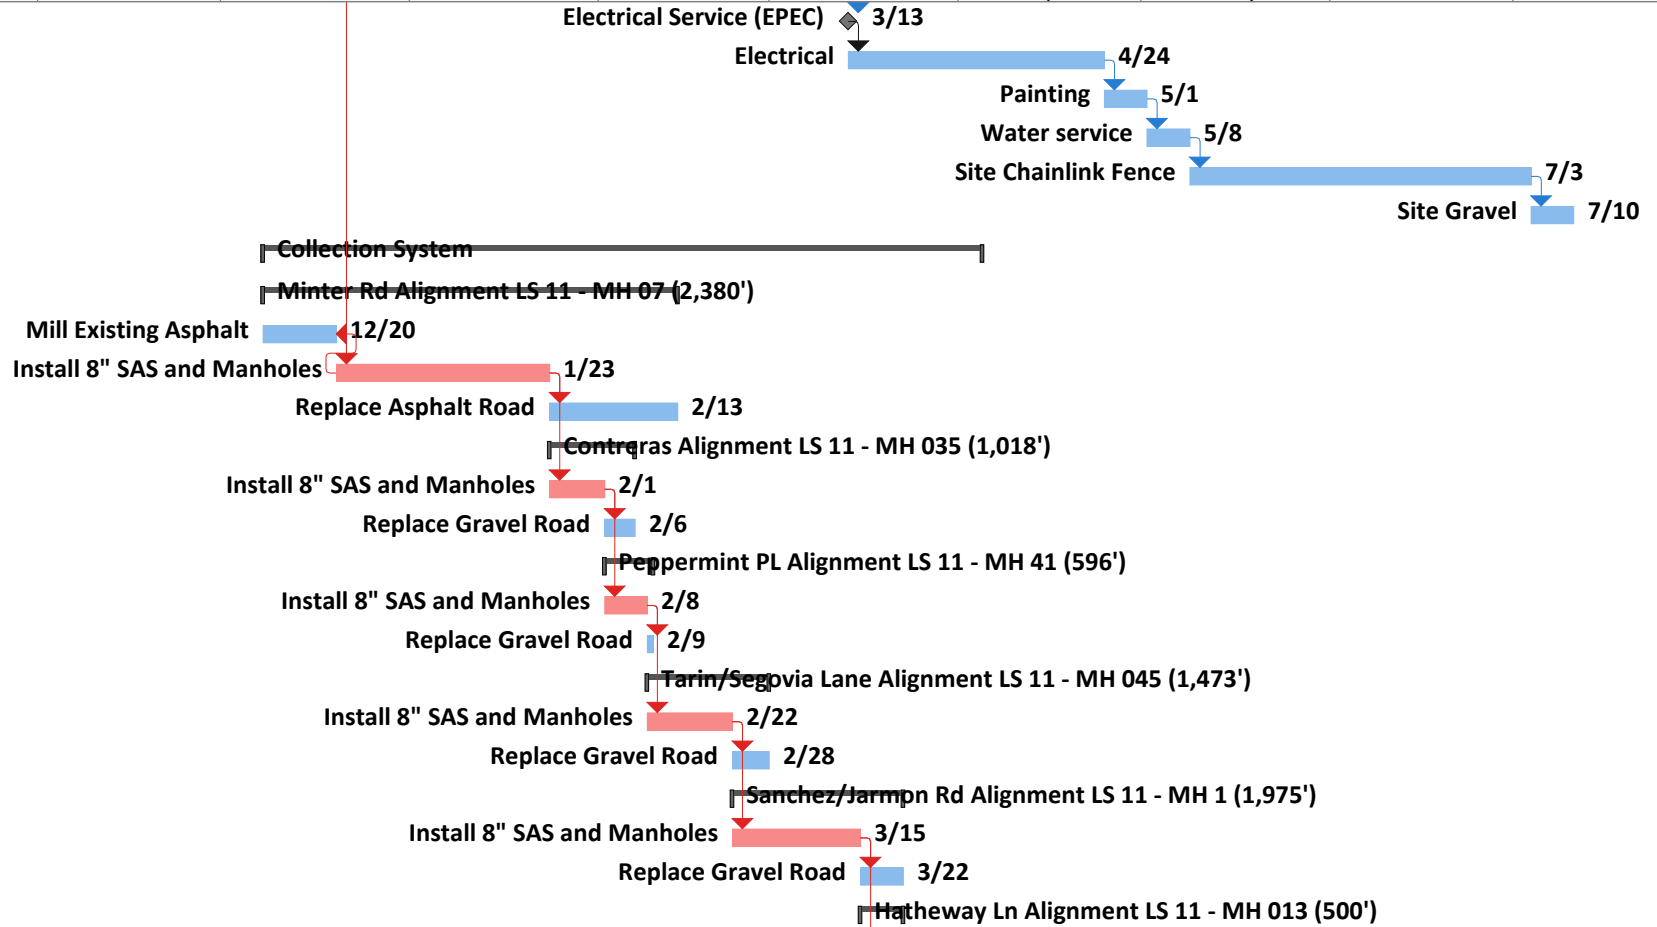


Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

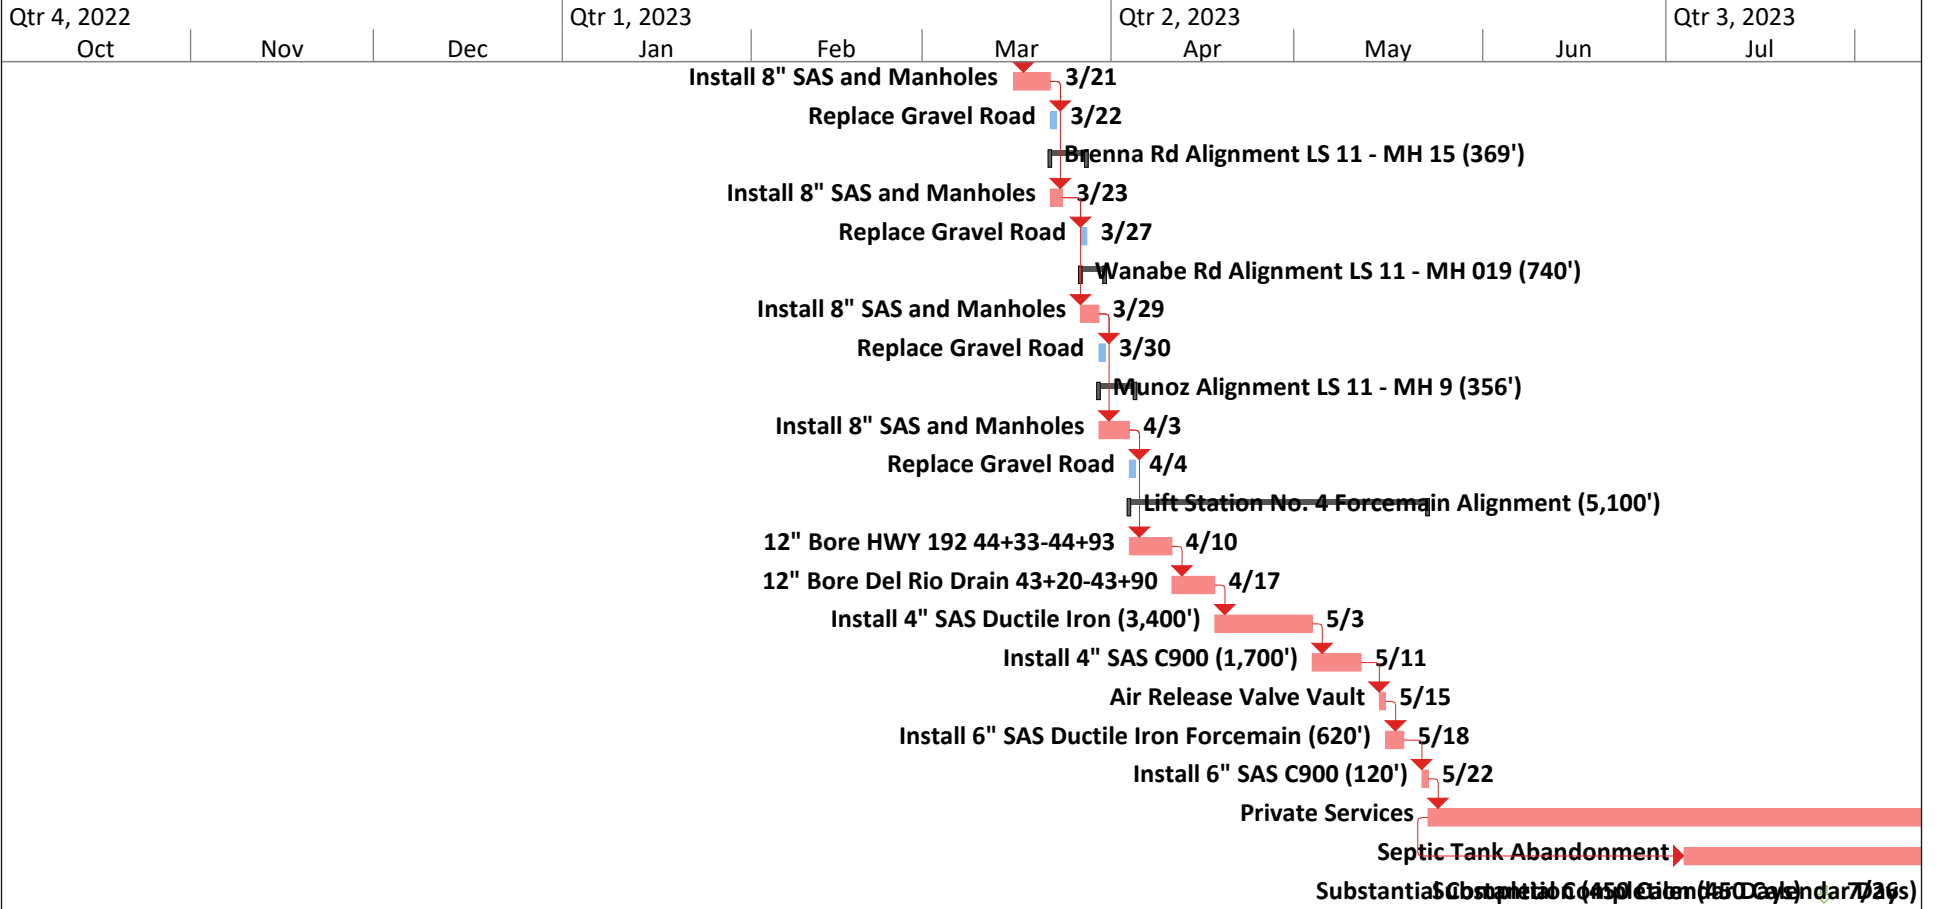


Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	




Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	




Project: msproj11
Date: Mon 8/8/22


Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	



Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	




Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	



Project: msproj11
Date: Mon 8/8/22






















Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	



Project: msproj11 Date: Mon 8/8/22	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary		Manual Progress	

Aug | Sep | Qtr 4, 2023 | Oct | Nov | Dec | Qtr 1, 2024 | Jan | Feb | Mar | Qtr 2, 2024 | Apr | May

Project: msproj11
Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	



8/14
 8/14
 8/14

Project: msproj11
 Date: Mon 8/8/22

Task		Inactive Task		Start-only	
Split		Inactive Milestone		Finish-only	
Milestone		Inactive Summary		Deadline	
Summary		Manual Task		Critical	
Project Summary		Duration-only		Critical Split	
External Tasks		Manual Summary Rollup		Progress	
External Milestone		Manual Summary		Manual Progress	
